



barrell
TREE CONSULTANCY

Permission is granted to scale from this drawing for Local Authority Planning Approval purposes relating to tree protection measures only. Where applicable this drawing is to be read in conjunction with the arboricultural report. This drawing is the copyright of Barrell Tree Consultancy 2020. ©

This drawing to be reproduced in colour only.

www.barrelltreecare.co.uk



BS category A



BS category C



Proposed layout



Estimated tree positions not included on original land survey and/or adjusted crown spreads



Protective barrier/fencing



Construction exclusion zone (CEZ)



Precautionary Areas




Construction exclusion zone protected by ground protection



Root protection area (RPA) boundary for category A tree



Root protection area (RPA) boundaries for category C trees

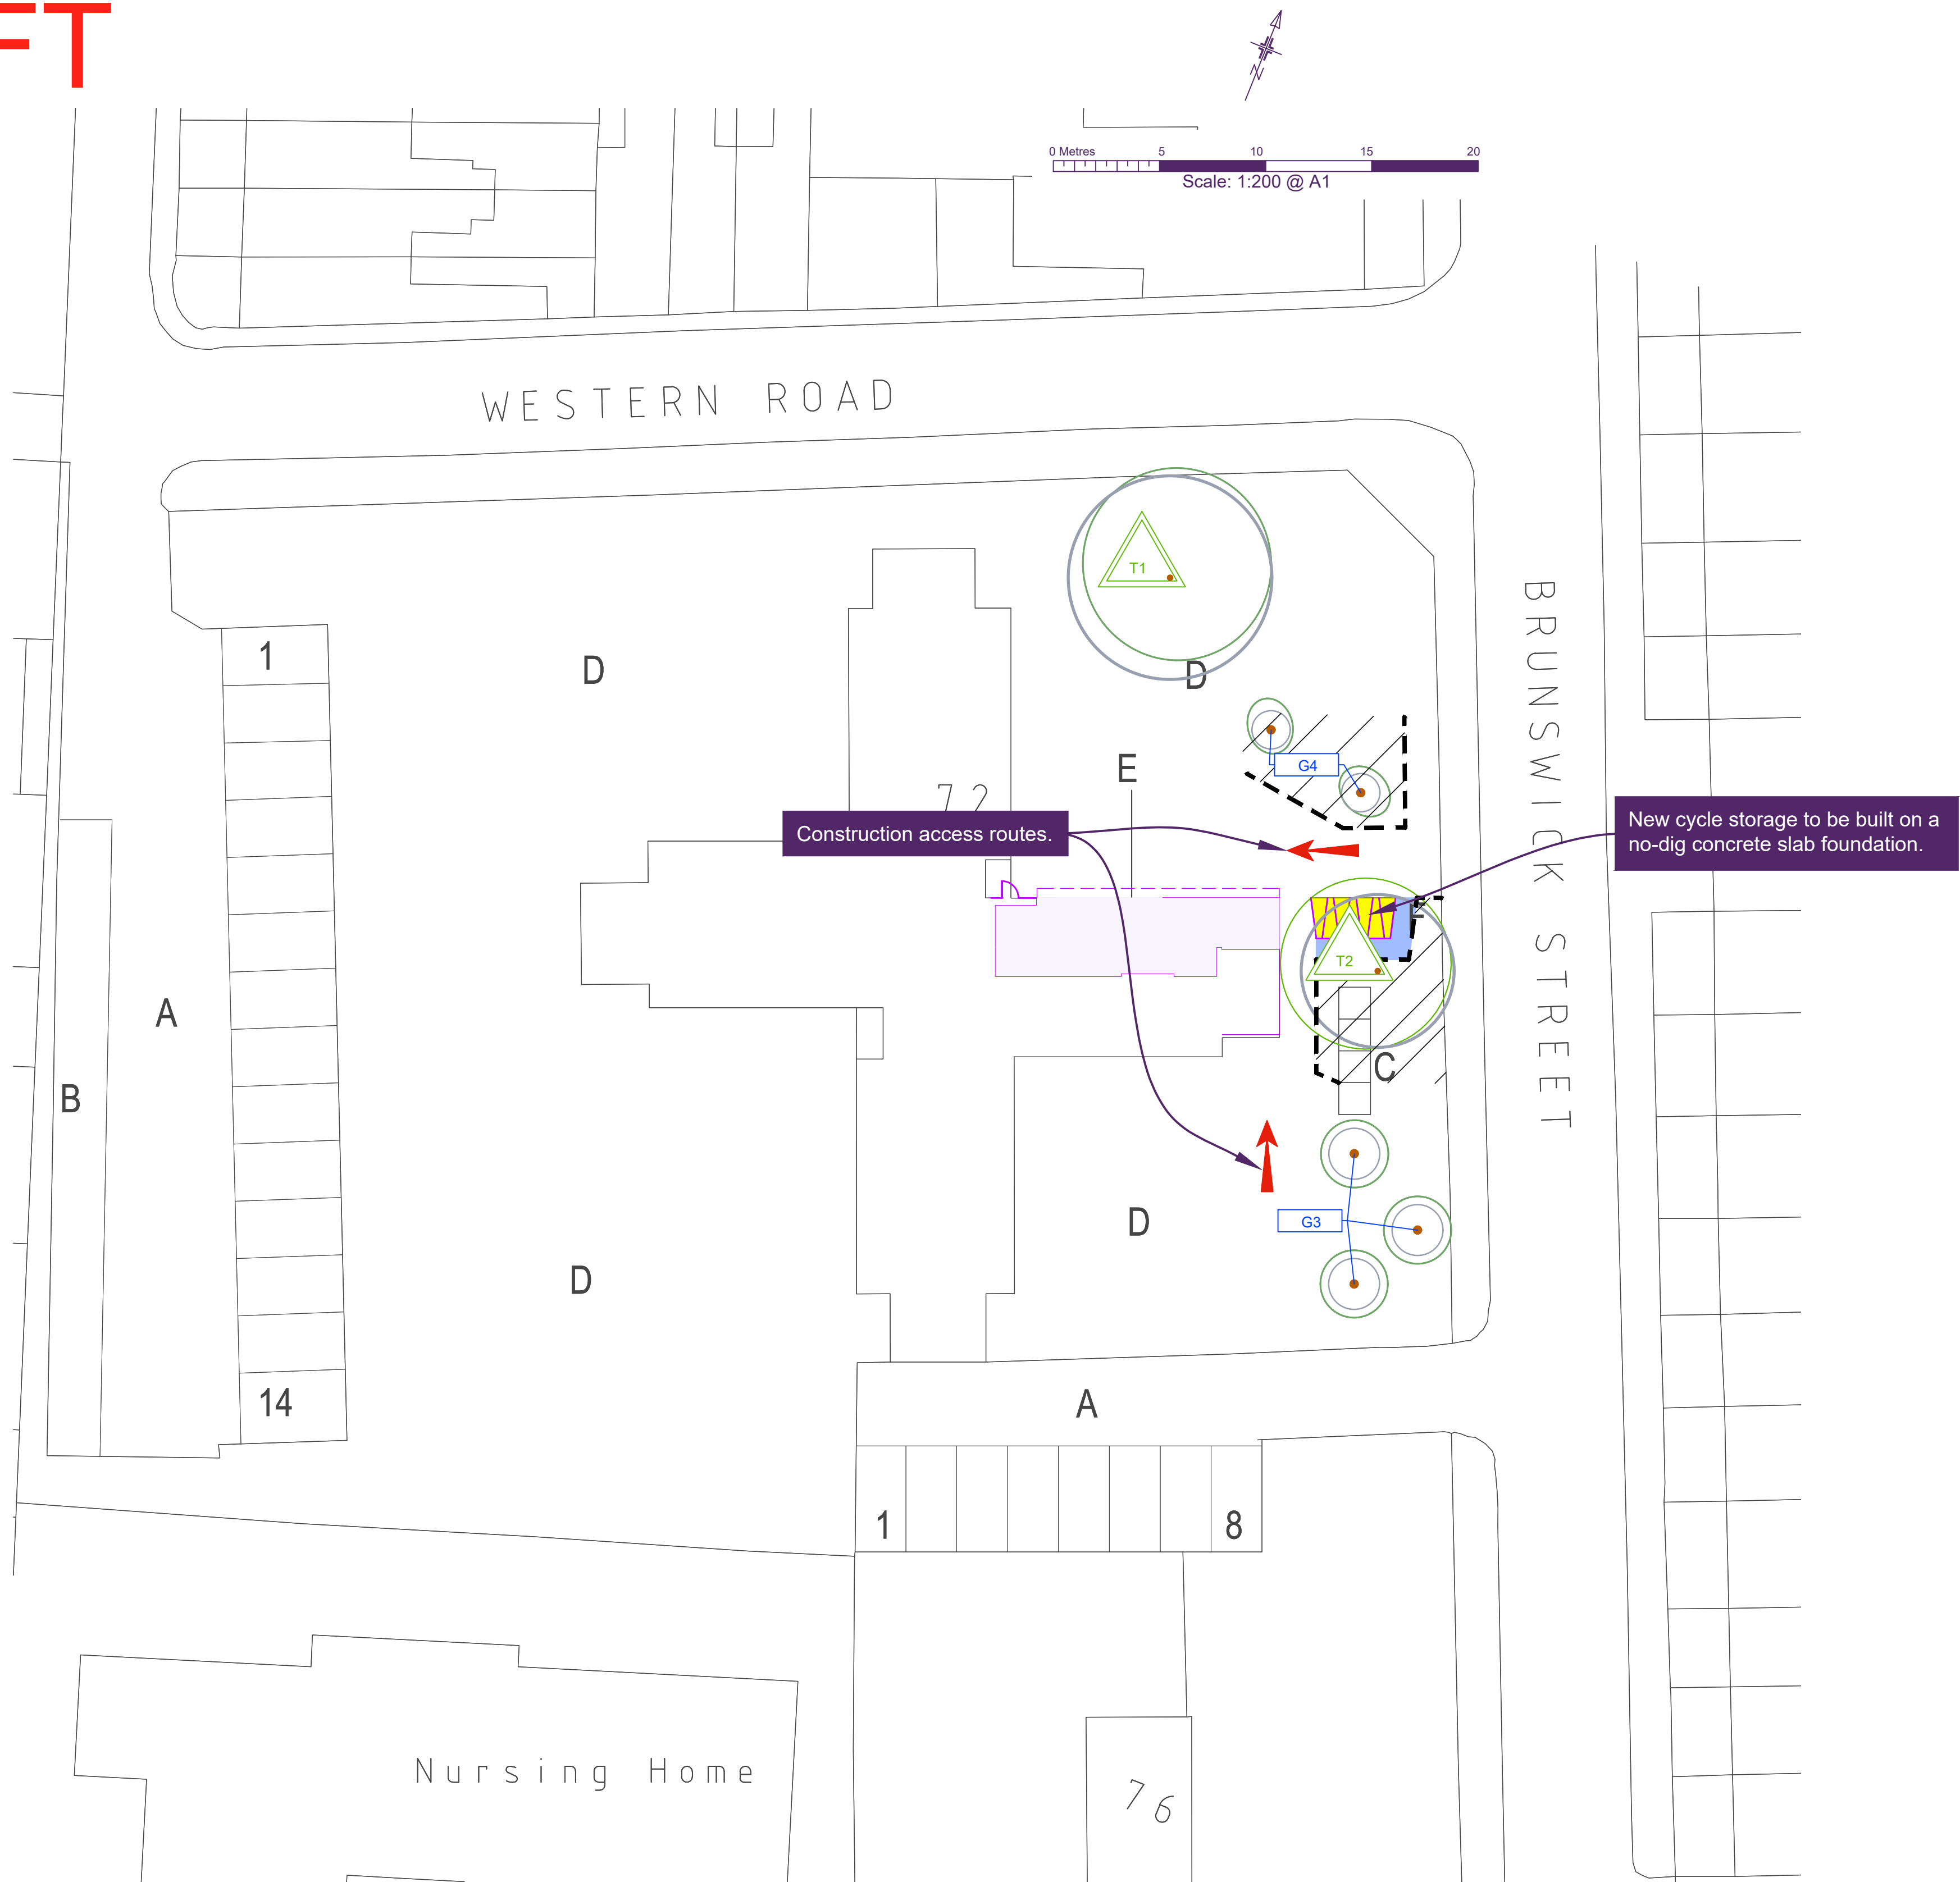

Tree schedule				
Tree No	Species	Category	RPA Radius	Tree Works
All retained trees				Carry out safety check and lift over site to 3-4m as necessary.
T1	Walnut	A	4.8	-
T2	Walnut	A	3.6	-
G3	Cherry	C	1.2	-
G4	Rowan	C	0.9	-



SGN 1 *Monitoring tree protection*

Always:

- ✓ have a pre-commencement meeting with the tree consultant before development starts
- ✓ use the tree consultant to regularly check that protection remains fit for purpose
- ✓ use the tree consultant to supervise work in RPAs
- ✓ keep a written record of supervision





SGN 3 *Ground protection*

Always:

- ✓ install protection before development starts
- ✓ make sure protection is fit for purpose, i.e. it prevents damage to trees and soil
- ✓ keep protection in place until there is no risk to trees
- ✓ get written permission to move or remove any protection





SGN 10 *Installing structures in RPAs*

Always:

- ✓ use the tree consultant to supervise work in RPAs
- ✓ hand-dig pile, pad, or post locations down to at least 60cm
- ✓ protect RPAs from contamination from poured wet concrete





SGN 12 *Landscaping in RPAs*

Always:

- ✓ use the tree consultant to supervise work in RPAs
- ✓ avoid raising ground levels within 1m of the trunks of retained trees





SGN 2 *Fencing protected trees*

Always:

- ✓ install protection before development starts
- ✓ make sure protection is fit for purpose, i.e. it prevents damage to trees and soil
- ✓ keep protection in place until there is no risk to trees
- ✓ get written permission to move or remove any protection





SGN 4 *Pollution control*

Always:

- ✓ keep toxic products away from RPAs





SGN 11 *Installing services in RPAs*

Always:

- ✓ use the tree consultant to supervise work in RPAs
- ✓ select the least damaging option when installing services, so prioritise trenchless, over broken trench over continuous trench
- ✓ hand-dig trenches if trenchless is not feasible



How to use plan

More detailed guidance on each Site Guidance Note (SGN) can be found in a printed hard copy compilation of all the SGNs, issued to the Site Manager at the pre-commencement site meeting (**Note:** This should be retained on site throughout the duration of works). Additionally, an electronic pdf compilation of all the SGNs, was submitted with this drawing to the local planning authority and the client. Alternatively, a pdf of each SGN can be downloaded by:

1. clicking the image links in the electronic pdf version of this plan;
2. holding a mobile phone QR (Quick Response) code reader over the QR code in the paper version of this plan; or,
3. visiting our website at <https://www.barrelltreecare.co.uk/resources/technical-guidance>
