



Arboricultural Consultancy
Holmwood Farm Grange Horsham Road North Holmwood Dorking Surrey RH5 4JR
Tel: 01306 743374 Email: info@challiceconsulting.co.uk Web: www.challiceconsulting.co.uk

Our Ref: CC/1574 AR3238

4th July 2017

Mr. Benjamin Allen
Bailey Partnership
Corum One
Corum Office Park
Crown Way
Warmley
Bristol
BS30 8FJ

Dear Mr. Allen,

Re: Revised Tree Protection Relating to The Acacias, London Road, University of Reading

Please find enclosed an arboricultural report relating to the proposed development at the above site. I would be grateful if you could review the contents of this report to ensure it meets your requirements before it is sent to the Local Planning Authority. A copy of this report should be maintained on site at all times and be available to all site personnel.

Attendance at the pre-commencement meeting and for inspections/supervision (sections 16.0 and 27.0 of report) is chargeable at the standard hourly rate, details of which are available upon request.

I hope that this information is clear and helpful and if I can be of any further assistance, please do not hesitate to contact me.

Yours sincerely,

Mr. David Challice
Chartered Arboriculturist

Enc.

Challice Consulting Ltd.
VAT Registration No. 886 2277 82
Registered Office: Griffins Court 24-32 London Road Newbury Berkshire RG14 1JX
Registered in England and Wales No. 6080792

**Revised Tree Survey
Arboricultural Impact Assessment
Arboricultural Method Statement**

Relating to:

**The Acacias, London Road,
University of Reading**

Produced for:
Bailey Partnership

Prepared by:
Challice Consulting Ltd.
Mr. David Challice
Dip. Arb. (RFS), F.Arbor.A, MICFor
Chartered Arboriculturist

Date:
4th July 2017

Our Ref:
CC/1574 AR3238

INTRODUCTION**SECTION**

Frequently Used Key Terms and Abbreviations	1.0
The Proposal	2.0
Instructions and Purpose	3.0
Scope	4.0
Documents Supplied/Used	5.0
Site Details	6.0

TREE SURVEY

Survey Method	7.0
Tree Details	8.0

ARBORICULTURAL IMPACT ASSESSMENT

Introduction to Arboricultural Impact Assessment	9.0
Tree Removal and Retention	10.0
Tree Pruning Works	11.0
Incursions into Root Protection Areas	12.0
Proximity Issues and Shading	13.0
Summary of Arboricultural Impact	14.0

ARBORICULTURAL METHOD STATEMENT

Introduction to Arboricultural Method Statement	15.0
Pre-Commencement Meeting	16.0
General Site Precautions	17.0
Tree Works	18.0
Tree Protective Fencing	19.0
Ground Protection	20.0
Site Access/Hard Surfaces	21.0
Demolition	22.0
Underground Services	23.0
Foundations	24.0
Construction/Hard Landscaping	25.0
Soft Landscaping/Boundary Fencing	26.0
Sequencing and Supervision	27.0
Amendments	28.0
List of Contacts	29.0

Challice Consulting Ltd.

Holmwood Farm Grange Horsham Road North Holmwood Dorking Surrey RH5 4JR
Tel: 01306 743374 Email: info@challiceconsulting.co.uk Web: www.challiceconsulting.co.uk

APPENDICES

Appendix 1	Tree Survey Schedule with Recommended Tree Works
Appendix 2	Tree Protection Plan in Colour at A1 and Scale 1:200 with Tree Protective Fencing and Ground Protection Specifications
Appendix 3	Example of Site Inspection Record
Appendix 4	Induction Form for Personnel

INTRODUCTION

1.0 Frequently Used Key Terms and Abbreviations

Tree Preservation Order	TPO
Arboricultural Method Statement	AMS
British Standard 5837:2012 – Recommendations for Trees in Relation to Design, Demolition and Construction	BS 5837
British Standard 3998:2010 - Recommendations for Tree Work	BS 3998
Root Protection Area/Root Protection Areas	RPA/RPAs
Local Planning Authority	LPA

2.0 The Proposal

- 2.1 It is proposed to refurbish the existing building without the requirement for additional foundations or outside works that could affect the surveyed trees. Vehicular access will be necessary around the building to facilitate the refurbishment.

3.0 Instructions and Purpose

- 3.1 This report has been commissioned by Bailey Partnership to;
- Survey the trees in accordance with British Standard (BS 5837) 5837:2012 - Trees in Relation to Design, Demolition and Construction- Recommendations.
 - Make suggestions to decrease the arboricultural impact of the proposed scheme on the retained trees during the design process.
 - Detail the arboricultural impact of the proposed project.
 - Prepare a tree work schedule to British Standard (BS 3998) 3998:2010 - Recommendations for Tree Work.
 - Develop a tree protection strategy for the duration of the development including any demolition works.
- 3.2 Provision of the above information is designed to address the requirements of the LPA in terms of the arboricultural information necessary to register and determine the planning application.

4.0 Scope

- 4.1 In surveying the trees to the requirements of BS 5837, trees on and immediately adjacent to the site with a stem diameter over 75mm have been included. Large shrubs and hedges have been included where these are considered to be of significant amenity value. These are particularly important where they provide boundary screening. For clarity and ease of data interpretation, large shrubs have been classified as trees.

Challice Consulting Ltd.

Holmwood Farm Grange Horsham Road North Holmwood Dorking Surrey RH5 4JR
Tel: 01306 743374 Email: info@challiceconsulting.co.uk Web: www.challiceconsulting.co.uk

- 4.2 A full hazard assessment of the trees (including the assessment of decay or defects and their impact), has not been undertaken as this is considered beyond the scope of this report. Any obvious hazards and defects have been identified in the Tree Survey Schedule and appropriate works recommended for immediate action.

5.0 Documents Supplied/Used

Document	Obtained From	Format/Ref.
Existing and proposed layout plans	Bailey Partnership	Dwg.
Topographical Survey	Bailey Partnership	Dwg.

6.0 Site Details

- 6.1 The site is comprised of the grounds surrounding The Acacias, London Road.
- 6.2 The site is within the administrative jurisdiction of Reading Borough Council.
- 6.3 I have not been instructed to ascertain the protection status of any of the trees on or near the site. However, the Client has informed me that all the trees surveyed except T2 are covered by a TPO.

TREE SURVEY

7.0 Survey Method

- 7.1 The site and trees were inspected on 26th January 2017.
- 7.2 The trees were inspected from ground level and no climbing inspections were undertaken.
- 7.3 Stem diameters were measured using a diameter tape at 1.5m from ground level. The locations of the surveyed trees has originated from the

drawings supplied by the client unless otherwise stated in the Tree Survey Schedule.

8.0 Tree Details

8.1 The total number of records is as follows:

Individual Trees (T): 10

Tree Groups (G): 1

8.2 The tree details and proposed works are presented in the Tree Survey Schedule with Recommended Tree Works at **Appendix 1** and tree positions are shown on the Tree Protection Plan at **Appendix 2**.

8.3 The quality and value of the tree stock has been broken down by BS 5837 quality grade. The grading system can be summarised as follows:

A Grade – trees of high quality and value with a life expectancy of more than 40 years

B Grade – trees of moderate quality and value, with a life expectancy of more than 20 years

C Grade – trees of low quality and value, with a life expectancy of more than 10 years

U Grade – trees for removal, with a life expectancy of less than 10 years

Quality and Value of Existing Tree Stock

Total No. Trees (12)	A Grade	B Grade	C Grade	U Grade
No. of Trees	2	8	2	0


8.4 The RPAs of the trees are included in the Tree Survey Schedule with reference to Table 1 of BS 5837. The RPA is the area, measured in m², which is calculated in accordance with the BS 5837 using the stem diameter of the trees. This should provide retained trees with sufficient rooting environment to survive the proposed development. Section 4.6.3 of BS 5837 provides for the shape of the RPA to be modified from the

Challice Consulting Ltd.

Holmwood Farm Grange Horsham Road North Holmwood Dorking Surrey RH5 4JR
Tel: 01306 743374 Email: info@challiceconsulting.co.uk Web: www.challiceconsulting.co.uk

starting point of a circle to account for site features where rooting may be restricted, as long as the total area remains the same.

Diagrammatic Representation of a Restricted Root Protection Area

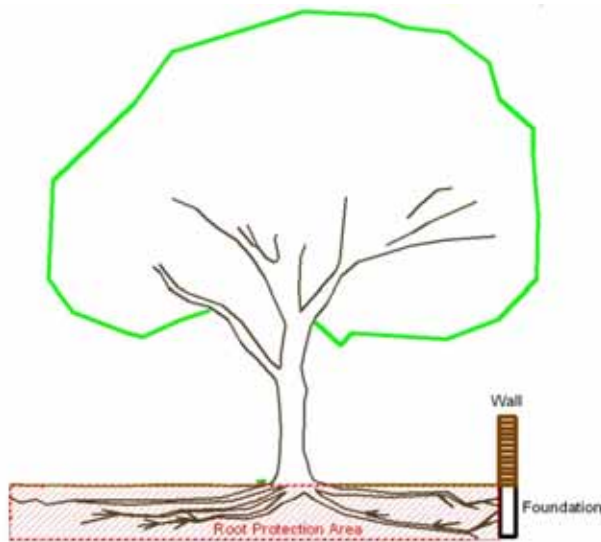

Modified RPAs

Tree No.	Impediments to Normal Rooting
T1, T6 and T8	Existing hard surfacing and buildings

ARBORICULTURAL IMPACT ASSESSMENT

9.0 Introduction to Arboricultural Impact Assessment

- 9.1 This section comprises an assessment of the impact the proposed works detailed in Section 2 above have on trees. It considers the arboricultural impact and how this may be mitigated.

10.0 Tree Removal and Retention

- 10.1 The proposed scheme provides for the retention and protection of all the trees surveyed.

11.0 Tree Pruning Works

- 11.1 Minor tree pruning is recommended to ensure reasonable clearance from the proposed construction. The pruning described in the Tree Survey Schedule with Recommended Tree Works at **Appendix 1** will not adversely affect the trees or their contribution to local amenity.

12.0 Incursions into Root Protection Areas

- 12.1 There are no incursions into the RPAs of retained trees within this scheme.
- 12.2 No new underground services are to be installed within the RPAs of retained trees.

13.0 Proximity Issues and Shading

- 13.1 The shade patterns for the surveyed trees has not been plotted as this is not a constraint to this type of development.
- 13.2 The juxtaposition between retained trees and the proposed development is in accordance with Section 5.3 of the BS 5837 and should not lead to future pressure to heavily prune or remove retained trees for the following reasons:
1. Tree pruning has been recommended to provide adequate separation between the proposed development and the retained trees.
 2. Any future tree pruning works are unlikely to be over and above those generally accepted as good arboricultural practice in an urban environment.
 3. Low maintenance gutters can be specified to negate the need for removing leaves from the rainwater collection system.

14.0 Summary of Arboricultural Impact

- 14.1 In summary, the arboricultural impact of the proposed scheme is minor as no trees are to be removed and minimal pruning is required to enable construction works to be completed.

- 14.2 The retained trees can be afforded an appropriate degree of protection in accordance with the BS 5837 as detailed in the AMS.

ARBORICULTURAL METHOD STATEMENT

15.0 Introduction to Arboricultural Method Statement

- 15.1 To safeguard the retained trees (both above and below ground parts) during the development works and preserve the soil structure of areas which could be allocated for new planting, it will be necessary to implement tree protection measures as outlined below.
- 15.2 The basic principle is that the area inside the tree protective fencing and where ground protection has been used is to be protected for the duration of the works.
- 15.3 A copy of this AMS shall be maintained on site at all times and made available to all site personnel.
- 15.4 All site personnel shall be made aware of the key impact of this AMS and be given an arboricultural induction by the Site Manager. An Induction Form is attached at **Appendix 4**. A copy of the Induction Form will be signed by all site personnel to confirm that they have understood the issues involved.
- 15.5 As of 2005, Local Planning Authorities have powers to serve **Temporary Stop Notices** if agreed tree protection measures are not carried out. Adhering to this AMS will ensure that such costly and time consuming action is avoided.

16.0 Pre-Commencement Meeting

- 16.1 A pre-commencement site meeting, involving representatives from the Development Company, the Arboricultural Consultant and the LPA Tree Officer will be held to ensure that all aspects of the tree protection process are understood and agreed. A record of the meeting will be communicated to all parties by the Arboricultural Consultant.

17.0 General Site Precautions

17.1 The following points will be observed at all times:

- o No fires will be lit on site during the construction or demolition phases.
- o No access will be permitted inside the tree protective fencing.
- o No materials, equipment or debris will be stored within the tree protective fencing.
- o Notice boards, telephone cables or other services will not be attached to any parts of retained trees.
- o Materials which will contaminate the soil (e.g. diesel oil and vehicle washings) will not be permitted to migrate into the RPAs of retained trees.
- o A dedicated mixing and cleaning area will be set up to prevent concrete, cement and cleaning residue leaching into the RPAs of the retained trees (see Tree Protection Plan for specification).

18.0 Tree Works

18.1 All works will be carried out in accordance with BS 3998:2010 'Recommendations for Tree Work' (as amended) and to current arboricultural best practice. Tree works will be carried out by a suitably qualified and experienced Arboricultural Contractor holding the necessary insurance cover. This contractor should carry out the relevant site specific risk assessments and record such information prior to commencement of tasks and work in accordance with current health and safety standards, practices and legislation. A list of such contractors is available from the Arboricultural Association at www.trees.org.uk.

18.2 The subject trees may be protected by virtue of being covered by a TPO. Submission of this AMS in connection with a planning application should be construed as a formal application to carry out those works specified in the Tree Survey Schedule with Recommended Tree Works at **Appendix 1**. It is recommended that this matter be clarified in writing with the LPA prior to any works commencing.

- 18.3 In addition, prior to the commencement of any tree works, an ecological assessment of specific trees may be required to ascertain whether protected species (e.g. bats, badgers and certain invertebrates) may be affected.
- 18.4 If additional pruning of trees is required to facilitate the proposed works or access for machinery/plant, the Arboricultural Consultant will be contacted to advise on appropriate works and liaise with the LPA as necessary.

19.0 Tree Protective Fencing

- 19.1 Tree protective fencing is used to ensure that the RPAs of retained trees are safeguarded. These measures may also be employed to protect areas of ground for new landscaping.
- 19.2 The positioning and specification of the fencing is shown in **Appendix 2**. In this case, the default specification of BS 5837 consisting of **fixed Heras** fencing would be effective.
- 19.3 The protective fencing will remain in position for the duration of the development, including the removal of any existing structures. Clear signs will be attached to the fencing once erected – suggested wording will be **‘Construction Exclusion Zone No Access’**.

20.0 Ground Protection

- 20.1 A provision has been made to install ground protection between the edge of the proposed development and the tree protective fencing. This provides adequate working space to permit the safe and practical completion of construction works whilst protecting the rooting environment of the retained trees (position and specification shown in **Appendix 2**). The ground protection will remain in place for the duration of the development, including the removal of any existing structures.

21.0 Site Access/Hard Surfaces

- 21.1 The existing vehicle access into the site is suitable for ingress during demolition and construction and little or no damage is anticipated to the root systems of the retained trees.

22.0 Demolition

- 22.1 There is no requirement for demolition within the RPAs of retained trees.

23.0 Underground Services

- 23.1 The proposed scheme can make use of existing services and all new services and soakaways will be located in the adequate space outside the RPAs of the retained trees.
- 23.2 The locations, specifications and installation methods of all new services will be available for review at the pre-commencement site meeting before any works start on site.

24.0 Foundations

- 24.1 There is no requirement for any foundations within the RPAs of the surveyed trees.

25.0 Construction/Hard Landscaping

- 25.1 There is no requirement for additional construction or hard landscaping that will affect the retained trees.
- 25.2 Construction is taken to include erection of scaffolding and the installation of associated hard landscaping features such as retaining walls, patios, and cycle stores.
- 25.3 In this instance, retained trees will not impede the erection of scaffolding and no ancillary structures are proposed within the RPAs of the retained trees.

- 25.4 Subject to all of the above tree protection measures being implemented, construction works may proceed without risk of damage to retained trees.

26.0 Soft Landscaping/Boundary Fencing

- 26.1 Soft landscaping will be undertaken when heavy machinery has been removed from site and tree protective fencing taken down. The following points will be observed:

- Care will be taken not to compact the soil within the RPAs of retained trees or where new tree planting is to be carried out.
- No changes in ground levels will occur within the RPAs of the retained trees.
- Unwanted vegetation will be removed manually or using contact herbicides that will not damage existing tree roots.
- No irrigation or drainage pipes will be installed within the RPAs of retained trees.
- If soil has been compacted in areas where planting is proposed, measures to improve soil structure (e.g. decompaction) may be necessary to facilitate successful plant establishment.
- Where fence and gate post holes are to be installed within the RPAs of the retained trees, they shall be lined with heavy duty polythene to prevent the harmful cement leaching into the soil and damaging the roots of the retained trees.

27.0 Sequencing and Supervision

- 27.1 Effective tree protection relies on following a logical sequence of events and arboricultural inspection/supervision.
- 27.2 Works which have the potential to affect trees will be supervised by a suitably qualified and experienced Arboricultural Consultant. Regular inspection visits will also be undertaken to ensure that tree protection measures are being adhered to. The final details of supervision and the frequency of inspection visits will be agreed with the Tree Officer at the pre-commencement meeting. The Arboricultural Consultant will make a record of visits, which will be attached to the site copy of the AMS for

inspection and communicated in writing to the LPA. An example of the Site Inspection Record is found in **Appendix 3**.

Sequencing and Supervision

Stage	Action	Personnel Responsible
1.	Issue arboricultural report to site manager	Client/Developer
2.	Give Arboricultural Consultant (AC) at least a week's notice of pre-commencement meeting	Client/Developer
3.	Pre-commencement meeting	Site Manager, Tree Officer and AC
4.	Arboricultural induction	Site Manager
5.	Carry out tree works	AC to monitor
6.	Erect tree protective fencing and install ground protection	AC to inspect
7.	Remove tree protective fencing/ground protection	Site Manager
8.	Carry out soft landscaping and erect boundary fencing	Site Manager to brief landscaping company on site and supervise

28.0 Amendments

28.1 Issues sometimes arise on development sites which require amendments to the previously agreed tree protection details. Any amendments to this AMS will be discussed with the Arboricultural Consultant and approved in writing by the LPA prior to being implemented. Copies of paperwork relating to any amendments shall be attached to the site copy of the AMS to provide a definitive record of what has been agreed.

29.0 List of Contacts

Contact	Name	Company/LPA	Contact Number(s)	Report Issued to?
Client	Mr. Benjamin Allen	Bailey Partnership	0117 947 4380	Yes
Arboricultural Supervisor	Mr. David Challice	Challice Consulting Ltd.	01306 743374 07831 855764	N/a

Appendix 1

Site: The Acacias, London Road, University of Reading

Surveyor: Mr. David Challice

Date Surveyed: Thu, 26 Jan 2017

Our Ref: CC/1574 AR3238

Tree No.	English Name	Height	Crown Spread	Ground Clearance	Age Class	Stem Diameter	Protection Multiplier	Protection Radius	Growth Vitality	Structural Condition	Landscape Contribution	B.S. Cat	Sub Cat	Useful Life	Observations
T1	Common Yew 1 Number	16	6 6 6	GC0.5 FB 0.5 N	Mature	590 1	12	7.1	Normal	Good	Medium	B	1,2	40+	Stem break at 4m with potentially weak unions Rooting restricted by nearby structures

Recommended Works/

Suggest climbing inspection to inform any remedial works

Reason for Works:

Advisable for good arboricultural practice

T2	Common Holly 1 Number	7	3 3 3	GC 0 FB 0 N	Early Mature	346 12	12	4.2	Normal	Good	Medium	C	1,2	40+	Multiple stems
----	--------------------------	---	-------------	----------------	--------------	-----------	----	-----	--------	------	--------	---	-----	-----	----------------

Recommended Works/

No work proposed

Reason for Works:

T3	Holm Oak 1 Number	17	8 8 8	GC1.5 FB 1.5 S	Mature	1010 1	12	12.1	Normal	Fair	High	B	1,2	40+	Decay fruiting fungi (<i>Ganoderma</i>) on stem northern side at 1.3m from ground level Numerous branch wounds with extensive supporting wound wood Heavily end loaded limbs
----	----------------------	----	-------------	-------------------	--------	-----------	----	------	--------	------	------	---	-----	-----	--

Recommended Works/

Suggest internal decay detection with view to reduction

Reason for Works:

Advisable for good arboricultural practice

T4	Norway Maple 1 Number	4	1 1 1	GC1.5 FB 1.5 N	Young	60 1	12	0.7	Normal	Good	Low	C	1,2	40+	A tree with insignificant defects
----	--------------------------	---	-------------	-------------------	-------	---------	----	-----	--------	------	-----	---	-----	-----	-----------------------------------

Recommended Works/

No work proposed

Reason for Works:

Notes:

- Height describes the approximate height of the tree measured in meters from ground level.
- The Crown Spread refers to the crown radius in meters from the stem centre and is shown above on each of the four compass points (i.e. N, S, E, W).
- Ground Clearance (**GC**) is the height in meters of crown clearance above adjacent ground level, the height of the first significant branch (**FB**) and the direction in which it is growing.
- Stem Diameter is the diameter of the stem measured in millimeters at 1.5m from ground level. The stem diameter may be estimated (**est**) where access is restricted or an average (**ave**) taken for groups or multi-stemmed trees with more than five stems. The number of stems is also indicated.
- Protection Multiplier is the number used to calculate the tree's protection radius and area and is shown as 12.

- Protection Radius is a radial distance measured from the trunk centre.
- Growth Vitality - Normal growth, Moderate (below normal), Poor (sparse/weak) or Dead (dead or dying tree).
- Structural Condition - Good (no or only minor defects), Fair (remedial defects), Poor (major defects present).
- Landscape Contribution - High (prominent landscape feature), Medium (visible in landscape), Low (secluded/among other trees).
- B.S. Cat refers to British Standard 5837:2012 Table 1 and refers to tree/group quality and value; '**A**' - High, '**B**' - Moderate, '**C**' - Low, '**U**' - Remove.
- Sub Cat refers to the retention criteria values where 1 is Arboricultural, 2 is Landscape and 3 is Cultural including Conservational, Historic and Commemorative.
- Useful Life is the tree's estimated remaining contribution in years.

Site: The Acacias, London Road, University of Reading

Surveyor: Mr. David Challice

Date Surveyed: Thu, 26 Jan 2017

Our Ref: CC/1574 AR3238

Tree No.	English Name	Height	Crown Spread	Ground Clearance	Age Class	Stem Diameter	Protection Multiplier	Protection Radius	Growth Vitality	Structural Condition	Landscape Contribution	B.S. Cat	Sub Cat	Useful Life	Observations
T5	Japanese Maple 1 Number	3	3 2 3 3	GC0.5 FB 0.5 S	Early Mature	200 1 est	12	2.4	Normal	Good	Medium	B	1,2	40+	A tree with insignificant defects

Recommended Works/ No work proposed

Reason for Works:

T6	Common Beech 1 Number	18	7 7 7 7	GC1.5 FB 3 W	Mature	770 1	12	9.2	Moderate	Good	High	B	1,2	40+	Damaged surface rooting Rooting restricted by nearby structures
----	--------------------------	----	---------------	-----------------	--------	----------	----	-----	----------	------	------	---	-----	-----	--

Recommended Works/ Cut back to give 2m clearance from building
Crown lift to 4m above ground protection
Reason for Works: Advisable for good arboricultural practice
Recommended to permit development

T7	Tulip Tree 1 Number	19	8 9 8 10	GC 2 FB 3 S	Mature	810 1	12	9.7	Moderate	Good	High	B	1,2	40+	Significant deadwood throughout crown
----	------------------------	----	----------------	----------------	--------	----------	----	-----	----------	------	------	---	-----	-----	---------------------------------------

Recommended Works/ Remove all deadwood over 25mm in diameter
Suggest inspecting weeping wounds on upper sides of limbs during removal of deadwood
Crown lift to 4m above ground protection
Reason for Works: Advisable for good arboricultural practice
Advisable for good arboricultural practice
Recommended to permit development

T8	London Plane 1 Number	27	15 16 18 12	GC1.5 FB 10 S	Mature	2140 1	12	15.0	Normal	Good	High	A	1,2	40+	Very impressive specimen with rooting anticipated under surrounding buildings to the north
----	--------------------------	----	-------------------	------------------	--------	-----------	----	------	--------	------	------	---	-----	-----	--

Recommended Works/ No work proposed

Reason for Works:

Notes:

- Height describes the approximate height of the tree measured in meters from ground level.
- The Crown Spread refers to the crown radius in meters from the stem centre and is shown above on each of the four compass points (i.e. N, S, E, W).
- Ground Clearance (**GC**) is the height in meters of crown clearance above adjacent ground level, the height of the first significant branch (**FB**) and the direction in which it is growing.
- Stem Diameter is the diameter of the stem measured in millimeters at 1.5m from ground level. The stem diameter may be estimated (**est**) where access is restricted or an average (**ave**) taken for groups or multi-stemmed trees with more than five stems. The number of stems is also indicated.
- Protection Multiplier is the number used to calculate the tree's protection radius and area and is shown as 12.

- Protection Radius is a radial distance measured from the trunk centre.
- Growth Vitality - Normal growth, Moderate (below normal), Poor (sparse/weak) or Dead (dead or dying tree).
- Structural Condition - Good (no or only minor defects), Fair (remedial defects), Poor (major defects present).
- Landscape Contribution - High (prominent landscape feature), Medium (visible in landscape), Low (secluded/among other trees).
- B.S. Cat refers to British Standard 5837:2012 Table 1 and refers to tree/group quality and value; '**A**' - High, '**B**' - Moderate, '**C**' - Low, '**U**' - Remove.
- Sub Cat refers to the retention criteria values where 1 is Arboricultural, 2 is Landscape and 3 is Cultural including Conservation, Historic and Commemorative.
- Useful Life is the tree's estimated remaining contribution in years.

Site: The Acacias, London Road, University of Reading

Surveyor: Mr. David Challice

Date Surveyed: Thu, 26 Jan 2017

Our Ref: CC/1574 AR3238

Tree No.	English Name	Height	Crown Spread	Ground Clearance	Age Class	Stem Diameter	Protection Multiplier	Protection Radius	Growth Vitality	Structural Condition	Landscape Contribution	B.S. Cat	Sub Cat	Useful Life	Observations
G9	Holly 2 Number	7	4 4 4 4	GC 0 FB 0 N	Mature	400 1 ave	12	4.8	Normal	Good	Medium	B	1,2	40+	Trees with insignificant defects

Recommended Works/ No work proposed

Reason for Works:

T10	Common Yew 1 Number	13	7 7 6 6	GC 0 FB 2 S	Mature	780 1	12	9.4	Normal	Good	High	A	1,2	40+	Branches are touching adjacent building
------------	------------------------	----	---------------	----------------	--------	----------	----	-----	--------	------	------	---	-----	-----	---

Recommended Works/ Cut back to give 2m clearance from adjacent building

Reason for Works:

Advisable for good arboricultural practice

T11	Japanese Maple 1 Number	7	3 3 2 2	GC1.5 FB 0 S	Early Mature	133 3	12	1.6	Normal	Good	Medium	B	1,2	40+	A tree with insignificant defects
------------	----------------------------	---	---------------	-----------------	--------------	----------	----	-----	--------	------	--------	---	-----	-----	-----------------------------------

Recommended Works/ No work proposed

Reason for Works:


Notes:

- Height describes the approximate height of the tree measured in meters from ground level.
- The Crown Spread refers to the crown radius in meters from the stem centre and is shown above on each of the four compass points (i.e. N, S, E, W).
- Ground Clearance (**GC**) is the height in meters of crown clearance above adjacent ground level, the height of the first significant branch (**FB**) and the direction in which it is growing.
- Stem Diameter is the diameter of the stem measured in millimeters at 1.5m from ground level. The stem diameter may be estimated (**est**) where access is restricted or an average (**ave**) taken for groups or multi-stemmed trees with more than five stems. The number of stems is also indicated.
- Protection Multiplier is the number used to calculate the tree's protection radius and area and is shown as 12.


- Protection Radius is a radial distance measured from the trunk centre.
- Growth Vitality - Normal growth, Moderate (below normal), Poor (sparse/weak) or Dead (dead or dying tree).
- Structural Condition - Good (no or only minor defects), Fair (remedial defects), Poor (major defects present).
- Landscape Contribution - High (prominent landscape feature), Medium (visible in landscape), Low (secluded/among other trees).
- B.S. Cat refers to British Standard 5837:2012 Table 1 and refers to tree/group quality and value; '**A**' - High, '**B**' - Moderate, '**C**' - Low, '**U**' - Remove.
- Sub Cat refers to the retention criteria values where 1 is Arboricultural, 2 is Landscape and 3 is Cultural including Conservational, Historic and Commemorative.
- Useful Life is the tree's estimated remaining contribution in years.

Appendix 2


CONSTRUCTION
EXCLUSIONS
NO ACCESS

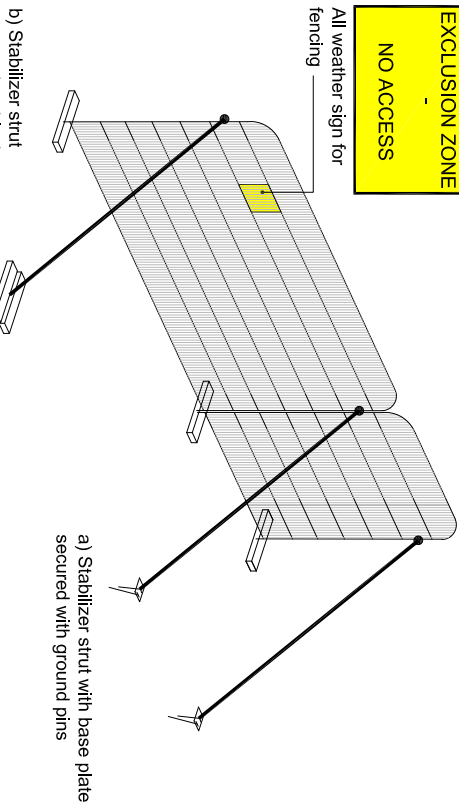

Dedicated mixing and cleaning area

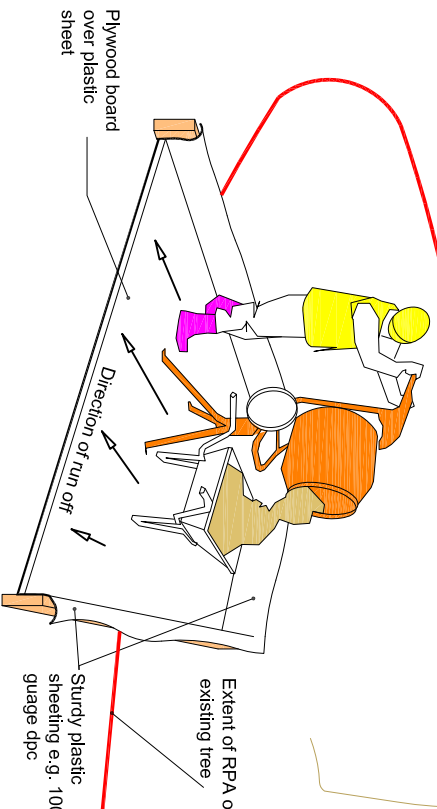


Ground Protection Detail

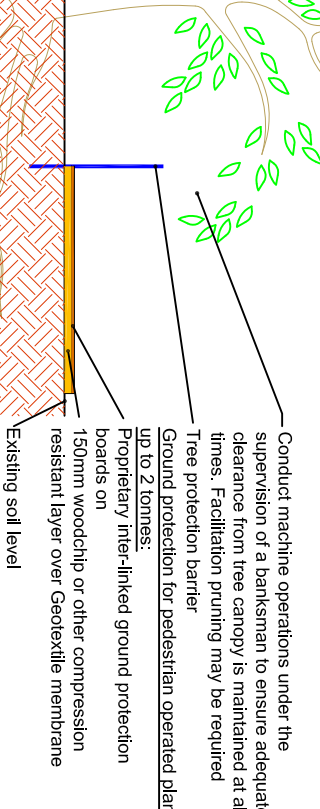

For wheeled or tracked construction traffic, greater than 200mm, proprietary trackways, boards may be used in place of proprietary inter-linked ground protection boards.

LONDON ROAD

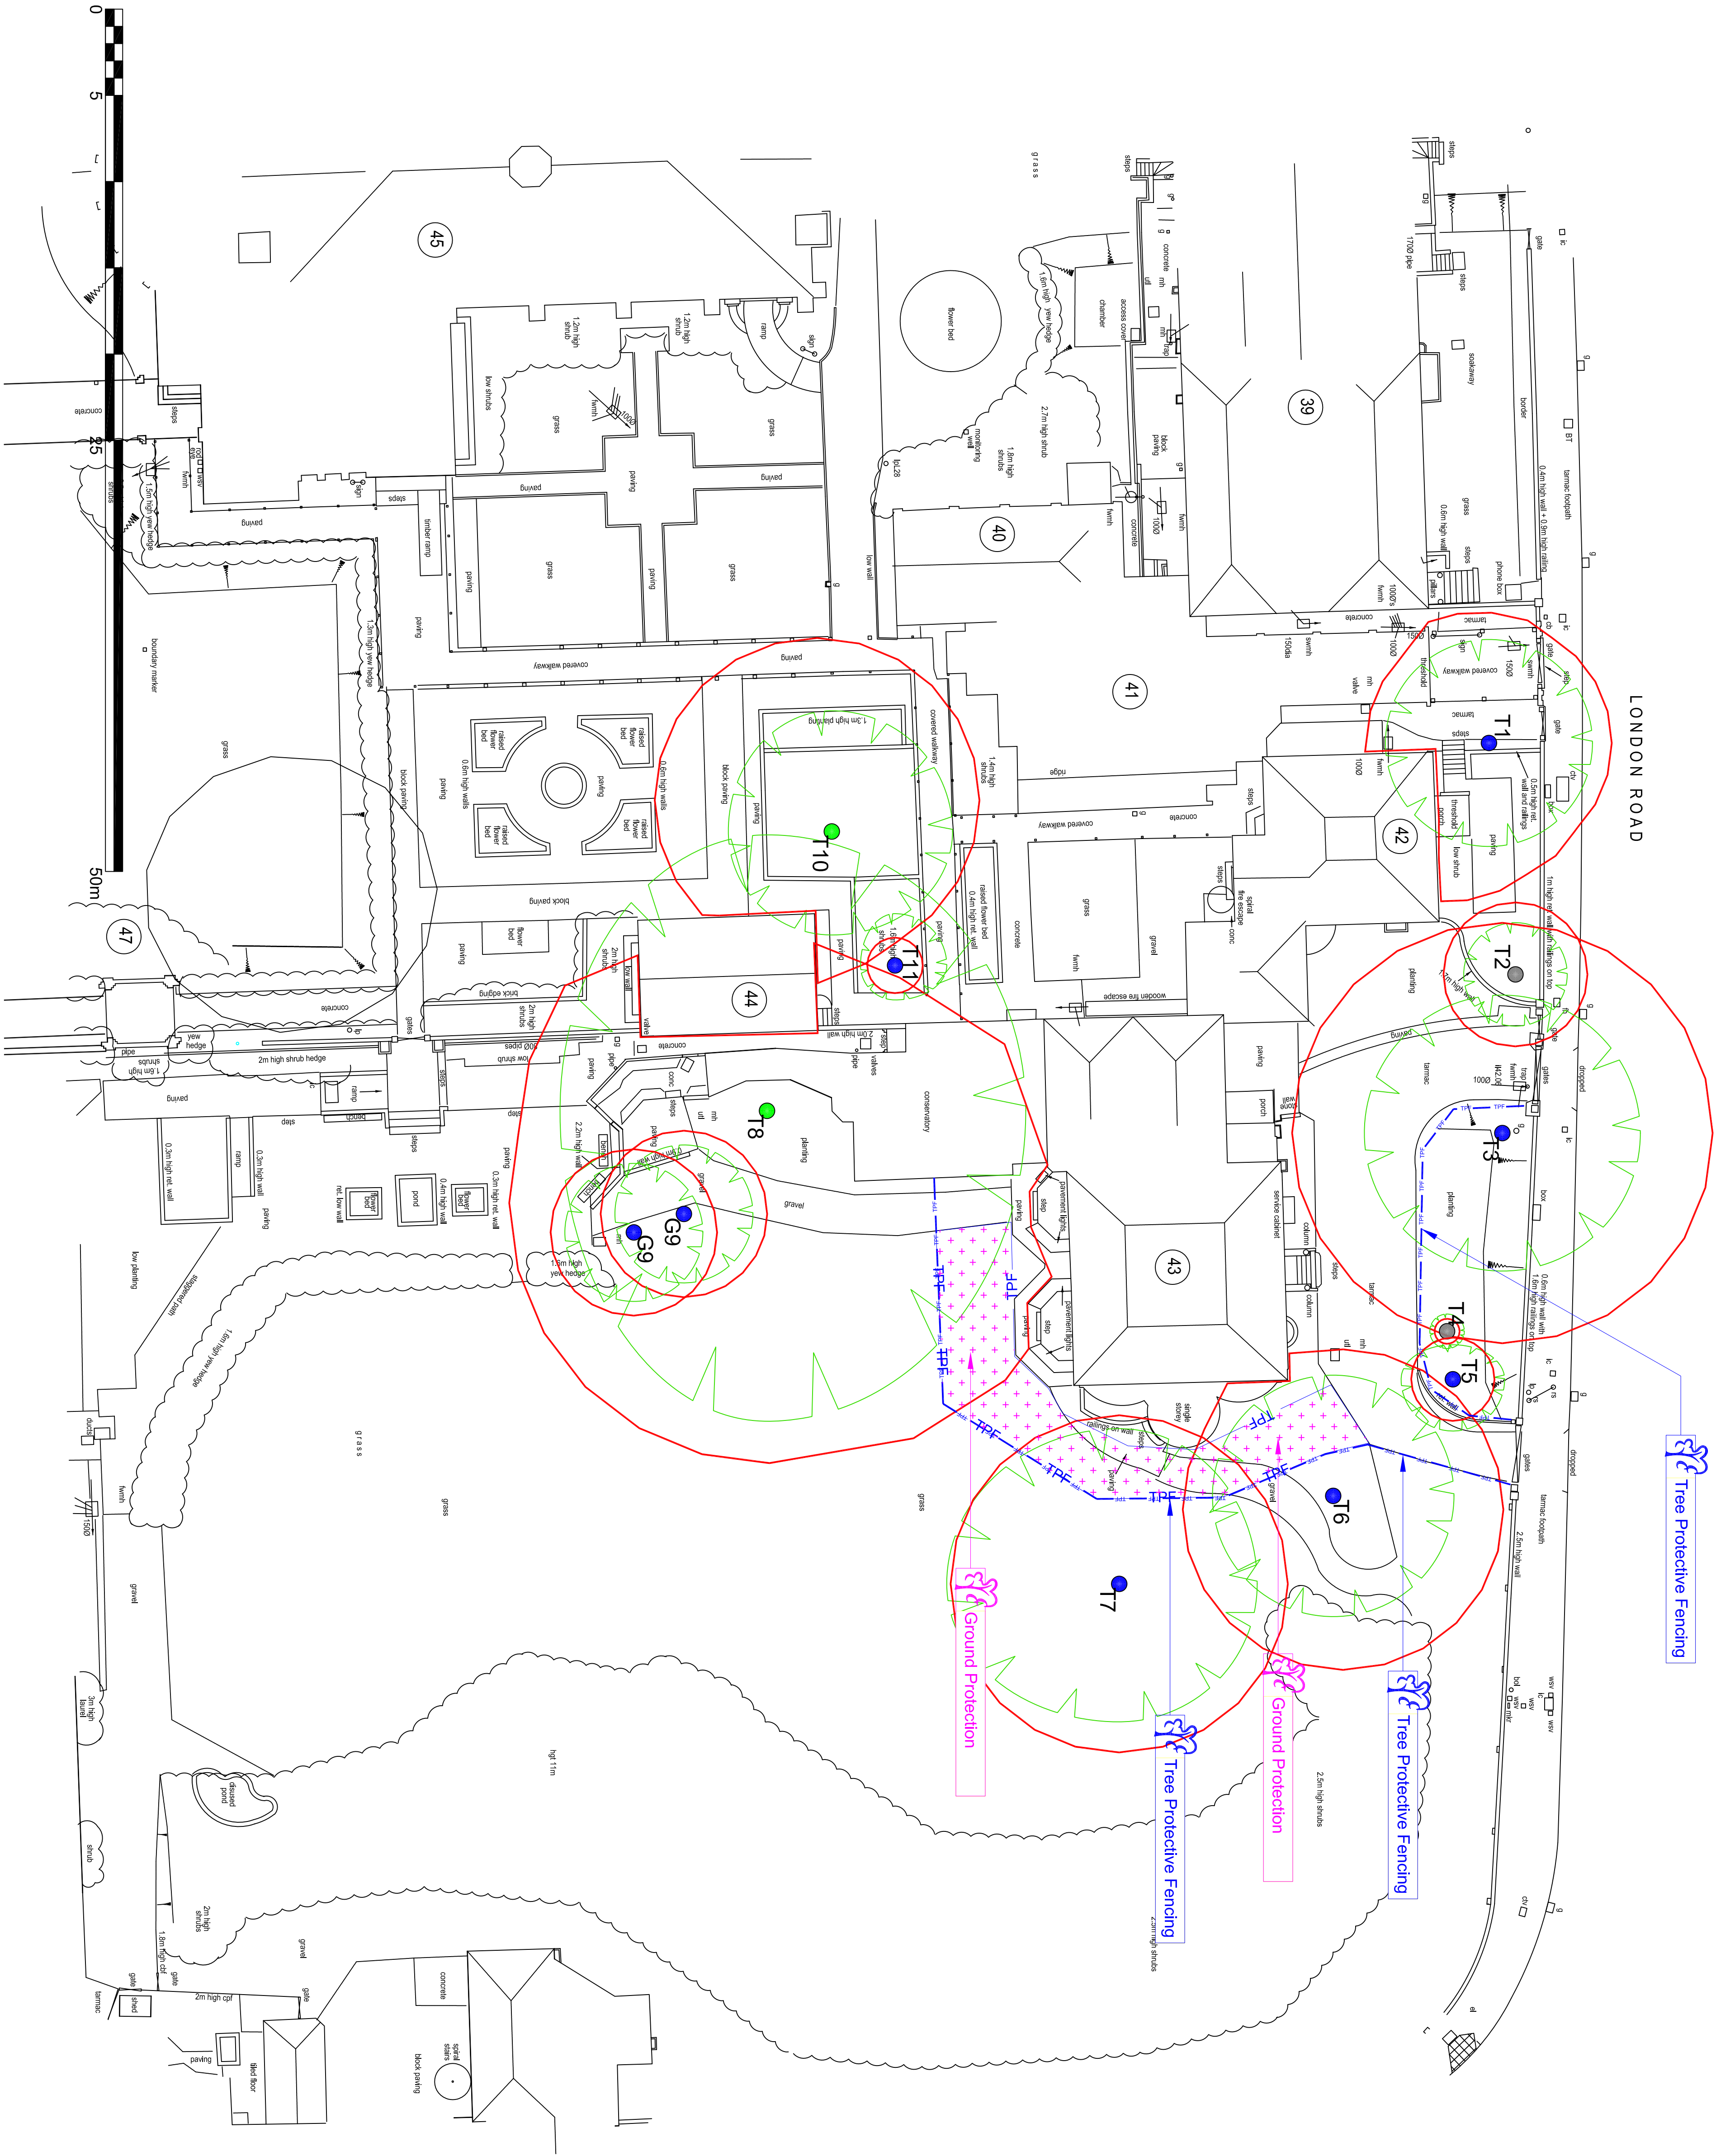

KEY:

	BS roofing area is shown uniform but may be modified to account for site features
	BS roofing area has been modified to account for site features
	A Grade
	B Grade
	C Grade
	U Grade (remove)
	Tree to be removed
	Position of fixed trees style fencing
	Position of ground protection

Challice Consulting Ltd.

annotation

Notes:

Tree protection barrier and ground protection to be erected and installed before machinery or materials are brought onto site, before any demolition or development of land and before soil stripping.

Tree protection measures should be implemented following any necessary pre-development tree work.

Where due to site constraints, construction activity cannot be fully or permanently excluded from all or part of a trees Root Protection Area, appropriate ground protection should be installed.

Barriers and ground protection must not be removed or altered except with prior recommendation by project arboriculturists and where necessary, approval from the Local Planning Authority.

Setting out to be confirmed by project arboriculturists prior to commencement of other operations.

The ground protection detail is to be used where the tree protection barrier needs to be set back so that it will expose unmade ground to construction activity. New temporary ground protection should be installed as part of the physical tree protection measures prior to starting work on site.

Suitable existing hard surfacing not proposed for re-use as part of the finished design shall be retained as ground protection within root protection areas, where and as long as it is possible.

Plan to be printed in colour and to scale

PROTECTIVE

Tree Protection Plan

PROTECTIVE

The Acadas, London Road,
University of Reading

SCALE: 1:200 @ A1 (04.07.2017) [D.C.]
TTP-CH1574 AR3238 1



Challice Consulting Ltd.
Holmwood Farm Garage
Horsham Road
North Holmwood
Dorking
Surrey
RH6 4JR
Tel: 01323 743374
Email: info@challiceconsulting.co.uk
Web: www.challiceconsulting.co.uk

THIS PLAN TO BE USED
FOR SETTING OUT OF
TREE PROTECTION
MEASURES ONLY; DO
NOT SCALE FROM THIS
PLAN UNLESS IT IS
PRINTED AT A1. DO NOT
USE UNLESS PRINTED IN
COLOUR

Appendix 3

Site: Sample
Inspected By: D. Challice
Client: The Builder
Site Agent: No staff present

Date of Inspection:
Time of Inspection:

Tree Protective Fencing

Tree protection in correct location

Comments/Action

No action at this time



Tree protection T23

Agreed Construction Exclusion Zone

No debris within construction exclusion zone

Comments/Action

No action at this time

Amendments to Documentation Required

No amendments required

Comments/Action



Tree protection T14

Remedial Works

Install protection as per Arboricultural Method Statement

General Comments

No ground protection in place for T11,12,14,17 & 22
Sweet Gum T1 not removed

Appendix 4

Induction Form for all Site Personnel:

Site Name:

- I have had explained to me by the Site Manager the key implications of the Arboricultural Method Statement relating to the development at the above site.
- I am aware that the tree protective fencing must remain in its original position and must not be moved without the approval of the appointed Arboricultural Consultant.
- I understand that certain operations must be supervised by the appointed Arboricultural Consultant and that these operations must not start until the consultant is present and has given approval.
- I confirm that I will bring any concerns about potential damage to trees to the attention of the Site Manager.
- I am aware that I must not cause damage to any of the retained trees on or adjacent to the site. Damage may be caused by direct means (i.e. physical damage caused to roots or the trunk/branches of the tree) or by indirect means (e.g. by fire or toxic materials entering the rooting environment of the tree).

Print Name:

Sign Name:

Date:
