

Tree Protection Areas - Construction Exclusion Zones

INSTALLING PROTECTION Protective barriers and ground protection (as approved), must be installed before any materials or machinery are brought onto the site and before the commencement of any demolition, general site clearance, ground or construction works of any description.

RETENTION OF PROTECTION All protective measures must remain fully intact, vertical (in the case of barriers), in their approved locations, from the outset of the development and maintained, at all times, until all works have been completed on site, including any earthworks and associated soft landscaping works. Any approved phasing of protective measures must be fully observed and complied with.

RESTRICTIONS Tree Protection Areas/ Construction Exclusion Zones are to remain completely undisturbed for the duration of all development works. No construction activity of any description including but not limited to the following must occur within these areas at any time.

- No excavation of any description.
- No storage, disposal of soil, rubble or materials of any other description.
- No alterations to existing levels or ground conditions.
- No vehicular access, parking or use of any tracked or wheeled machinery of any description.
- No tree works, without the written consent of the Council's Tree Service.
- No erection of temporary structures of any description.
- No fires.
- No storage disposal handling or use of any Chemicals including cement washings.
- No fixtures or fittings of any description, security lighting, signage etc shall be attached to any part of a tree.


- No fires shall be light within 10 metres of the canopies of any tree or spread of any hedge.

- No chemicals, fuel, liquids/waste residues of any other description to be stored or disposed of within close proximity to or drained towards/ into protection areas.

PROTECTION AREA SIGNAGE - All weather notices as below or similar to be fixed to protective barriers at regular intervals (maximum spacing 5m) throughout site and maintained until completion of all development works




PLANNING COMPLIANCE - The protective measures detailed on this drawing are a legal requirement. Failure to protect the trees/ hedges in full accordance with the approved scheme may lead to enforcement action being taken by the Local Authority.

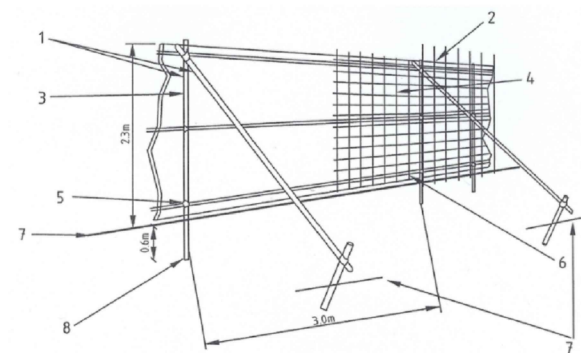

- Standard scaffold poles
- Uprights to be driven into the ground
- Poles secured to uprights with wire ties and, where necessary, standard scaffold clamps
- Wiremesh welded to the uprights and horizontals
- Standard clamps
- Wire hauled and secured on inside face of fencing to avoid any climbing
- Ground level
- Approx. 0.6m driven into the ground

BS:5837 Figure 2 - Tree Protection Fencing structure around RPA

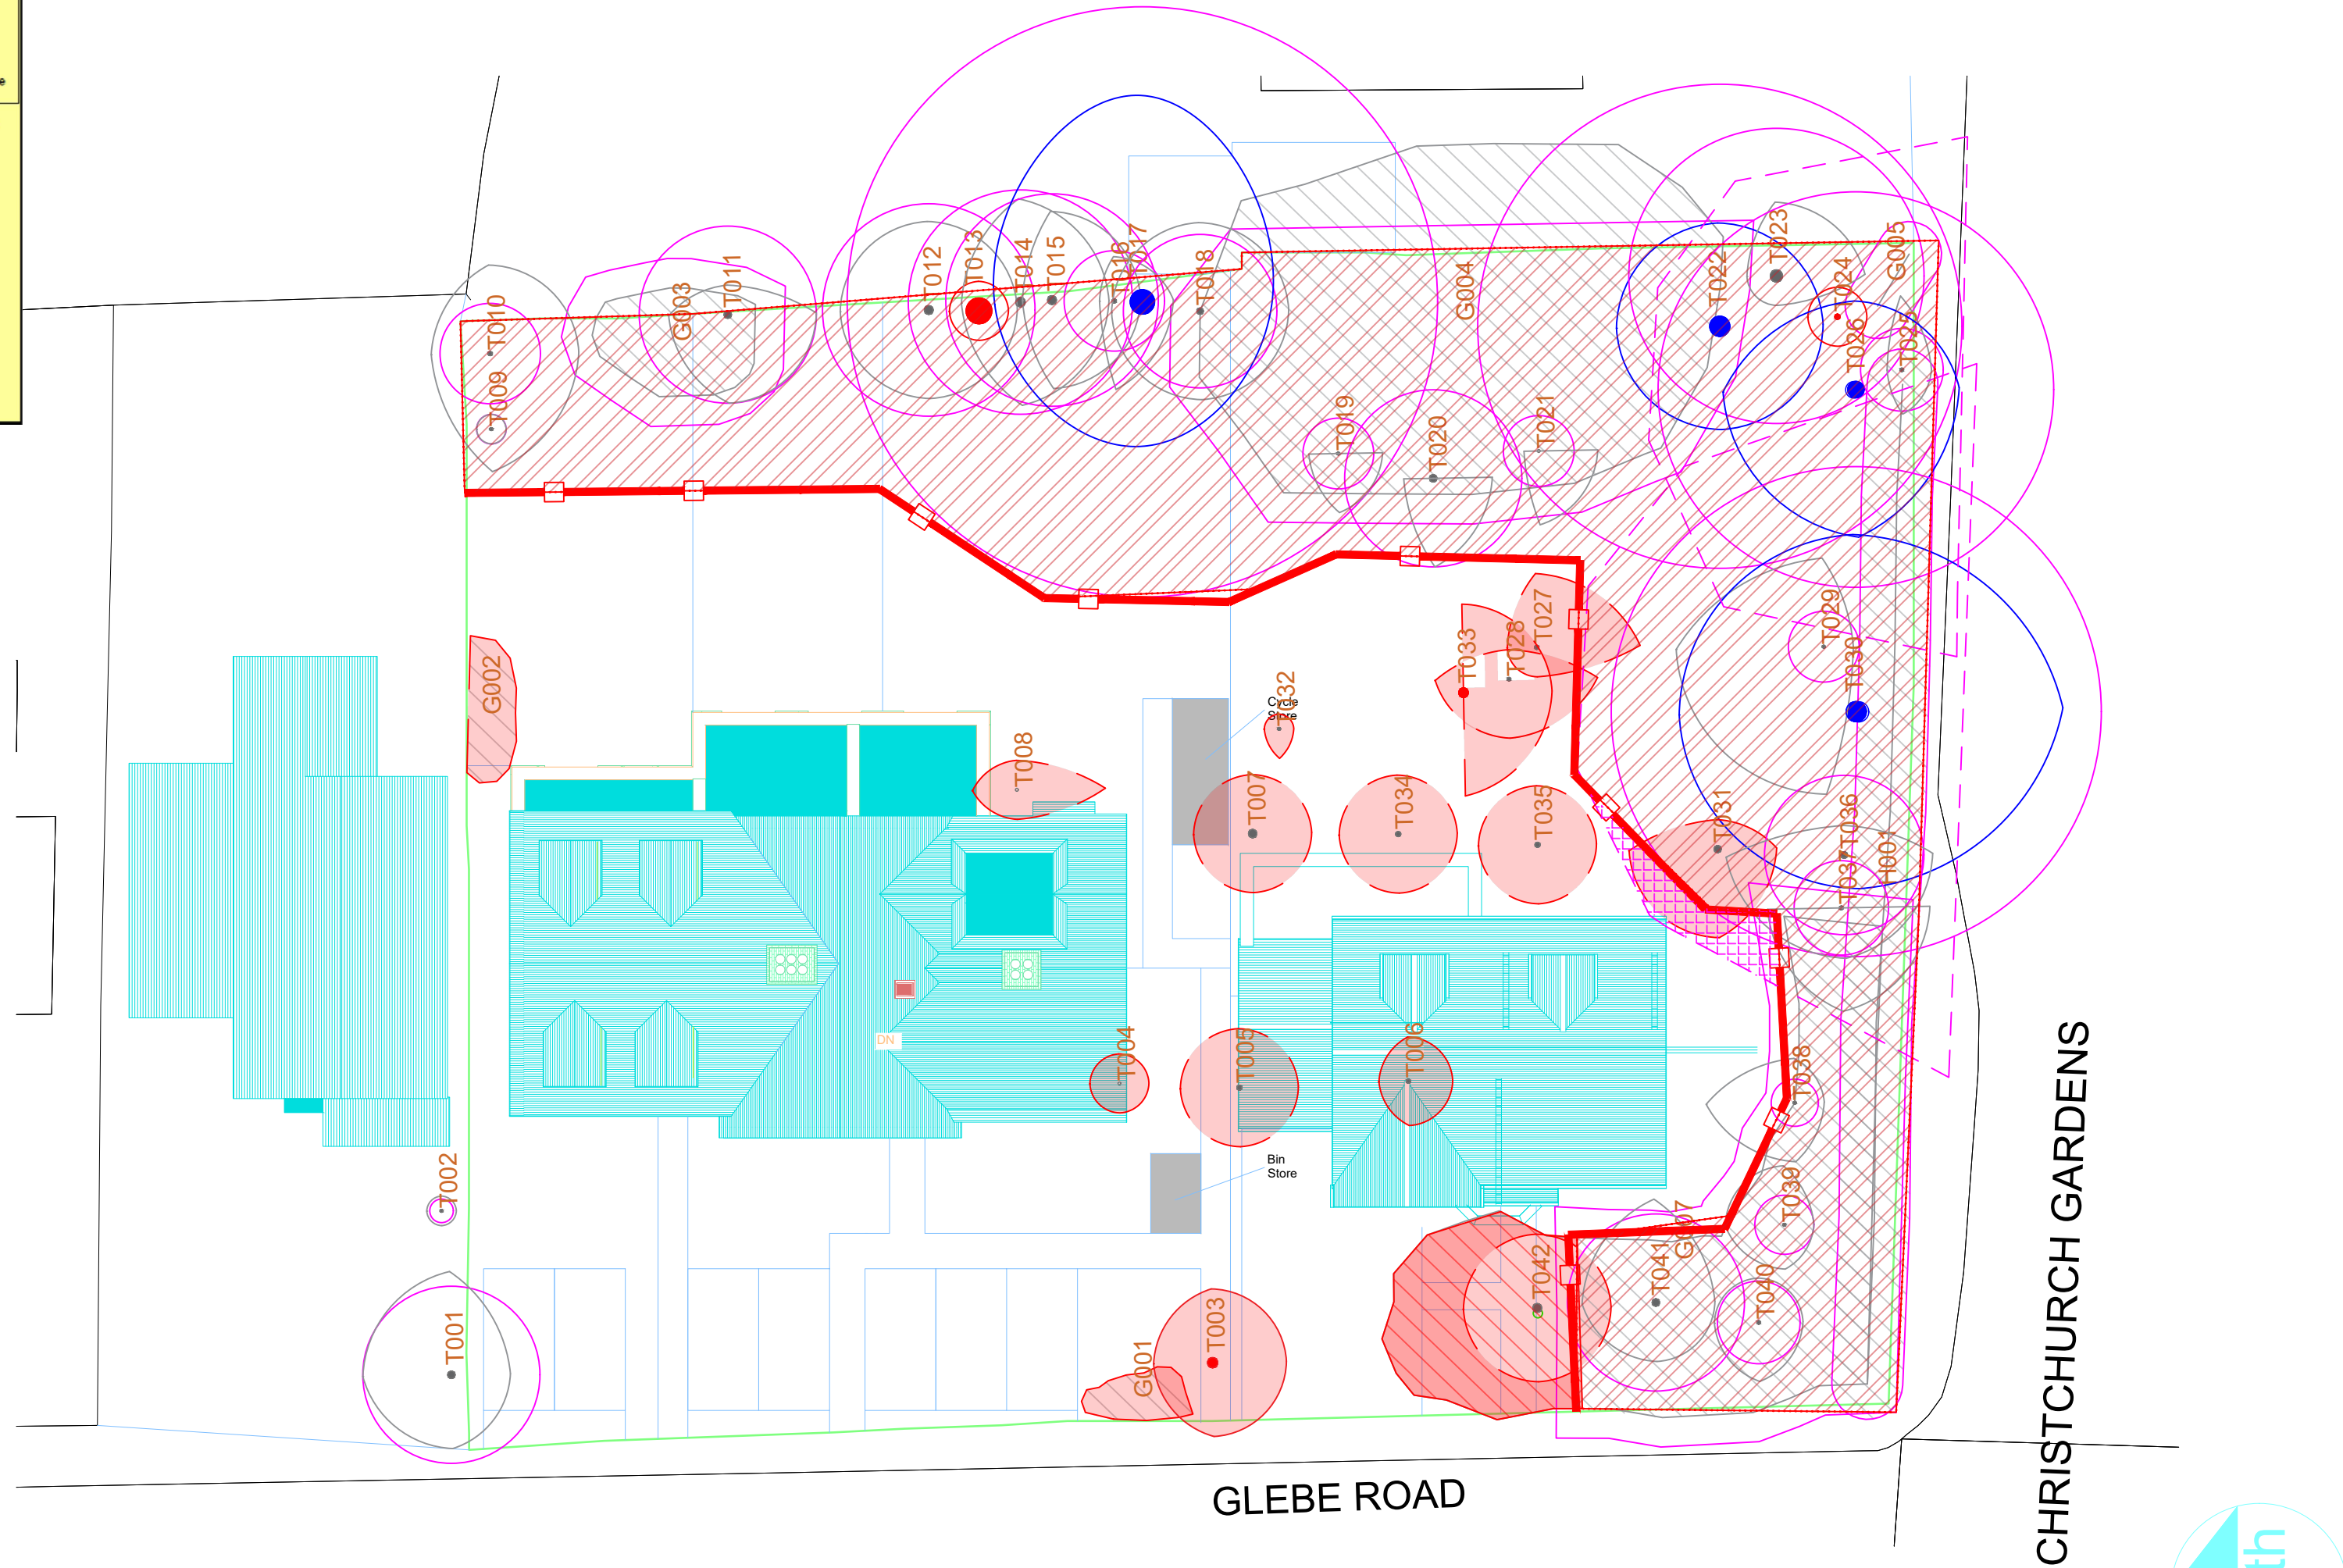

KEY - TREES

- HIGH-GRADE CATEGORY 'A' TREE
PROTECT & RETAIN
- MEDIUM-GRADE CATEGORY 'B' TREE
PROTECT & RETAIN
- LOW-GRADE CATEGORY 'C' TREE
PROTECT & RETAIN WHERE POSSIBLE
- CATEGORY 'U' POOR QUALITY TREE -
HAZARDOUS
- ROOT PROTECTION AREA (RPA)
- OFFSET ROOT PROTECTION AREA
- TEMPORARY TREE PROTECTION
FENCING
- TEMPORARY GROUND PROTECTION
- CONSTRUCTION EXCLUSION ZONE
- KEEP OUT!

**BS:5837 TREE
PROTECTION
PLAN**

Client:
MICHAEL SNOOKS / LANDIM

Site:
11 GLEBE ROAD
READING
BERKSHIRE
RG2 7AG

A topographical survey has been provided by the client. Smaller trees not shown in the topographical survey have been plotted by eye by the Tree Surveyor.

The position of trees should not be taken as exact but is considered to be a good representation of their locations in relation to the property and any future building works.

Survey by Sarah Duckworth
Arboricultural Consultant

sarahduckworth@hotmail.com
T:01672 519811 M:07810440546

Scale 1:200 @ A2
Date: JULY 2024

Ref: 11 GLEBE ROAD (BS5837) TPP 06404 / 2024

