


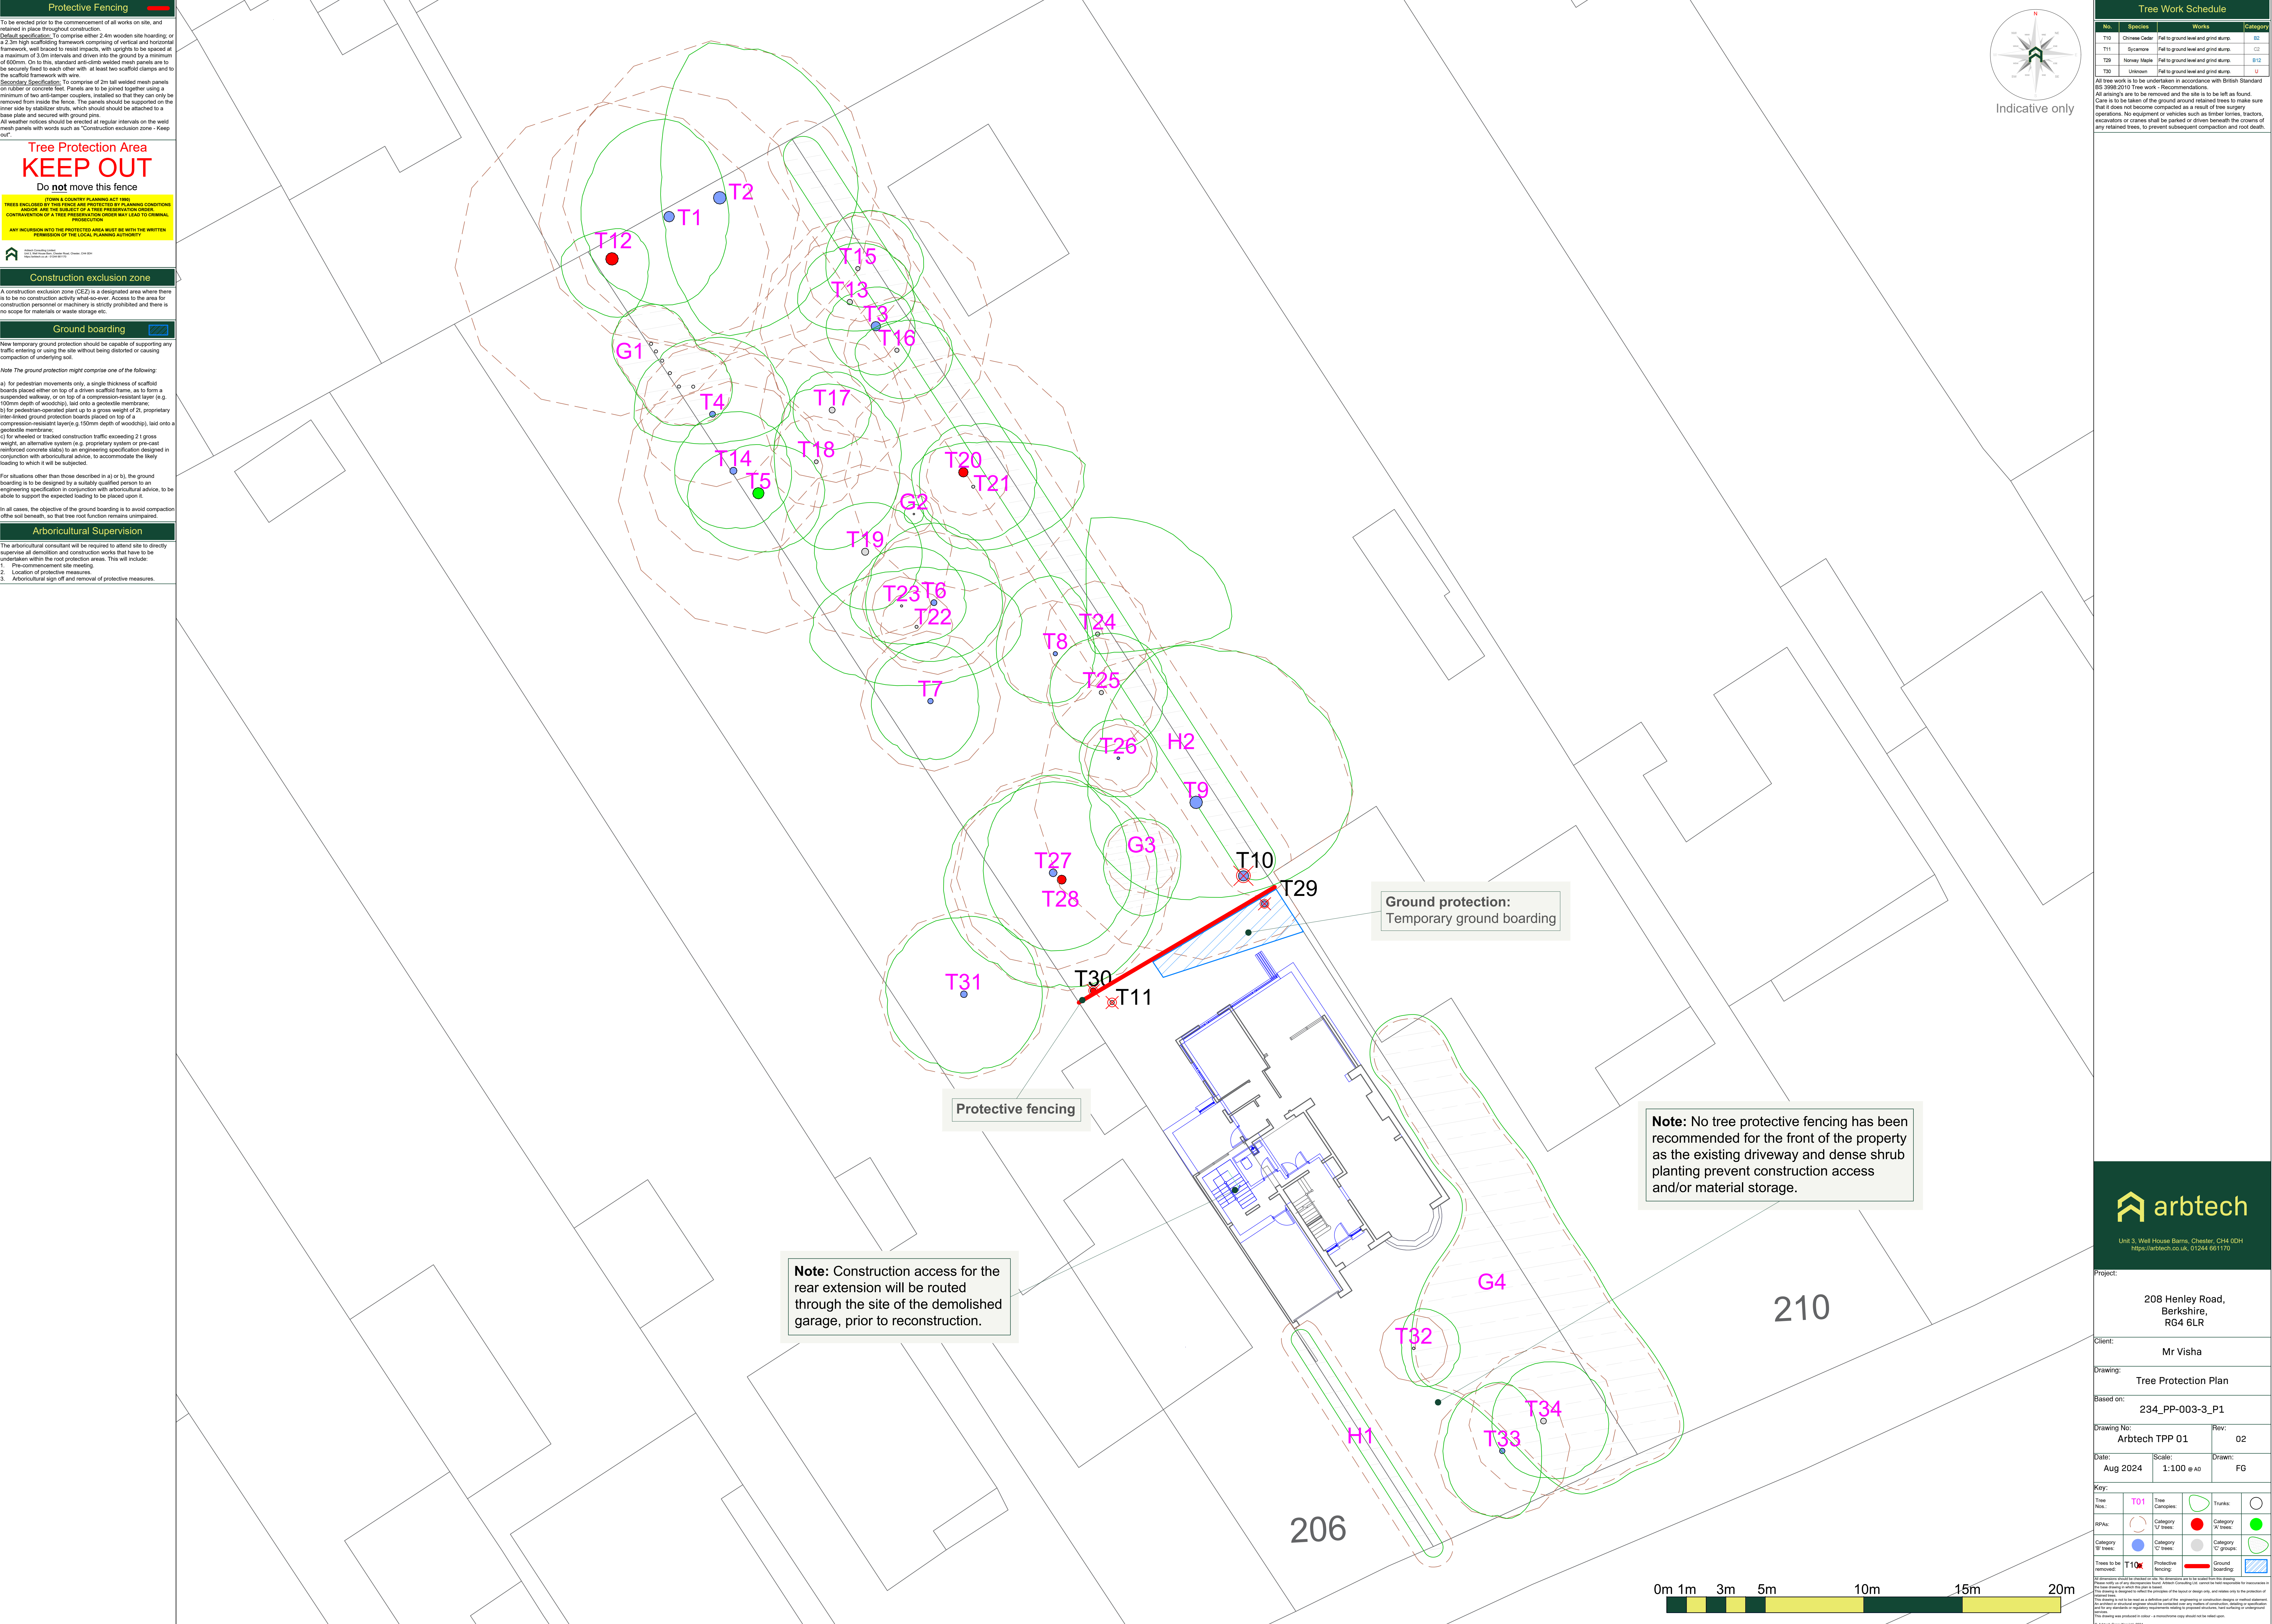

Protective Fencing

To be erected prior to the commencement of all works on site, and retained in place throughout construction.

Default Specification: To comprise either 2.4m wooden site hoarding, or a 2.3m high scaffolding framework comprising of vertical and horizontal framework, well braced to resist impacts, with uprights to be spaced at a maximum of 3.0m intervals and driven into the ground to a minimum of 600mm. On to this, standard anti-climb welded mesh panels are to be securely fixed to each other with at least two scaffold clamps and to the scaffold framework with wire.

Secondary Specification: To comprise of 2m tall welded mesh panels on rubber or concrete feet. Panels are to be joined together using a minimum of two anti-lamper couplers, installed so that they can only be removed from inside the fence. The panels should be supported on the inner side by stabilizer struts, which should be attached to a base plate and secured with ground pins.

All weather notices should be erected at regular intervals on the wind mesh panels with words such as "Construction exclusion zone - Keep out".

Tree Protection Area

KEEP OUT

Do not move this fence

FROM A COUNTY COUNCIL PLANNING ACT 1990
THESE ENCLOSURES ARE THE PROPERTY OF PROTECTED PLANNING CONDITIONS
AND/OR ARE THE PROPERTY OF A TREE PRESERVATION ORDER.
CONVICTION OF A TREE PRESERVATION ORDER MAY LEAD TO CRIMINAL PROSECUTION.

ANY INCURSION INTO THE PROTECTED AREA MUST BE WITH THE WRITTEN PERMISSION OF THE LOCAL PLANNING AUTHORITY.

Construction exclusion zone

A construction exclusion zone (CEZ) is a designated area where there is to be no construction activity what-so-ever. Access to the area for construction personnel or machinery is strictly prohibited and there is no scope for materials or waste storage etc.

Ground boarding

New temporary ground protection should be capable of supporting any traffic entering or using the site without being distorted or causing compaction of underlying soil.

Note: The ground protection might comprise one of the following:

- a) for pedestrian movements only, a single thickness of scaffold boards placed either on top of a driven scaffold frame, as to form a suspended walkway; or on top of a compression-resistant layer (e.g. 100mm depth of woodchip), laid onto a geotextile membrane;
- b) for pedestrian-operated plant up to a gross weight of 2t, proprietary inter-linked ground protection boards placed on top of a compression-resistant layer (e.g. 150mm depth of woodchip), laid onto a geotextile membrane;
- c) for wheeled or tracked construction traffic exceeding 2t gross weight, an alternative system (e.g. proprietary system or pre-cast reinforced concrete slabs) to an engineering specification designed in conjunction with arboricultural advice, to accommodate the heavy loading to which it will be subjected.

For situations other than those described in a) or b), the ground boarding is to be designed by a suitably qualified person to an engineering specification in conjunction with arboricultural advice, to be able to support the expected loading to be placed upon it.

In all cases, the objective of the ground boarding is to avoid compaction of the soil beneath, so that tree root function remains unimpaired.

Arboricultural Supervision

The arboricultural consultant will be required to attend site to directly supervise all demolition and construction works that have to be undertaken within the root protection areas. This will include:

1. Pre-commencement site meeting;
2. Location of protective measures;
3. Arboricultural sign off and removal of protective measures.

Tree Work Schedule

No.	Species	Works	Category
T10	Cherry Cedar	Fell to ground level and grind stump.	B2
T11	Sycamore	Fell to ground level and grind stump.	C2
T28	Hornbeam	Fell to ground level and grind stump.	B12
T30	Unknown	Fell to ground level and grind stump.	1

All tree work is to be undertaken in accordance with British Standard BS 3998:2010 Tree work - Recommendations.

All stumps are to be removed and the site is to be left as found. Care is to be taken of the ground around retained trees to make sure that it does not become compacted as a result of tree surgery operations. No equipment or vehicles such as timber lorries, tractors, excavators or cranes shall be parked or driven beneath or over of any retained trees, to prevent subsequent compaction and root death.

arbtech

Unit 3, Well House Barns, Chesham, G44 0DH
http://arbtech.co.uk, 01294 681170

Project:

208 Henley Road,
Berkshire,
RG4 6LR

Client:

Mr Visha

Drawing:

Tree Protection Plan

Based on:

234_PP-003-3_P1

Drawing No:

Arbtech TPP 01

Rev:

02

Date:

Aug 2024

Scale:

1:100 @ A0

Drawn:

FG

Key:

Tree Nos.:	T01	Tree Canopies:		Trunks:	
RPAs:		Category 'U' trees:		Category 'A' trees:	
Category 'B' trees:		Category 'C' trees:		Category 'D' trees:	
Trees to be removed:	T10	Protective fencing:		Ground boarding:	

0m 1m 3m 5m 10m 15m 20m
