

Intended for
St Edward Homes Limited

Document type
Report

Date
October, 2017

Job No
1620000492

GREEN PARK VILLAGE PHASE 5 ENABLING WORKS VERIFICATION REPORT

GREEN PARK VILLAGE PHASE 5 ENABLING WORKS VERIFICATION REPORT

Revision **R01**
Date **11/10/2017**
Made by **Jørn Pace / Tom Smith**
Checked by **Tom Smith**
Approved by **Simon Corness**
Description **Verification Report**

Ref 1620000492/RPT/011

Ramboll
Carlton House
Ringwood Road
Woodlands
Southampton
SO40 7HT
United Kingdom
T +44 (0) 238 081 7500
F +44 (0) 845 299 1610
www.ramboll.co.uk

CONTENTS

1.	INTRODUCTION	1
1.1	Brief	1
1.2	Constraints and Limitations	1
2.	BACKGROUND INFORMATION	2
2.1	Site Location and Description	2
2.2	Proposed Development and Intended Earthworks	2
2.3	Previous Work	2
3.	VALIDATION OF ENABLING WORKS	5
3.1	Introduction	5
3.2	Project Roles	5
3.3	Ramboll watching briefs during enabling works	5
3.3.1	Stage 1 Works – August / September 2016	5
3.3.2	Stage 2 Works – April/May 2017	6
3.3.3	Stage 3 Works – June 2017	7
3.3.4	Additional Drainage Works	8
3.3.5	Licensing Status	8
3.3.6	Implementation of Asbestos Control Measures	8
3.3.7	Background Reassurance Monitoring	8
3.4	Clean service corridors	9
3.5	Clean cover system	9
3.6	Unforeseen contamination protocol	9
4.	CONCLUSION	10

APPENDICES

Appendix 1 – Figures/Drawings

Appendix 2 – Analytical Results

Appendix 3 – Photographic Record

Appendix 4 – Lucion Bulk Sample Analysis

Appendix 5 – Lucion Background Air Monitoring Results

Appendix 6 – Duty of Care Information

Appendix 7 – Report Reliance

1. INTRODUCTION

1.1 Brief

Ramboll UK Limited has been appointed by St Edward Homes Limited to prepare a Verification Report following the enabling works in Phase 5 of the proposed Green Park Village (GPV) development. Phase 5 is split into two sub phases comprising Phase 5A and Phase 5B.

This Verification Report has been prepared pursuant to Condition 44 of Planning Permission ref 10/01461/OUT dated 13th July 2011 which states that:

Within one month of the completion of any required remediation being carried out for each phase of development, a Site Completion Report shall be submitted to, and approved in writing by, the local planning authority for that phase. The report must include;

Confirmation that all remediation measures have been carried out fully in accordance with the approved remediation scheme. An appropriately qualified person shall oversee the implementation of all remediation.

A long term monitoring and maintenance plan for longer term monitoring of pollutant linkages, maintenance and arrangements for contingency action and for the reporting of this to the local planning authority.

If no contamination is encountered during the development, a letter confirming this fact shall be submitted to the local planning authority upon completion of the development.

This Verification Report forms the 'Site Completion Report' which provides documentary evidence that the risk management measures identified within the Ground Investigation Findings and Remedial Options Technical Note¹ have been successfully completed onsite. A key component of this was mitigation of asbestos risks during the enabling works within Phase 5A with operational procedures formalised within an Asbestos Management Plan² (AMP) for the site.

The scope of works within this report comprises validation of the actions taken at the site in accordance with the Ground Investigation Findings and Remedial Options Technical Note¹.

1.2 Constraints and Limitations

This report has been prepared for the use of St Edwards Homes Ltd and should not be used in whole or in part by any third parties without the express permission of Ramboll in writing. This verification report has been prepared with reference to the information sources presented in Table 2.1. Ramboll has endeavoured to assess all information provided to them during this validation process, however, this report summarises information provided from a number of external sources and Ramboll cannot offer any guarantees or warranties for the completeness or accuracy of information relied upon.

¹ Ramboll (2016). Asbestos Ground Investigation Findings and Remedial Options ref. 1620000492/TN/003

² Ramboll (2017). Asbestos Management Plan – Phase 5 Green Park Village ref. 1620000192-GPV-P5-AMP-R3

2. BACKGROUND INFORMATION

2.1 Site Location and Description

The GPV site is located approximately 4km to the south of Reading Town Centre, Berkshire. Phase 5 is present on the northern central area of the GPV site occupying approximately 2.10 ha at a National Grid reference of SU 699 703. Phase 5 is bounded by a historic landfill site to north, Trout Lakes to the west and Phases 1, 4, 6 and 3C to the south, east and north respectively. The site location is shown in Figure 1 in Appendix 1.

Early Ordnance Survey mapping (1883) indicates that Phase 5 was undeveloped open land known as "Smallmead Common". By the 1990s the area to the west of the north-south trending ditch was a vehicle storage area belonging to Pingemead Industrial Estate (Phase 5A). The area to the east of the (north-south) ditch was undeveloped open land with evidence of re-profiling of the ground and stockpiling (Phase 5B). These stockpiles have been utilised for the purpose of land raising at Phase 1.

Following the clearance of Phase 5A and the former industrial estate, upon lifting and breaking of the concrete slab in the south-western corner of the phase in 2016, suspected cement bound asbestos sheeting was identified within the soils. Delineation of the impacted soil was subsequently undertaken and is discussed within Section 2.3.

2.2 Proposed Development and Intended Earthworks

Proposals for Phase 5 of the GPV redevelopment comprise residential housing with gardens, with areas of soft landscaping and associated infrastructure.

As part of the redevelopment, the site will be raised to an elevation of approximately 40.2 m above ordnance datum (AOD) for flood alleviation purposes. The existing ground level at the site is approximately 39mAOD. The filling activities are to be undertaken under waste recovery Environmental Permit number EPR/DB3206HL.

The enabling works phase of the redevelopment within Phase 5 was proposed to comprise the turning over of the Made Ground to remove oversize materials and obstructions ahead of ground improvement, the compaction of the soils and the placement of a brightly coloured demarcation layer to signify the divide between clean soils imported as part of the land raise and the asbestos impacted soils underneath.

2.3 Previous Work

Various phases of work have been undertaken at the site to assess the potential risks from contamination, as summarised in Table 2.1.

Table 2.1: Information Sources

Report	Author	Date
Geoenvironmental Investigation for Phase III, Green Park, Reading	Peter Brett Associates	August 2002
Earthwork Material Suitability Assessment. Phase III, Green Park, Reading	Peter Brett Associates	November 2005
Ground Contamination Interpretative Report	Ramboll	March 2016

Report	Author	Date
Technical Note - Asbestos Ground Investigation Findings and Remedial Options ref. 1620000492/TN/003	Ramboll	July 2016
Asbestos Management Plan – Phase 5 Green Park Village ref. 1620000192-GPV-P5-AMP-R3	Ramboll	April 2017

As discussed within Section 2.1, suspected cement bound asbestos sheeting was identified within the soils of the south-western corner of Phase 5A. Twenty-three trial pits were initially undertaken across Phase 5A alongside the collection of four composite samples from the cement sheeting impacted soils to delineate the extent of the asbestos contamination across the phase. The initial delineation exercise identified the asbestos impacts to spread across Phase 5A with bulk asbestos containing materials (ACM) in the form of cement bound sheeting (frequently encountered), insulation board, lagging (infrequently encountered) and also free fibres. Further details of the initial delineation exercise are included in the Technical Note on Asbestos Ground Investigation Findings and Remedial Options.

The remediation strategy contained within the Technical Note is centred on the land raise works comprising the capping of the impacted residual soils with the importation and placement of clean soils and separation with a demarcation layer. Further specific mitigation actions required during the enabling works and outlined within the strategy included:

- Further delineation of the asbestos impacted soils within Phase 5A;
- Waste management procedures for any unsuitable materials arising during enabling works;
- Creation of a clean service corridors for deep sewers within the Phase;
- Provision of a clean cover system through general filling under the Environmental Permit within the Phase; and
- Adoption of an unforeseen contamination protocol.

In addition, and in relation to asbestos risks during the enabling works, several procedural mitigation measures were recommended including the use of suitable personal and respiratory protective equipment (PPE/RPE), reassurance air monitoring for asbestos fibres and 'clean' and 'dirty' work areas separated by fences, warning signs and a decontamination unit. These operational procedures were formalised within an Asbestos Management Plan (AMP)² which was prepared to allow site enabling works to progress in an appropriate safe manner.

Table 2.2 below contains an overview of the control measures contained within the AMP that were required to be in place for any earthworks associated with asbestos impacted soils at Phase 5A.

Table 2.2: Overview of Control Measures

Methodology	Responsible Party	Control Measures
Watching Brief	Ramboll	Trained and competent person to assess contaminated soils during the excavation process.
Air monitoring	Lucion Environmental	Independent air monitoring to be conducted around the Phase 5A site to provide quantitative data with respect to fibre suppression mitigation measures. To include boundary, operational and personal air monitoring.
Excavation Controlled	Contractor	Impacted area fenced off, adequate signage provided.

Methodology	Responsible Party	Control Measures
Earthworks and site quarantine		
Dust suppression	Contractor	Dust suppression will be required in all areas of excavation. Dust suppression method shall be dependent on available water supply, but as a minimum will comprise low pressure jet-washers with bowzers in each of the areas in which Ramboll personnel are working. Dust suppression to be the responsibility of the Contractor personnel.
Movement of impacted soils [If required]	Contractor	Implement Contractor Materials Management Plan (MMP) to control the movement of asbestos contaminated soils. Contaminated soil movements further outlined if required.
Movement of non-impacted materials [e.g. concrete obstructions for crushing],	Contractor	Adherence to MMP for all material movements. Inspection of stockpiles prior to movement by Watching Brief for the presence of visible asbestos. Following processing of materials further testing recommended.
PPE	All parties	Use appropriate PPE at all times: • Washable safety boots or a dedicated pair of safety boots for the 'dirty' side of the decontamination unit; • Disposable gloves and Category 3 Type 5/6 Tyvek disposable hooded overalls; • Face Fitted Respirators EN140 with P3 filter, semi-disposable respirators – EN405 with P3 filter

Based on the type and condition of ACMs encountered during the delineation works, it was anticipated that the enabling works would be categorised as unlicensed works. It was also considered that the works were not expected to significantly induce any deterioration of the ACMs. Ramboll's watching brief during the enabling works was undertaken to determine whether the consideration of non-licensed work remained applicable to the works being carried out. Such consideration could be altered from the identification of asbestos coating or asbestos insulation board (AIB) or the works leading to the deterioration of any ACMs present.

Section 3 provides the documentary evidence collated to demonstrate that the enabling works were carried out in accordance with the Remediation Strategy¹ and AMP².

3. VALIDATION OF ENABLING WORKS

3.1 Introduction

The information presented in this section aims to demonstrate how the risks outlined above, and in particular the potential asbestos hazard, were managed during the enabling works at the site.

3.2 Project Roles

St Edwards Homes Ltd (SEHL) employed Woolridge Ecotec Ltd (WEL) to undertake the enabling works comprising the 'turning over' of Made Ground for the removal of below ground obstructions and oversized materials, placement of a brightly coloured marker layer and compaction of soils. This works was undertaken in three stages in August/September 2016, April/May 2017 and June 2017 as shown on Figure 4. Further details of the enabling works carried out by WEL are contained within their Asbestos Remediation Completion Report³.

Lucion Environmental (Lucion) were employed by SEHL to provide reassurance air monitoring to confirm the works were not leading to the mobilisation of airborne fibres. Lucion were also responsible for the analysis of bulk asbestos samples collected throughout the course of the works.

Ramboll acted as the project Environmental Consultant throughout the enabling works. A watching brief was provided for the turning over works with Ramboll's duties comprising the following:

- Visual assessment of the Made Ground for ACM;
- Liaison with Lucion Environmental for the provision of background air and personal monitoring;
- Provision of toolbox talks on the AMP for site operatives entering the 'asbestos exclusion zone'; and
- Provision of advice to WEL regarding the use of PPE/RPE, dust suppression, the use of the decontamination unit and washing down of plant exiting the asbestos exclusion zone.

3.3 Ramboll watching briefs during enabling works

3.3.1 Stage 1 Works – August / September 2016

Asbestos Exclusion Zone and Additional Delineation Investigation

Due to the identification of ACM within the previous delineation exercise, additional trial pits were undertaken prior to the commencement of the turning over works on the 24th August 2016 to determine the extent of the asbestos exclusion zone. With the exception of chrysotile loose fibres below detection limits (<0.001% weight/weight) within RTP26 at 0.1m, no ACMs were identified within the trial pits RTP21 to RTP28. The locations of RTP21 to RTP28 are shown on the AMP works plan - Figure 2. It was therefore agreed with WEL that these trial pits would mark the area in which the turning over works would extend to beneath proposed building footprints, essentially constraining the works to Phase 5A with no asbestos related works required in Phase 5B. Analytical Results associated with the delineation exercise are presented in Appendix 2.

The asbestos exclusion zone was separated from the surrounding areas by heras fencing with asbestos warning signs. A decontamination unit was installed on the north-eastern corner of

³ Woolridge Ecotec Ltd. (2017). Phase 5A Asbestos Remediation Completion Report ref. GPV-PH5AARC-REV2

the asbestos exclusion zone. The extents of the asbestos exclusion zone during Ramboll's watching briefs are shown in the photographic record in Appendix 3.

Ramboll were present on site for the turning over works between the 24th August and 23rd September 2016. During the course of works numerous cement bound asbestos fragments were identified particularly in the southern section of Phase 5A reducing in frequency towards the north. Where suspected higher risk ACMs were identified including AIB or lagging, Ramboll would consult with Lucion prior to the material being sampled and sent to Lucion's laboratory for bulk identification analysis. In each instance where suspected higher risk ACMs were encountered, they were identified as single fragments or debris rather than hotspots of frequent occurrences. With the exception of the detection of AIB fragments near the commencement of the turning over works, no other high risk ACMs (lagging, AIB) were identified. Ramboll continued to consult with Lucion throughout the works and based on their/Ramboll's professional opinion and the results of the bulk identification analysis, no further high risk ACMs were encountered.

During the course of visible fragments of asbestos were handpicked by UKATA trained personnel, double bagged and goose necked tied along with contaminated masks and coveralls. These were removed from site on 5th October 2016 by WEL (carrier license CBDU81963) to Comley and Sons, Calf Lane, Rye Common, Odiham, RG29 1HU (permit ref FP3393EF/V003).

Following completion of the turnover works the ground was compacted and a brightly coloured orange membrane was laid out across the area. Figure 3 shows the area which had the Made Ground turned for obstructions during Ramboll's presence on site in Stage 1. Ramboll were informed that the turning over works continued following their departure from site with the final turned, compacted and membrane installed area shown within Figure 4 and Appendix A of WEL's Remediation Completion Report³.

Deep Made Ground Area

During the course of the enabling works, an area of deeper Made Ground was identified within the central western section of Phase 5A. The Made Ground consisting predominantly of tyres, oversized metal and black ash extended below the groundwater table at circa 2mbgl. Two samples (P5_A and P5_B) of the deep Made Ground were collected and analysed to determine whether the material required separate segregation. The samples were scheduled against a suite containing asbestos, heavy metals, inorganics, petroleum hydrocarbons, volatile and semi-volatile organic compounds. The samples were identified to contain ACM albeit below detection limits and a single occurrence of marginally elevated lead (330mg/kg) against residential Generic Assessment Criteria. Based on the limited evidence of the deep Made Ground being grossly contaminated, attempts were made to continue excavating the obstructions. However this became unfeasible due to the lack of visibility below groundwater and turning over works was ceased in this area. The indicative area of deep Made Ground is shown on Figure 3. Analytical Results are presented in Appendix 2.

3.3.2 Stage 2 Works – April/May 2017

Following finalisation of the proposed lakeside contouring the second stage of turnover works were completed between 10th April and 3rd May 2017 and principally involved a continuation of obstruction clearance and extension of the brightly coloured marker layer across the western boundary of Phase 5A to the trout lake edge. At the time of the works the western strip that required clearance was an elevation approximately 0.5 m to 1 m lower than the ground to the east which had been remediated during Stage 1 and subsequently raised.

The asbestos exclusion zone was separated from the surrounding areas by heras fencing with asbestos warning signs. A decontamination unit was installed on the central western edge of the asbestos exclusion zone. The extents of the asbestos exclusion zone during Ramboll's watching briefs are shown in the photographic record in Appendix 3. An access route was created within the exclusion zone upon the higher previously remediated area to allow for the dust suppression bowser and dumper to access the work area without tracking over impacted soils.

At the start of works it became apparent that the western extent of the area remediated during Stage 1 was at an elevation higher than the revised contours. As such initial works comprised the removal of the western ~3 m of this platform down to the previously installed demarcation layer and re-profiling to tie in with the revised contours.

Following this the western strip was turned over and excavated to allow for the installation of a 1 m clean cap. During the turnover process WEL collected four additional soil samples for waste analysis as any material arising from these excavations had previously been classified as unsuitable for reuse and treated as excess necessitating removal. Analysis indicated the soils to be classified as non-hazardous waste owing to the presence of asbestos containing materials but at concentrations below the hazardous waste threshold of 0.1% w/w. The strip of excess soils progressed from south to north with materials stockpiled and subsequently loaded on to wagons (with dust suppression) for removal within a designated loading bay at the northern boundary of the exclusion zone.

In total ~700 m³ of non-hazardous waste soils were removed from site by WEL (carrier license CBDU81963) to Bugle Nurseries Ltd landfill on Upper Halliford Road, Shepperton, TW17 8SN (permit ref EPR/BB3105HY).

During the course of works visible fragments of asbestos were handpicked by UKATA trained personnel, double bagged and goose necked tied along with contaminated masks and coveralls. These were removed from site on 10th May 2017 by Luton Environmental Ltd (carrier license CBDU43110) to Asbestos Waste Solution LLP's facility at 27a Oliver Close, West Thurrock, Essex, RM20 3EE (permit ref FP3694VC/A001).

Following completion of the turnover works a brightly coloured orange membrane was laid out across the area and lapped over the membrane laid during the stage 1 works. Following this the area was filled by WEL in accordance with the Environmental Permit. This is described further in the WEL Earthworks Completion Report⁴

3.3.3 Stage 3 Works – June 2017

The third stage of works was undertaken between 26th and 28th June 2017 and comprised the turnover of Made Ground beneath the footprints of several proposed buildings in the east of Phase 5A and partially within Phase 5B which were within the areas of delineated asbestos impact carried out during stage 1 of the enabling works. This area had not been previously cleared as was until recently covered by a construction access road to Phase 1 of the GPV development.

The asbestos exclusion zone was separated from the surrounding areas by heras fencing with asbestos warning signs. A decontamination unit was installed on the northern edge of the asbestos exclusion zone. The extents of the asbestos exclusion zone during Ramboll's watching briefs

⁴ Wooldridge Ecotec Ltd. (2017). Phase 5A Earthworks Completion Report ref. GPV-PH5A-FEB17

are shown in the photographic record in Appendix 3. An access route was created within the exclusion zone upon the higher previously remediated area to allow for the dust suppression bowser and dumper to access the work area without tracking over impacted soils.

Following completion of the turnover works a brightly coloured orange membrane was laid out across the area and lapped over the membrane laid during the stage 1 works. Following this the area was filled by WEL in accordance with the Environmental Permit. This is described further in the WEL Earthworks Completion Report⁴.

3.3.4 Additional Drainage Works

A further stage of works was carried out between 20th and 22nd September 2017 to excavate material below the previously installed orange demarcation layer for the extension of the drainage clean corridor and the installation of an “aquablock” attenuation system. Approximately 600 m³ of suspected asbestos impacted Made Ground was excavated under controlled conditions (see below) and stockpiled for chemical analysis. Following this the demarcation layer was reinstalled and “aquablock” fitted and ground to be filled with chemical suitable fill under the environmental permit for the site. These works were not witnessed by Ramboll.

A series of progress photographs supplied by WEL are contained in Appendix 3.

3.3.5 Licensing Status

During the course of the three stages of work Ramboll visually inspected the Made Ground assessing the soils for the presence of ACMs. In selected locations where ACMs were identified laboratory analysis and identification was undertaken. The majority of asbestos identified in soils (both visually and through laboratory analysis) comprised cement bound asbestos with very rare occurrences of higher risks ACMs such as lagging and AIB. On the basis of the frequency of encountering these materials the categorisation of the works as non-licensed was considered to remain valid and works progressed as such.

3.3.6 Implementation of Asbestos Control Measures

The following asbestos management control measures were implemented throughout the three stages of works:

- Dust suppression measures were employed throughout the works to prevent the liberation of airborne fibres;
- Oversized materials including concrete, metal and general waste was removed from the asbestos exclusion zone with all adhered soil removed as reasonably practicable;
- All personal within the asbestos exclusion zone adhered to the PPE/RPE requirements and were briefed on the AMP prior to entering;
- Background air monitoring was undertaken which is discussed in further detail in Section 3.3.7; and
- Washing down of plant exiting the asbestos exclusion zone.

3.3.7 Background Reassurance Monitoring

Lucion conducted reassurance monitoring at the site during the various stages of works as follows:

- Stage 1 - 24th August to 29th September 2016.
- Stage 2 - 10th April to 3rd May 2017.
- Stage 3 - 26th to 28th June 2017.
- Drainage Works - 20th to 22nd September 2017.

Ramboll liaised with Lucion during these stages of work to determine suitable locations for the boundary monitors dependant on where the turning works were taking place and taking wind direction into account. Personal monitors were rotated amongst the operatives within the asbestos exclusion zone. The reassurance monitoring confirmed no identification of fibres above background levels throughout the works. The results of the reassurance monitoring are contained within Appendix 5.

3.4 Clean service corridors

As part of the stage 1 enabling works a clean corridor was required to be completed along the main access road within Phase 5A to ensure that future construction and maintenance works do not come into contact with asbestos impact soils. The corridor was excavated to a width of 2 m in the centre of the road and to a depth of 1.5 m below the sewer invert level. Following excavation a brightly coloured demarcation layer was laid to the base and sides of excavation and was filled with material in accordance with the Environmental Permit for the site⁴. A selection of photographs showing the construction of the service corridor is included in Appendix 3.

3.5 Clean cover system

Following the turnover of Made Ground soils and placement of the brightly coloured demarcation layer filling activities which effectively provide the clean cap were undertaken in Phase 5A by WEL which includes the placement of a minimum of 1 m of chemically suitable materials in accordance with the Environmental Permit for the site. At the time of writing Phase 5A had been filled with Phase 5B due to be completed later this year. Across both phases it is estimated that ~36,300 m³ of inert soils will be used to raise the site. The filling operation is discussed in detail within the WEL Earthworks Completion Report⁴

3.6 Unforeseen contamination protocol

Aside from the area of deep Made Ground identified during Stage 1 of the enabling works ad described in Section 3.3.1 no unforeseen contamination was identified during the course of works.

4. CONCLUSION

This Verification Report has been prepared for St Edward Homes Ltd to demonstrate how ground contamination hazards and risks associated with asbestos impacted soils have been managed throughout the enabling works within Phase 5 of the Green Park Village development. Risks associated with controlled waters and ground gases have been assessed under separate covers⁵⁶⁷.

The Phase 5A Ground Investigation Findings and Remedial Options Technical Note¹ outlined mitigation measures required to deliver a suitable for use site. In relation to the enabling works this included the following:

- Further delineation of the asbestos impacted soils within Phase 5A;
- Waste management procedures for any unsuitable materials arising during enabling works;
- Creation of a clean service corridors for deep sewers within the Phase;
- Provision of a clean cover system through general filling under the Environmental Permit within the Phase; and
- Adoption of an unforeseen contamination protocol.

Operational procedures required during the works were outlined within an Asbestos Management Plan² for the site to ensure the enabling works could progress in an appropriate safe manner. These measures comprised:

- A watching brief from a competent trained asbestos operative (Ramboll);
- Reassurance air monitoring (Lucion);
- Controlled earthworks and site quarantine;
- Dust suppression measures;
- Inspection of materials removed from the asbestos exclusion zone (e.g. oversized concrete and metal); and
- Adherence to the required PPE/RPE for all operatives within the asbestos exclusion zone.

This report has provided the evidence of the implementation of the aforementioned mitigation and control measures during the enabling works within Phase 5A. The Asbestos Management Plan categorised works as a non-licensed activity. The watching briefs undertaken by Ramboll identified no plausible reason to change this categorisation on the following basis:

- Higher risk asbestos containing materials including asbestos insulation board or lagging were encountered on very rare occasions throughout the works;
- The works were not considered to be leading to the degradation of the cement bound asbestos present within the Made Ground soils; and
- There were no failures of permissible limits during the personal and background reassurance monitoring.

The placement of a brightly coloured demarcation and land raising in accordance with the Environmental Permit has encapsulated the asbestos impacted soils resulting in negligible residual risks and no further works are required within Phase 5A in this regard.



⁵ Ramboll (2017). Ground Contamination Interpretative Report – Phase 5 ref. 1620000492/RPT/014.

⁶ Ramboll (2017). Ground Gas Risk Assessment – Phase 3 to 5 ref. 1620000492/RPT/016.

⁷ Ramboll (2017). Foundation Works Risk Assessment ref. 1620000492/RPT/006.

Note that should future works within Phase 5A penetrate the land raise and demarcation layer and have the potential to disturb ACM impacted soils then the measures outlined within the Asbestos Management Plan will be required to be adhered to.

APPENDIX 1 – FIGURES/DRAWINGS

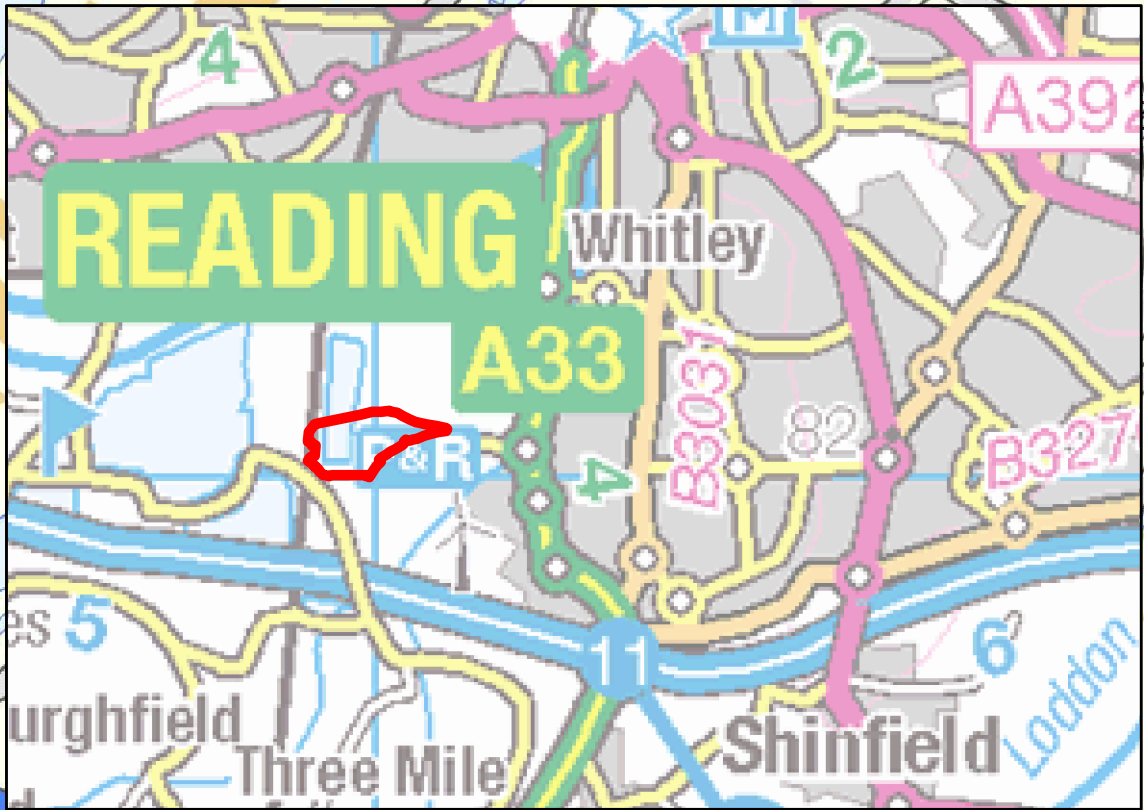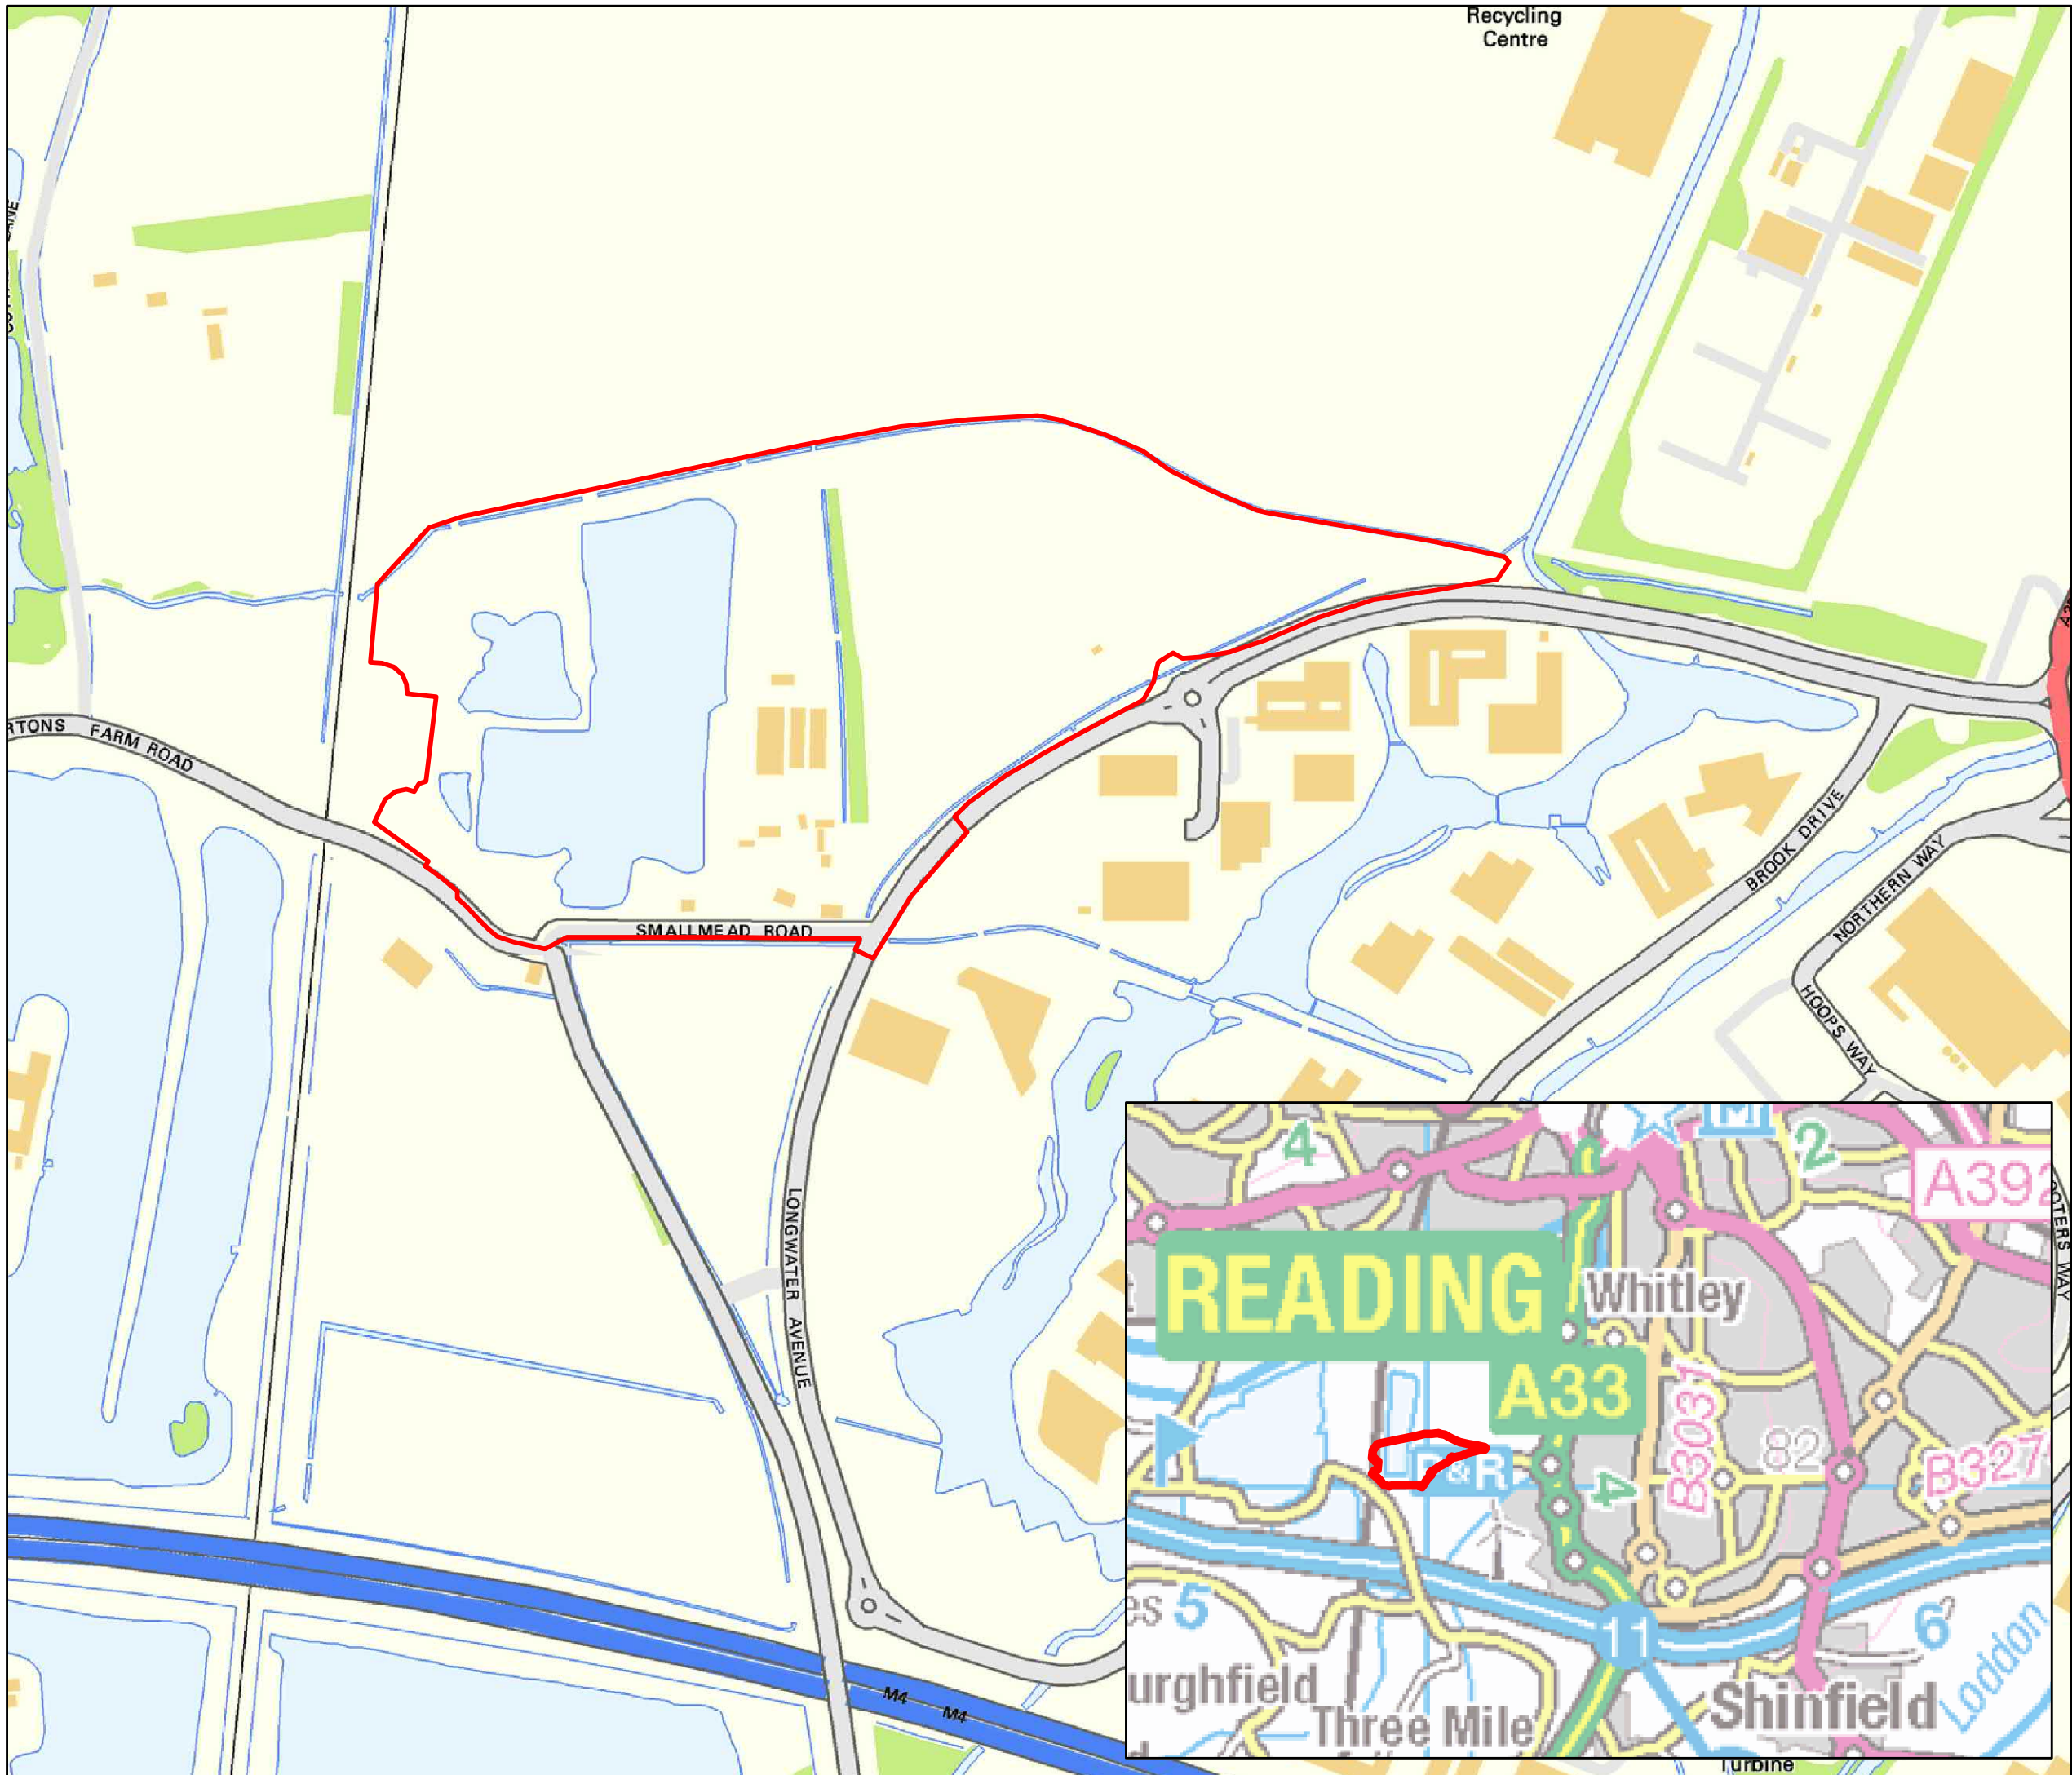

Site Boundary

1:5,000

1:50,000



Drawn at A3

Reproduced from Ordnance Survey
digital map data © Crown copyright
2015 All rights reserved.
Licence number 100040631

Client

St Edward Homes Ltd

Project Title

Green Park Village

Project Number

1620000492

Figure Title

Site Location Plan

RAMBOLL

Tel: 023 8081 7500
Fax: 023 8081 7600

southampton@ramboll.co.uk
www.ramboll.co.uk

Date

March 2016

Prepared By


BH

Figure No.

Figure 1

Revision

01

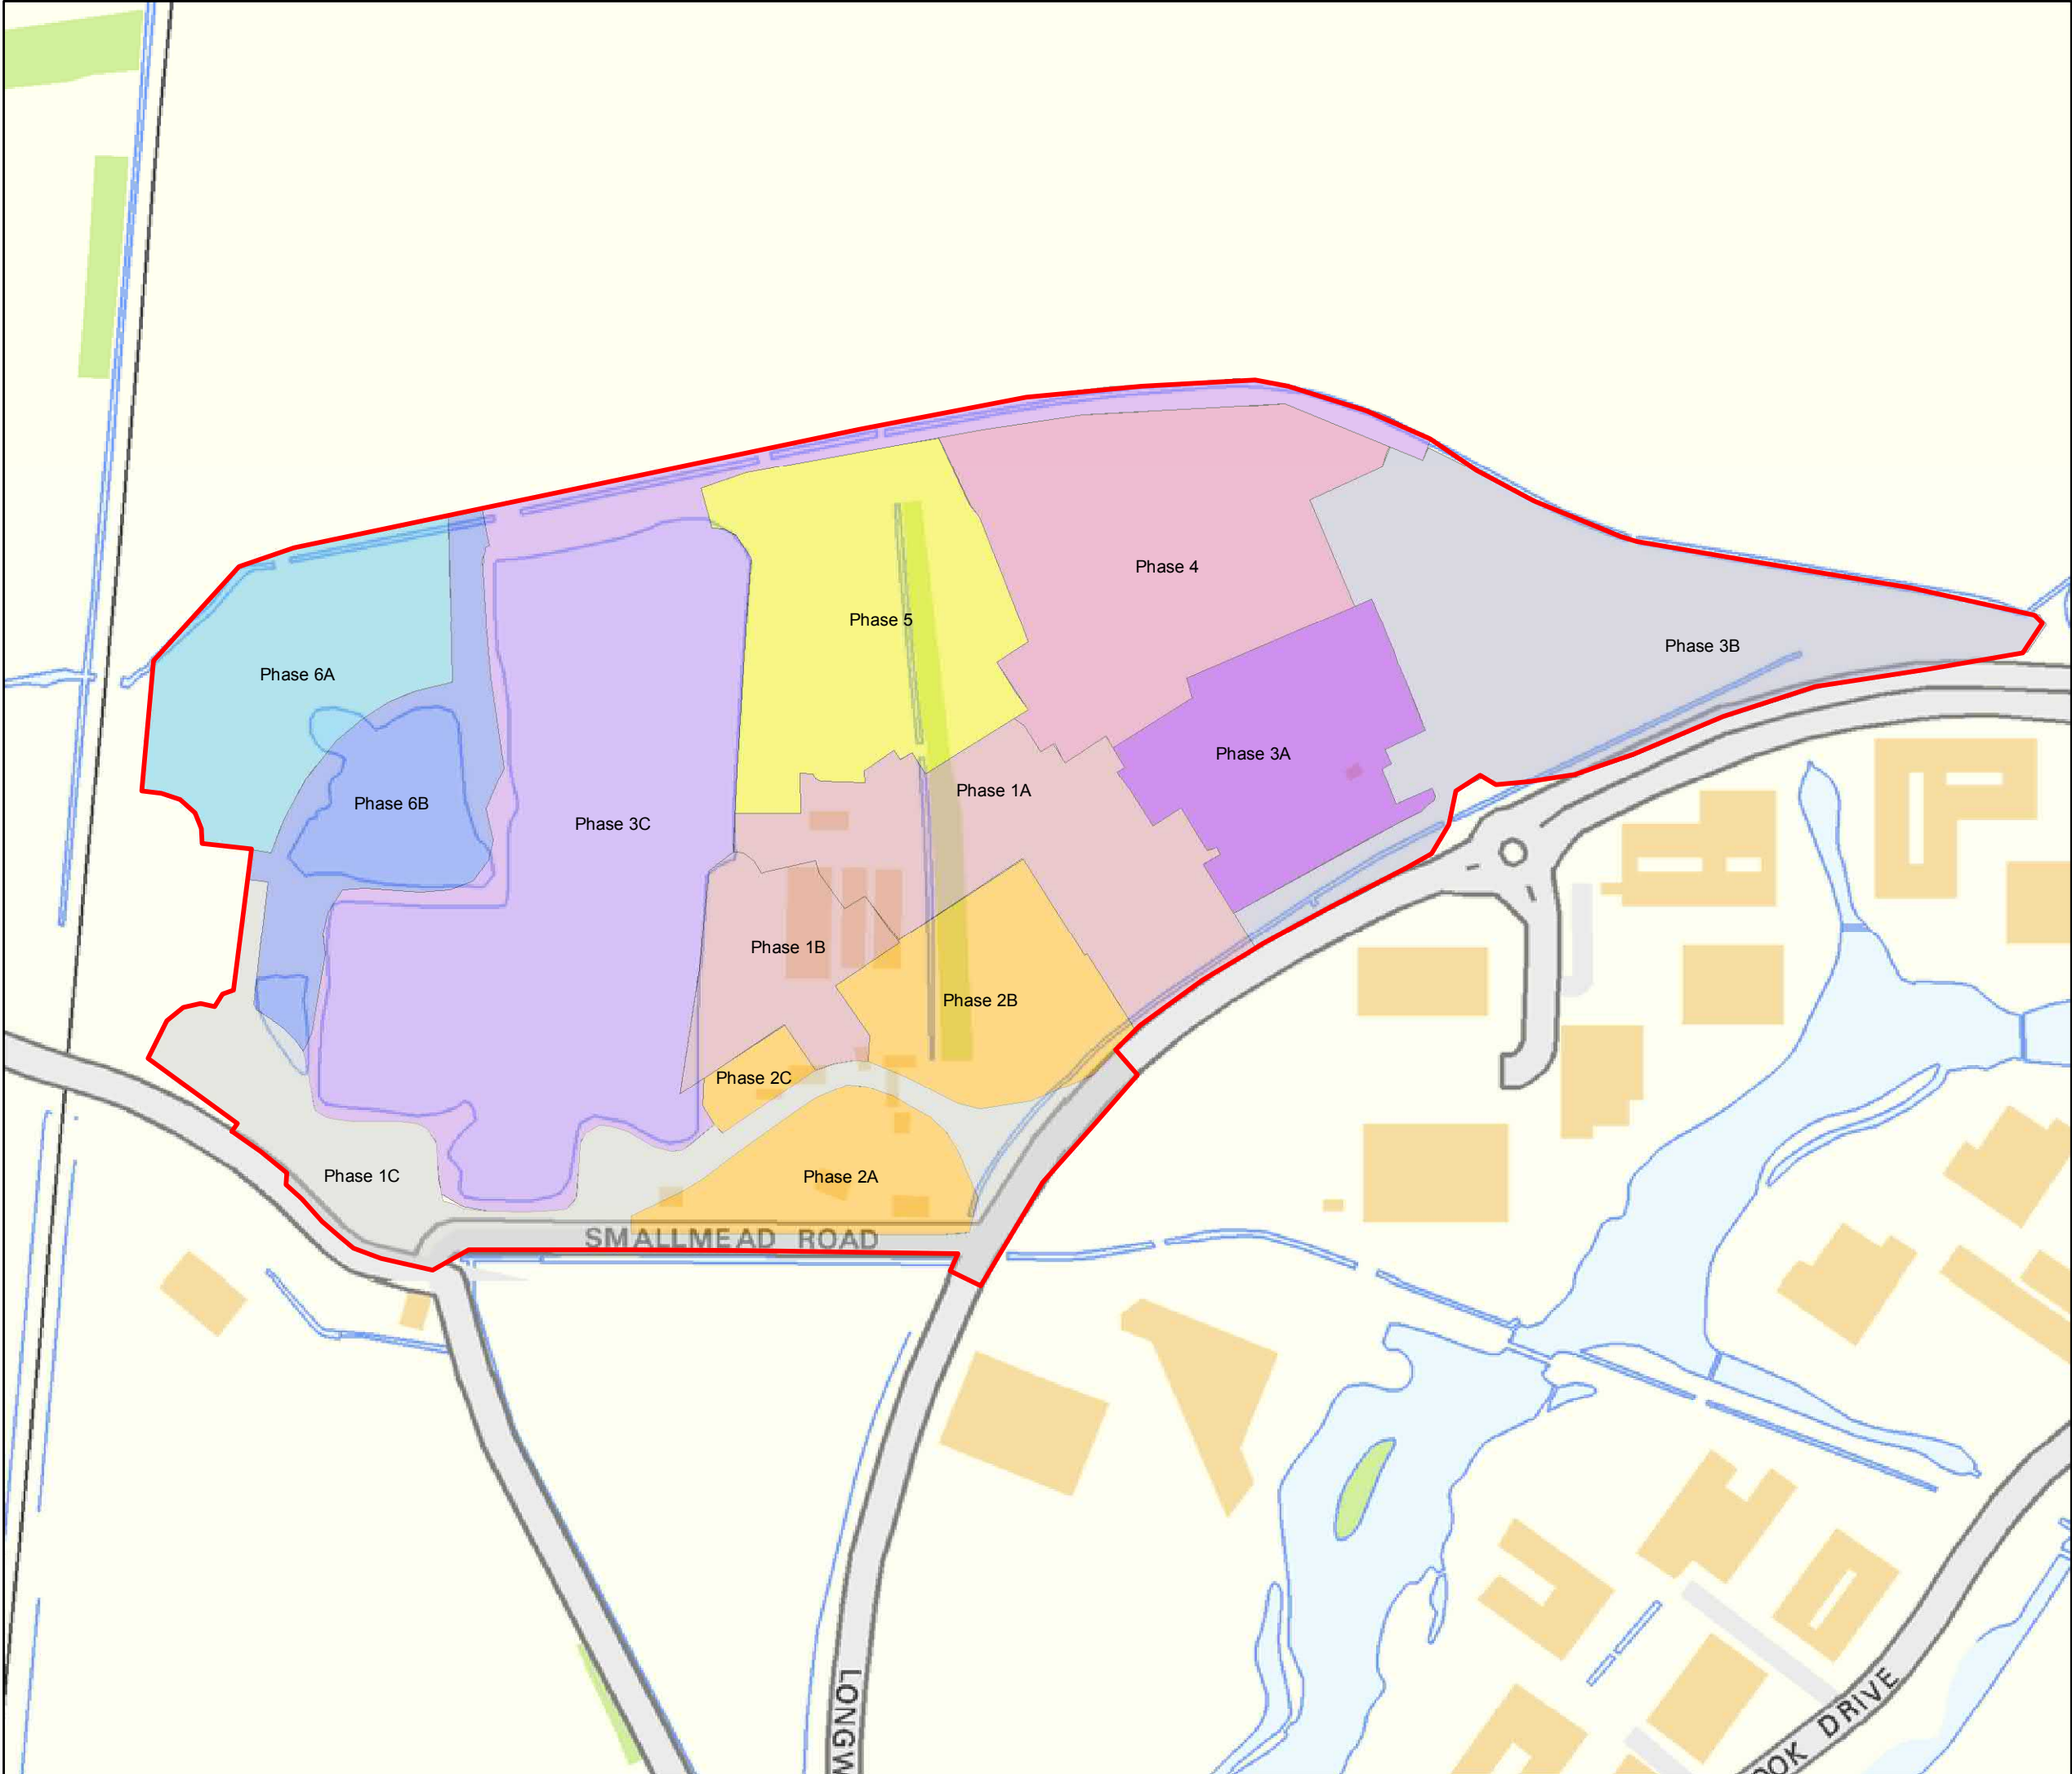

- Site Boundary
- Phase 1A

Phase 1B

Phase 1C

Phase 2A

Phase 2B

Phase 2C

Phase 3A

Phase 3B

Phase 3C

Phase 4

Phase 5

Phase 6A

Phase 6B



1:3,000
Drawn at A3
Reproduced from Ordnance Survey
digital map data © Crown copyright
2015 All rights reserved.
Licence number 100040631

Client	
S Edward Homes Ltd	
Project Title	
Green Park Village	
Project Number	
1620000492	
Figure Title	
Phasing Plan	
RAMBOLL Tel: 023 8081 7500 Fax: 023 8081 7600 southampton@ramboll.co.uk www.ramboll.co.uk	
Date	July 2016
Prepared By	BH
Figure No.	Figure 2
Revision	02



Key


Excavation Extent

Deep Made Ground Area


Known Area of Asbestos Impact

- Phase**
- Phase 1A
 - Phase 1B
 - Phase 1C
 - Phase 2A
 - Phase 2B
 - Phase 2C
 - Phase 3
 - Phase 4
 - Phase 5
 - Phase 6
 - Phase 7

Scale: 1:846
Drawn at A3
Baseplan adopted from
BroadwayMalyanSite Layout
Drawing PL-P1-002 rev P



Client	
St Edward Homes Ltd	
Project Title	
Green Park Village	
Project Number	
1620000492	
Figure Title	
Phase 5 - Excavation Extent	
RAMBOLL Tel: 023 8081 7500 Fax: 023 8081 7600 southampton@ramboll.co.uk www.ramboll.co.uk www.ramboll.co.uk southampton@ramboll.co.uk www.ramboll.co.uk	
Date	10/03/2017
Prepared By	JP
Figure No.	Figure 3.1
Revision	01

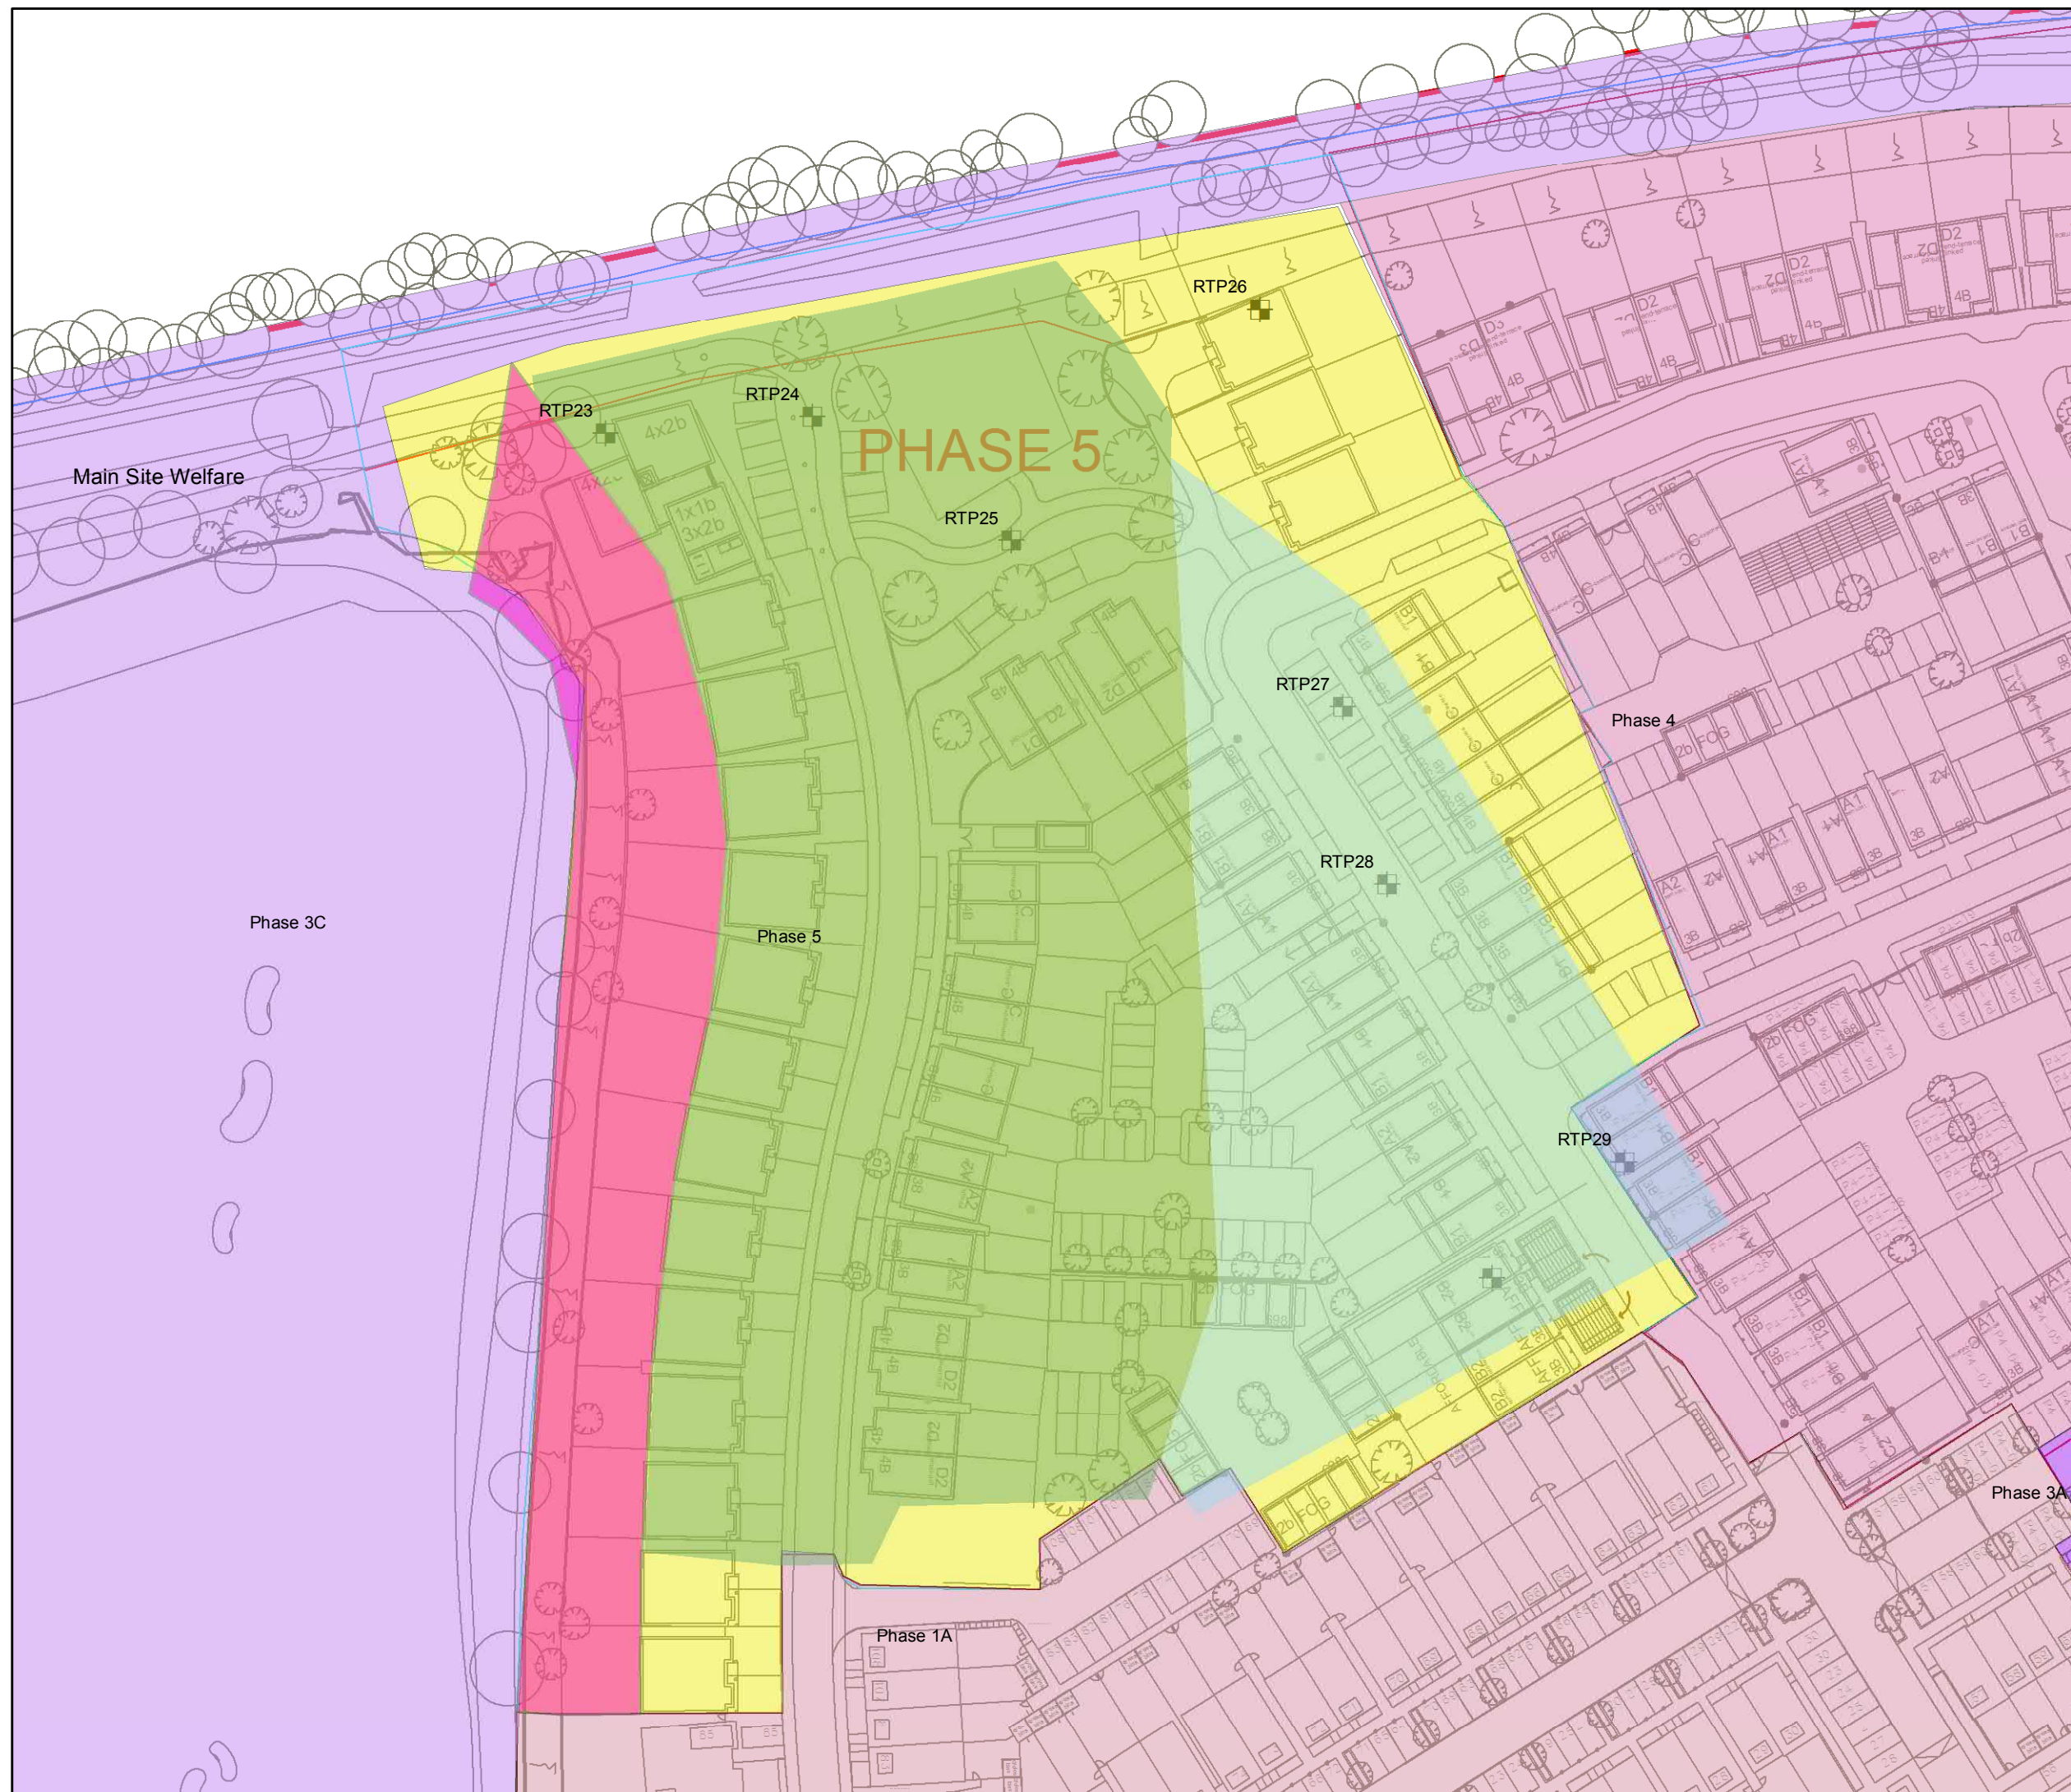

Key

Area

- Stage 1 - August/September 2016
- Stage 2 - April /May 2017
- Stage 3 - June 2017
- Phase 1A
- Phase 1B
- Phase 1C
- Phase 2A
- Phase 2B
- Phase 2C
- Phase 3A
- Phase 3B
- Phase 3C
- Phase 4
- Phase 5
- Phase 6A
- Phase 6B


As Built Additional Delineation Trial Pits

Note - Turnover and membrane placement area referenced from Wooldridge Ecotec Drawing Phase5A Area June 2017 ref 103C

Scale: 1:750

Drawn at A3

Baseplan adopted from BroadwayMalyanSite Layout Drawing PL-P1-002 rev P



Client

St Edward Homes Ltd

Project Title

Green Park Village

Project Number

1620000492

Figure Title

Phase 5A - Earthworks Plan (Membrane Location)



www.ramboll.co.uk

Tel: 023 8081 7500
Fax: 023 8081 7600

southampton@ramboll.co.uk
www.ramboll.co.uk

Date

17/07/17

Prepared By

TS

Figure No.

Figure 4

Revision

-

APPENDIX 2 – ANALYTICAL RESULTS

**Tom Smith**

Ramboll Environ UK Limited
240
Blackfriars Road
London
SE1 8NW

i2 Analytical Ltd.
7 Woodshots Meadow,
Croxley Green
Business Park,
Watford,
Herts,
WD18 8YS

e: thomas.smith@ramboll.co.uk

t: 01923 225404
f: 01923 237404
e: reception@i2analytical.com

Analytical Report Number : 16-26903

Project / Site name:	Green Park Village	Samples received on:	26/08/2016
Your job number:	1620000492	Samples instructed on:	02/09/2016
Your order number:	1620009315	Analysis completed by:	08/09/2016
Report Issue Number:	1	Report issued on:	08/09/2016
Samples Analysed:	14 soil samples		

Signed:

Rexona Rahman
Reporting Manager
For & on behalf of i2 Analytical Ltd.

Signed:

Dr Irma Doyle
Senior Account Manager
For & on behalf of i2 Analytical Ltd.

Standard Geotechnical, Asbestos and Chemical Testing Laboratory located at: ul. Pionierów 39, 41 -711 Ruda Śląska, Poland.

Accredited tests are defined within the report, opinions and interpretations expressed herein are outside the scope of accreditation.

Standard sample disposal times, unless otherwise agreed with the laboratory, are :	soils	- 4 weeks from reporting
	leachates	- 2 weeks from reporting
	waters	- 2 weeks from reporting
	asbestos	- 6 months from reporting

Excel copies of reports are only valid when accompanied by this PDF certificate.

Analytical Report Number: 16-26903
Project / Site name: Green Park Village
Your Order No: 1620009315

Lab Sample Number				624752	624753	624754	624755	624756
Sample Reference				RTP23	RTP24	RTP24	RTP25	RTP25
Sample Number				None Supplied	None Supplied	None Supplied	None Supplied	None Supplied
Depth (m)				0.30	0.15	0.40	0.10	0.30
Date Sampled				26/08/2016	26/08/2016	24/08/2016	24/08/2016	25/08/2016
Time Taken				None Supplied	None Supplied	None Supplied	None Supplied	None Supplied
Analytical Parameter (Soil Analysis)	Units	Limit of detection	Accreditation Status					
Stone Content	%	0.1	NONE	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
Moisture Content	%	N/A	NONE	11	14	17	6.6	11
Total mass of sample received	kg	0.001	NONE	1.2	1.2	1.0	1.3	1.4

Asbestos in Soil Screen / Identification Name	Type	N/A	ISO 17025	-	-	-	-	-
Asbestos in Soil	Type	N/A	ISO 17025	Not-detected	Not-detected	Not-detected	Not-detected	Not-detected
Asbestos Quantification (Stage 2)	%	0.001	ISO 17025	-	-	-	-	-
Asbestos Quantification Total	%	0.001	ISO 17025	-	-	-	-	-

General Inorganics

pH - Automated	pH Units	N/A	MCERTS	8.3	8.2	7.9	8.6	7.9
Total Cyanide	mg/kg	1	MCERTS	< 1	< 1	< 1	< 1	< 1
Water Soluble SO ₄ 16hr extraction (2:1 Leachate Equivalent)	g/l	0.00125	MCERTS	0.11	0.29	0.094	0.37	0.21
Fraction Organic Carbon (FOC)	N/A	0.001	NONE	0.0070	0.0091	0.020	0.0053	0.0092

Total Phenols

Total Phenols (monohydric)	mg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
----------------------------	-------	---	--------	-------	-------	-------	-------	-------

Speciated PAHs

Naphthalene	mg/kg	0.05	MCERTS	< 0.05	< 0.05	< 0.05	< 0.05	< 0.05
Acenaphthylene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	< 0.10
Acenaphthene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	< 0.10
Fluorene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	< 0.10
Phenanthrene	mg/kg	0.1	MCERTS	0.36	< 0.10	< 0.10	< 0.10	< 0.10
Anthracene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	< 0.10
Fluoranthene	mg/kg	0.1	MCERTS	0.81	< 0.10	< 0.10	< 0.10	< 0.10
Pyrene	mg/kg	0.1	MCERTS	0.68	< 0.10	< 0.10	< 0.10	< 0.10
Benzo(a)anthracene	mg/kg	0.1	MCERTS	0.53	< 0.10	< 0.10	< 0.10	< 0.10
Chrysene	mg/kg	0.05	MCERTS	0.41	< 0.05	< 0.05	< 0.05	< 0.05
Benzo(b)fluoranthene	mg/kg	0.1	MCERTS	0.46	< 0.10	< 0.10	< 0.10	< 0.10
Benzo(k)fluoranthene	mg/kg	0.1	MCERTS	0.33	< 0.10	< 0.10	< 0.10	< 0.10
Benzo(a)pyrene	mg/kg	0.1	MCERTS	0.49	< 0.10	< 0.10	< 0.10	< 0.10
Indeno(1,2,3-cd)pyrene	mg/kg	0.1	MCERTS	0.34	< 0.10	< 0.10	< 0.10	< 0.10
Dibenz(a,h)anthracene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	< 0.10
Benzo(ghi)perylene	mg/kg	0.05	MCERTS	0.47	< 0.05	< 0.05	< 0.05	< 0.05

Total PAH

Speciated Total EPA-16 PAHs	mg/kg	1.6	MCERTS	4.88	< 1.60	< 1.60	< 1.60	< 1.60
-----------------------------	-------	-----	--------	------	--------	--------	--------	--------

Analytical Report Number: 16-26903
Project / Site name: Green Park Village
Your Order No: 1620009315

Lab Sample Number				624752	624753	624754	624755	624756
Sample Reference				RTP23	RTP24	RTP24	RTP25	RTP25
Sample Number				None Supplied	None Supplied	None Supplied	None Supplied	None Supplied
Depth (m)				0.30	0.15	0.40	0.10	0.30
Date Sampled				26/08/2016	26/08/2016	24/08/2016	24/08/2016	25/08/2016
Time Taken				None Supplied	None Supplied	None Supplied	None Supplied	None Supplied
Analytical Parameter (Soil Analysis)	Units	Limit of detection	Accreditation Status					

Heavy Metals / Metalloids

Arsenic (aqua regia extractable)	mg/kg	1	MCERTS	7.7	8.9	14	9.9	10
Beryllium (aqua regia extractable)	mg/kg	0.06	MCERTS	0.78	0.74	1.2	0.61	0.51
Boron (water soluble)	mg/kg	0.2	MCERTS	0.8	1.7	3.4	0.6	1.0
Cadmium (aqua regia extractable)	mg/kg	0.2	MCERTS	< 0.2	< 0.2	< 0.2	< 0.2	< 0.2
Chromium (hexavalent)	mg/kg	4	MCERTS	< 4.0	< 4.0	< 4.0	< 4.0	< 4.0
Chromium (aqua regia extractable)	mg/kg	1	MCERTS	22	30	59	28	21
Copper (aqua regia extractable)	mg/kg	1	MCERTS	17	15	24	17	9.7
Lead (aqua regia extractable)	mg/kg	1	MCERTS	32	28	56	30	19
Mercury (aqua regia extractable)	mg/kg	0.3	MCERTS	< 0.3	< 0.3	0.5	< 0.3	< 0.3
Nickel (aqua regia extractable)	mg/kg	1	MCERTS	18	16	25	15	13
Selenium (aqua regia extractable)	mg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Vanadium (aqua regia extractable)	mg/kg	1	MCERTS	26	33	38	31	29
Zinc (aqua regia extractable)	mg/kg	1	MCERTS	66	62	130	63	55

Monoaromatics

Benzene	µg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Toluene	µg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Ethylbenzene	µg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
p & m-xylene	µg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
o-xylene	µg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
MTBE (Methyl Tertiary Butyl Ether)	µg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0

Petroleum Hydrocarbons

TPH-CWG - Aliphatic >EC5 - EC6	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
TPH-CWG - Aliphatic >EC6 - EC8	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
TPH-CWG - Aliphatic >EC8 - EC10	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
TPH-CWG - Aliphatic >EC10 - EC12	mg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
TPH-CWG - Aliphatic >EC12 - EC16	mg/kg	2	MCERTS	< 2.0	< 2.0	< 2.0	< 2.0	< 2.0
TPH-CWG - Aliphatic >EC16 - EC21	mg/kg	8	MCERTS	< 8.0	< 8.0	< 8.0	< 8.0	< 8.0
TPH-CWG - Aliphatic >EC21 - EC35	mg/kg	8	MCERTS	10	< 8.0	< 8.0	16	22
TPH-CWG - Aliphatic (EC5 - EC35)	mg/kg	10	MCERTS	11	< 10	< 10	23	28

TPH-CWG - Aromatic >EC5 - EC7	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
TPH-CWG - Aromatic >EC7 - EC8	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
TPH-CWG - Aromatic >EC8 - EC10	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
TPH-CWG - Aromatic >EC10 - EC12	mg/kg	1	MCERTS	< 1.0	1.5	< 1.0	< 1.0	< 1.0
TPH-CWG - Aromatic >EC12 - EC16	mg/kg	2	MCERTS	< 2.0	2.4	< 2.0	< 2.0	< 2.0
TPH-CWG - Aromatic >EC16 - EC21	mg/kg	10	MCERTS	11	< 10	< 10	< 10	< 10
TPH-CWG - Aromatic >EC21 - EC35	mg/kg	10	MCERTS	51	20	< 10	< 10	< 10
TPH-CWG - Aromatic (EC5 - EC35)	mg/kg	10	MCERTS	63	29	12	< 10	< 10

Analytical Report Number: 16-26903
Project / Site name: Green Park Village
Your Order No: 1620009315

Lab Sample Number				624757	624758	624759	624760	624761
Sample Reference				RTP26	RTP26	RTP27	RTP27	RTP28
Sample Number				None Supplied	None Supplied	None Supplied	None Supplied	None Supplied
Depth (m)				0.10	0.25	0.15	1.10	0.10
Date Sampled				25/08/2016	25/08/2016	25/08/2016	25/08/2016	25/08/2016
Time Taken				None Supplied	None Supplied	None Supplied	None Supplied	None Supplied
Analytical Parameter (Soil Analysis)	Units	Limit of detection	Accreditation Status					
Stone Content	%	0.1	NONE	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
Moisture Content	%	N/A	NONE	6.2	21	10	9.6	4.9
Total mass of sample received	kg	0.001	NONE	1.3	1.0	1.1	1.3	1.3

Asbestos in Soil Screen / Identification Name	Type	N/A	ISO 17025	Chrysotile	-	-	-	-
Asbestos in Soil	Type	N/A	ISO 17025	Detected	Not-detected	Not-detected	Not-detected	Not-detected
Asbestos Quantification (Stage 2)	%	0.001	ISO 17025	< 0.001	-	-	-	-
Asbestos Quantification Total	%	0.001	ISO 17025	< 0.001	-	-	-	-

General Inorganics

pH - Automated	pH Units	N/A	MCERTS	9.0	7.9	6.9	8.1	7.9
Total Cyanide	mg/kg	1	MCERTS	< 1	< 1	3	< 1	< 1
Water Soluble SO ₄ 16hr extraction (2:1 Leachate Equivalent)	g/l	0.00125	MCERTS	1.3	0.025	0.031	0.0097	0.014
Fraction Organic Carbon (FOC)	N/A	0.001	NONE	0.019	0.026	0.013	0.0018	0.0013

Total Phenols

Total Phenols (monohydric)	mg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
----------------------------	-------	---	--------	-------	-------	-------	-------	-------

Speciated PAHs

Naphthalene	mg/kg	0.05	MCERTS	< 0.05	< 0.05	< 0.05	< 0.05	< 0.05
Acenaphthylene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	< 0.10
Acenaphthene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	< 0.10
Fluorene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	< 0.10
Phenanthrene	mg/kg	0.1	MCERTS	0.35	< 0.10	< 0.10	< 0.10	< 0.10
Anthracene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	< 0.10
Fluoranthene	mg/kg	0.1	MCERTS	1.1	< 0.10	< 0.10	< 0.10	< 0.10
Pyrene	mg/kg	0.1	MCERTS	0.94	< 0.10	< 0.10	< 0.10	< 0.10
Benzo(a)anthracene	mg/kg	0.1	MCERTS	0.62	< 0.10	< 0.10	< 0.10	< 0.10
Chrysene	mg/kg	0.05	MCERTS	0.67	< 0.05	< 0.05	< 0.05	< 0.05
Benzo(b)fluoranthene	mg/kg	0.1	MCERTS	1.0	< 0.10	< 0.10	< 0.10	< 0.10
Benzo(k)fluoranthene	mg/kg	0.1	MCERTS	0.40	< 0.10	< 0.10	< 0.10	< 0.10
Benzo(a)pyrene	mg/kg	0.1	MCERTS	0.84	< 0.10	< 0.10	< 0.10	< 0.10
Indeno(1,2,3-cd)pyrene	mg/kg	0.1	MCERTS	0.62	< 0.10	< 0.10	< 0.10	< 0.10
Dibenz(a,h)anthracene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	< 0.10
Benzo(ghi)perylene	mg/kg	0.05	MCERTS	0.77	< 0.05	< 0.05	< 0.05	< 0.05

Total PAH

Speciated Total EPA-16 PAHs	mg/kg	1.6	MCERTS	7.34	< 1.60	< 1.60	< 1.60	< 1.60
-----------------------------	-------	-----	--------	------	--------	--------	--------	--------

Analytical Report Number: 16-26903
Project / Site name: Green Park Village
Your Order No: 1620009315

Lab Sample Number				624757	624758	624759	624760	624761
Sample Reference				RTP26	RTP26	RTP27	RTP27	RTP28
Sample Number				None Supplied	None Supplied	None Supplied	None Supplied	None Supplied
Depth (m)				0.10	0.25	0.15	1.10	0.10
Date Sampled				25/08/2016	25/08/2016	25/08/2016	25/08/2016	25/08/2016
Time Taken				None Supplied	None Supplied	None Supplied	None Supplied	None Supplied
Analytical Parameter (Soil Analysis)	Units	Limit of detection	Accreditation Status					
Heavy Metals / Metalloids								
Arsenic (aqua regia extractable)	mg/kg	1	MCERTS	8.4	11	10	2.6	4.4
Beryllium (aqua regia extractable)	mg/kg	0.06	MCERTS	0.81	1.3	1.1	0.21	0.27
Boron (water soluble)	mg/kg	0.2	MCERTS	2.6	2.5	1.6	0.6	0.7
Cadmium (aqua regia extractable)	mg/kg	0.2	MCERTS	0.2	0.2	< 0.2	< 0.2	< 0.2
Chromium (hexavalent)	mg/kg	4	MCERTS	< 4.0	< 4.0	< 4.0	< 4.0	< 4.0
Chromium (aqua regia extractable)	mg/kg	1	MCERTS	31	74	70	17	18
Copper (aqua regia extractable)	mg/kg	1	MCERTS	36	41	39	15	11
Lead (aqua regia extractable)	mg/kg	1	MCERTS	71	110	91	5.9	10
Mercury (aqua regia extractable)	mg/kg	0.3	MCERTS	< 0.3	< 0.3	< 0.3	< 0.3	< 0.3
Nickel (aqua regia extractable)	mg/kg	1	MCERTS	18	27	20	13	12
Selenium (aqua regia extractable)	mg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Vanadium (aqua regia extractable)	mg/kg	1	MCERTS	34	39	40	8.6	13
Zinc (aqua regia extractable)	mg/kg	1	MCERTS	130	190	150	14	22

Monoaromatics

Benzene	µg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Toluene	µg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Ethylbenzene	µg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
p & m-xylene	µg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
o-xylene	µg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
MTBE (Methyl Tertiary Butyl Ether)	µg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0

Petroleum Hydrocarbons

TPH-CWG - Aliphatic >EC5 - EC6	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
TPH-CWG - Aliphatic >EC6 - EC8	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
TPH-CWG - Aliphatic >EC8 - EC10	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
TPH-CWG - Aliphatic >EC10 - EC12	mg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
TPH-CWG - Aliphatic >EC12 - EC16	mg/kg	2	MCERTS	< 2.0	< 2.0	< 2.0	< 2.0	< 2.0
TPH-CWG - Aliphatic >EC16 - EC21	mg/kg	8	MCERTS	< 8.0	< 8.0	< 8.0	< 8.0	< 8.0
TPH-CWG - Aliphatic >EC21 - EC35	mg/kg	8	MCERTS	16	9.4	< 8.0	< 8.0	< 8.0
TPH-CWG - Aliphatic (EC5 - EC35)	mg/kg	10	MCERTS	20	< 10	< 10	< 10	< 10

TPH-CWG - Aromatic >EC5 - EC7	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
TPH-CWG - Aromatic >EC7 - EC8	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
TPH-CWG - Aromatic >EC8 - EC10	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
TPH-CWG - Aromatic >EC10 - EC12	mg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
TPH-CWG - Aromatic >EC12 - EC16	mg/kg	2	MCERTS	< 2.0	< 2.0	< 2.0	< 2.0	< 2.0
TPH-CWG - Aromatic >EC16 - EC21	mg/kg	10	MCERTS	< 10	< 10	< 10	< 10	< 10
TPH-CWG - Aromatic >EC21 - EC35	mg/kg	10	MCERTS	87	10	< 10	< 10	< 10
TPH-CWG - Aromatic (EC5 - EC35)	mg/kg	10	MCERTS	95	14	< 10	< 10	< 10

Analytical Report Number: 16-26903
Project / Site name: Green Park Village
Your Order No: 1620009315

Lab Sample Number				624762	624763	624764	624765	
Sample Reference				RTP28	RTP29	RTP30	RTP30	
Sample Number				None Supplied	None Supplied	None Supplied	None Supplied	
Depth (m)				0.80	0.20	0.15	0.50	
Date Sampled				25/08/2016	26/08/2016	26/08/2016	26/08/2016	
Time Taken				None Supplied	None Supplied	None Supplied	None Supplied	
Analytical Parameter (Soil Analysis)	Units	Limit of detection	Accreditation Status					
Stone Content	%	0.1	NONE	< 0.1	< 0.1	< 0.1	< 0.1	
Moisture Content	%	N/A	NONE	13	21	10	25	
Total mass of sample received	kg	0.001	NONE	1.1	1.1	0.96	0.95	

Asbestos in Soil Screen / Identification Name	Type	N/A	ISO 17025	-	-	-	-	
Asbestos in Soil	Type	N/A	ISO 17025	Not-detected	Not-detected	Not-detected	Not-detected	
Asbestos Quantification (Stage 2)	%	0.001	ISO 17025	-	-	-	-	
Asbestos Quantification Total	%	0.001	ISO 17025	-	-	-	-	

General Inorganics

pH - Automated	pH Units	N/A	MCERTS	7.3	7.6	7.6	6.4	
Total Cyanide	mg/kg	1	MCERTS	< 1	1	< 1	< 1	
Water Soluble SO ₄ 16hr extraction (2:1 Leachate Equivalent)	g/l	0.00125	MCERTS	0.069	0.096	0.062	0.027	
Fraction Organic Carbon (FOC)	N/A	0.001	NONE	0.017	0.022	0.019	0.028	

Total Phenols

Total Phenols (monohydric)	mg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	
----------------------------	-------	---	--------	-------	-------	-------	-------	--

Speciated PAHs

Naphthalene	mg/kg	0.05	MCERTS	< 0.05	< 0.05	< 0.05	< 0.05	
Acenaphthylene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	
Acenaphthene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	
Fluorene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	
Phenanthrene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	
Anthracene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	
Fluoranthene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	
Pyrene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	
Benzo(a)anthracene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	
Chrysene	mg/kg	0.05	MCERTS	< 0.05	< 0.05	< 0.05	< 0.05	
Benzo(b)fluoranthene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	
Benzo(k)fluoranthene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	
Benzo(a)pyrene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	
Indeno(1,2,3-cd)pyrene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	
Dibenz(a,h)anthracene	mg/kg	0.1	MCERTS	< 0.10	< 0.10	< 0.10	< 0.10	
Benzo(ghi)perylene	mg/kg	0.05	MCERTS	< 0.05	< 0.05	< 0.05	< 0.05	

Total PAH

Speciated Total EPA-16 PAHs	mg/kg	1.6	MCERTS	< 1.60	< 1.60	< 1.60	< 1.60	
-----------------------------	-------	-----	--------	--------	--------	--------	--------	--

Analytical Report Number: 16-26903
Project / Site name: Green Park Village
Your Order No: 1620009315

Lab Sample Number				624762	624763	624764	624765	
Sample Reference				RTP28	RTP29	RTP30	RTP30	
Sample Number				None Supplied	None Supplied	None Supplied	None Supplied	
Depth (m)				0.80	0.20	0.15	0.50	
Date Sampled				25/08/2016	26/08/2016	26/08/2016	26/08/2016	
Time Taken				None Supplied	None Supplied	None Supplied	None Supplied	
Analytical Parameter (Soil Analysis)	Units	Limit of detection	Accreditation Status					
Heavy Metals / Metalloids								
Arsenic (aqua regia extractable)	mg/kg	1	MCERTS	12	13	7.4	11	
Beryllium (aqua regia extractable)	mg/kg	0.06	MCERTS	1.2	1.2	1.2	1.6	
Boron (water soluble)	mg/kg	0.2	MCERTS	1.4	3.2	1.2	1.9	
Cadmium (aqua regia extractable)	mg/kg	0.2	MCERTS	< 0.2	0.3	< 0.2	< 0.2	
Chromium (hexavalent)	mg/kg	4	MCERTS	< 4.0	< 4.0	< 4.0	< 4.0	
Chromium (aqua regia extractable)	mg/kg	1	MCERTS	48	100	48	44	
Copper (aqua regia extractable)	mg/kg	1	MCERTS	24	47	33	20	
Lead (aqua regia extractable)	mg/kg	1	MCERTS	55	130	80	40	
Mercury (aqua regia extractable)	mg/kg	0.3	MCERTS	< 0.3	1.1	< 0.3	< 0.3	
Nickel (aqua regia extractable)	mg/kg	1	MCERTS	21	23	21	25	
Selenium (aqua regia extractable)	mg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	
Vanadium (aqua regia extractable)	mg/kg	1	MCERTS	52	40	48	63	
Zinc (aqua regia extractable)	mg/kg	1	MCERTS	100	230	130	100	

Monoaromatics

Benzene	ug/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	
Toluene	ug/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	
Ethylbenzene	ug/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	
p & m-xylene	ug/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	
o-xylene	ug/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	
MTBE (Methyl Tertiary Butyl Ether)	ug/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	

Petroleum Hydrocarbons

TPH-CWG - Aliphatic >EC5 - EC6	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	
TPH-CWG - Aliphatic >EC6 - EC8	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	
TPH-CWG - Aliphatic >EC8 - EC10	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	
TPH-CWG - Aliphatic >EC10 - EC12	mg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	
TPH-CWG - Aliphatic >EC12 - EC16	mg/kg	2	MCERTS	< 2.0	< 2.0	< 2.0	< 2.0	
TPH-CWG - Aliphatic >EC16 - EC21	mg/kg	8	MCERTS	< 8.0	< 8.0	< 8.0	< 8.0	
TPH-CWG - Aliphatic >EC21 - EC35	mg/kg	8	MCERTS	< 8.0	< 8.0	< 8.0	12	
TPH-CWG - Aliphatic (EC5 - EC35)	mg/kg	10	MCERTS	< 10	< 10	< 10	12	

TPH-CWG - Aromatic >EC5 - EC7	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	
TPH-CWG - Aromatic >EC7 - EC8	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	
TPH-CWG - Aromatic >EC8 - EC10	mg/kg	0.1	MCERTS	< 0.1	< 0.1	< 0.1	< 0.1	
TPH-CWG - Aromatic >EC10 - EC12	mg/kg	1	MCERTS	< 1.0	< 1.0	< 1.0	< 1.0	
TPH-CWG - Aromatic >EC12 - EC16	mg/kg	2	MCERTS	< 2.0	< 2.0	< 2.0	< 2.0	
TPH-CWG - Aromatic >EC16 - EC21	mg/kg	10	MCERTS	< 10	< 10	< 10	< 10	
TPH-CWG - Aromatic >EC21 - EC35	mg/kg	10	MCERTS	< 10	< 10	< 10	< 10	
TPH-CWG - Aromatic (EC5 - EC35)	mg/kg	10	MCERTS	< 10	< 10	< 10	< 10	



Analytical Report Number: 16-26903
Project / Site name: Green Park Village
Your Order No: 1620009315

Certificate of Analysis - Asbestos Quantification

Methods:

Qualitative Analysis

The samples were analysed qualitatively for asbestos by polarising light and dispersion staining as described by the Health and Safety Executive in HSG 248.

Quantitative Analysis

"The analysis was carried out using our documented in-house method A006 based on HSE Contract Research Report No: 83/1996: Development and Validation of an analytical method to determine the amount of asbestos in soils and loose aggregates (Davies et al, 1996) and HSG 248. Our method includes initial examination of the entire representative sample, then fractionation and detailed analysis of each fraction, with quantification by hand picking and weighing.

The limit of detection (reporting limit) of this method is 0.001 %.

The method has been validated using samples of at least 100 g, results for samples smaller than this should be interpreted with caution.

Both Qualitative and Quantitative Analyses are UKAS accredited.

Sample Number	Sample ID	Sample Depth (m)	Sample Weight (g)	Asbestos Containing Material Types Detected (ACM)	PLM Results	Asbestos by hand picking/weighing (%)	Total % Asbestos in Sample
624757	RTP26	0.10	156	Loose Fibres	Chrysotile	< 0.001	< 0.001

Opinions and interpretations expressed herein are outside the scope of UKAS accreditation

Analytical Report Number : 16-26903

Project / Site name: Green Park Village

* These descriptions are only intended to act as a cross check if sample identities are questioned. The major constituent of the sample is intended to act with respect to MCERTS validation. The laboratory is accredited for sand, clay and loam (MCERTS) soil types. Data for unaccredited types of solid should be interpreted with care.

Stone content of a sample is calculated as the % weight of the stones not passing a 10 mm sieve. Results are not corrected for stone content.

Lab Sample Number	Sample Reference	Sample Number	Depth (m)	Sample Description *
624752	RTP23	None Supplied	0.30	Brown loam and clay with gravel.
624753	RTP24	None Supplied	0.15	Brown loam and clay with gravel.
624754	RTP24	None Supplied	0.40	Brown clay and loam with gravel.
624755	RTP25	None Supplied	0.10	Brown loam and sand with gravel.
624756	RTP25	None Supplied	0.30	Brown loam and sand with gravel.
624757	RTP26	None Supplied	0.10	Brown loam and sand with gravel.
624758	RTP26	None Supplied	0.25	Brown clay and loam with gravel.
624759	RTP27	None Supplied	0.15	Brown loam and clay with gravel.
624760	RTP27	None Supplied	1.10	Brown sand with gravel.
624761	RTP28	None Supplied	0.10	Brown sand with gravel.
624762	RTP28	None Supplied	0.80	Brown loam and clay with gravel.
624763	RTP29	None Supplied	0.20	Brown loam and clay with gravel.
624764	RTP30	None Supplied	0.15	Brown loam and clay with gravel.
624765	RTP30	None Supplied	0.50	Brown loam and clay with gravel.



Analytical Report Number : 16-26903

Project / Site name: Green Park Village

Water matrix abbreviations: Surface Water (SW) Potable Water (PW) Ground Water (GW)

Analytical Test Name	Analytical Method Description	Analytical Method Reference	Method number	Wet / Dry Analysis	Accreditation Status
Asbestos identification in soil	Asbestos Identification with the use of polarised light microscopy in conjunction with disperion staining techniques.	In house method based on HSG 248	A001-PL	D	ISO 17025
Asbestos Quantification - Gravimetric	Asbestos quantification by gravimetric method - in ouse method based on references.	HSE Report No: 83/1996, HSG 248, HSG 264 & SCA Blue Book (draft).	A006-PL	D	ISO 17025
Boron, water soluble, in soil	Determination of water soluble boron in soil by hot water extract followed by ICP-OES.	In-house method based on Second Site Properties version 3	L038-PL	D	MCERTS
BTEX and MTBE in soil (Monoaromatics)	Determination of BTEX in soil by headspace GC-MS.	In-house method based on USEPA8260	L073B-PL	W	MCERTS
D.O. for Gravimetric Quant if Screen/ID positive	Dependent option for Gravimetric Quant if Screen/ID positive scheduled.	In house asbestos methods A001 & A006.	A006-PL	D	NONE
Fraction of Organic Carbon in soil	Determination of fraction of organic carbon in soil by oxidising with potassium dichromate followed by titration with iron (II) sulphate.	In-house method based on BS1377 Part 3, 1990, Chemical and Electrochemical Tests	L023-PL	D	NONE
Hexavalent chromium in soil	Determination of hexavalent chromium in soil by extraction in water then by acidification, addition of 1,5 diphenylcarbazine followed by colorimetry.	In-house method	L080-PL	W	MCERTS
Metals in soil by ICP-OES	Determination of metals in soil by aqua-regia digestion followed by ICP-OES.	In-house method based on MEWAM 2006 Methods for the Determination of Metals in Soil.	L038-PL	D	MCERTS
Moisture Content	Moisture content, determined gravimetrically.	In-house method based on BS1377 Part 3, 1990, Chemical and Electrochemical Tests	L019-UK/PL	W	NONE
Monohydric phenols in soil	Determination of phenols in soil by extraction with sodium hydroxide followed by distillation followed by colorimetry.	In-house method based on Examination of Water and Wastewater 20th Edition: Clesceri, Greenberg & Eaton (skalar)	L080-PL	W	MCERTS
pH in soil (automated)	Determination of pH in soil by addition of water followed by automated electrometric measurement.	In-house method based on BS1377 Part 3, 1990, Chemical and Electrochemical Tests	L099-PL	D	MCERTS
Speciated EPA-16 PAHs in soil	Determination of PAH compounds in soil by extraction in dichloromethane and hexane followed by GC-MS with the use of surrogate and internal standards.	In-house method based on USEPA 8270	L064-PL	D	MCERTS
Stones content of soil	Standard preparation for all samples unless otherwise detailed. Gravimetric determination of stone > 10 mm as % dry weight.	In-house method based on British Standard Methods and MCERTS requirements.	L019-UK/PL	D	NONE
Sulphate, water soluble, in soil (16hr extraction)	Determination of water soluble sulphate by ICP-OES. Results reported directly (leachate equivalent) and corrected for extraction ratio (soil equivalent).	In-house method based on BS1377 Part 3, 1990, Chemical and Electrochemical Tests, 2:1 water:soil extraction, analysis by ICP-OES.	L038-PL	D	MCERTS
Total cyanide in soil	Determination of total cyanide by distillation followed by colorimetry.	In-house method based on Examination of Water and Wastewater 20th Edition: Clesceri, Greenberg & Eaton (Skalar)	L080-PL	W	MCERTS
TPHCWG (Soil)	Determination of hexane extractable hydrocarbons in soil by GC-MS/GC-FID.	In-house method	L076-PL	W	MCERTS

For method numbers ending in 'UK' analysis have been carried out in our laboratory in the United Kingdom.

For method numbers ending in 'PL' analysis have been carried out in our laboratory in Poland.

Soil analytical results are expressed on a dry weight basis. Where analysis is carried out on as-received the results obtained are multiplied by a moisture correction factor that is determined gravimetrically using the moisture content which is carried out at a maximum of 30oC.

Iss No 16-26903-1 Green Park Village 1620000492

This certificate should not be reproduced, except in full, without the express permission of the laboratory.

The results included within the report are representative of the samples submitted for analysis.

Page 10 of 10

**Tom Smith**

Ramboll Environ UK Limited
Carlton House
Ringwood Road
Woodlands
Southampton
SO40 7HT

t: 02380817500

e: tom.smith@ramboll.co.uk

i2 Analytical Ltd.
7 Woodshots Meadow,
Croxley Green
Business Park,
Watford,
Herts,
WD18 8YS

t: 01923 225404

f: 01923 237404

e: reception@i2analytical.com

Analytical Report Number : 16-27300

Project / Site name:	Green Park Village	Samples received on:	07/09/2016
Your job number:		Samples instructed on:	08/09/2016
Your order number:	1620009315	Analysis completed by:	13/09/2016
Report Issue Number:	1	Report issued on:	13/09/2016
Samples Analysed:	2 soil samples		

Signed:

Rexona Rahman
Reporting Manager
For & on behalf of i2 Analytical Ltd.

Signed:

Dr Irma Doyle
Senior Account Manager
For & on behalf of i2 Analytical Ltd.

Standard Geotechnical, Asbestos and Chemical Testing Laboratory located at: ul. Pionierów 39, 41 -711 Ruda Śląska, Poland.

Accredited tests are defined within the report, opinions and interpretations expressed herein are outside the scope of accreditation.

Standard sample disposal times, unless otherwise agreed with the laboratory, are :	soils	- 4 weeks from reporting
	leachates	- 2 weeks from reporting
	waters	- 2 weeks from reporting
	asbestos	- 6 months from reporting

Excel copies of reports are only valid when accompanied by this PDF certificate.

Analytical Report Number: 16-27300

Project / Site name: Green Park Village

Your Order No: 1620009315

Lab Sample Number				626860	626861			
Sample Reference				P5_A	P5_B			
Sample Number				None Supplied	None Supplied			
Depth (m)				None Supplied	None Supplied			
Date Sampled				07/09/2016	07/09/2016			
Time Taken				None Supplied	None Supplied			
Analytical Parameter (Soil Analysis)	Units	Limit of detection	Accreditation Status					
Stone Content	%	0.1	NONE	< 0.1	< 0.1			
Moisture Content	%	N/A	NONE	19	18			
Total mass of sample received	kg	0.001	NONE	1.6	1.5			

Asbestos in Soil Screen / Identification Name	Type	N/A	ISO 17025	Chrysotile, Amosite	Chrysotile			
Asbestos in Soil	Type	N/A	ISO 17025	Detected	Detected			
Asbestos Quantification (Stage 2)	%	0.001	ISO 17025	< 0.001	< 0.001			
Asbestos Quantification Total	%	0.001	ISO 17025	< 0.001	< 0.001			

General Inorganics

pH - Automated	pH Units	N/A	MCERTS	8.2	8.3			
Total Cyanide	mg/kg	1	MCERTS	< 1	< 1			
Water Soluble SO ₄ 16hr extraction (2:1 Leachate Equivalent)	g/l	0.00125	MCERTS	0.37	0.33			

Total Phenols

Total Phenols (monohydric)	mg/kg	1	MCERTS	< 1.0	< 1.0			
----------------------------	-------	---	--------	-------	-------	--	--	--

Speciated PAHs

Naphthalene	mg/kg	0.05	MCERTS	0.19	0.20			
Acenaphthylene	mg/kg	0.1	MCERTS	0.26	< 0.10			
Acenaphthene	mg/kg	0.1	MCERTS	0.28	0.41			
Fluorene	mg/kg	0.1	MCERTS	0.59	0.55			
Phenanthrene	mg/kg	0.1	MCERTS	5.0	2.3			
Anthracene	mg/kg	0.1	MCERTS	1.0	0.59			
Fluoranthene	mg/kg	0.1	MCERTS	7.4	4.7			
Pyrene	mg/kg	0.1	MCERTS	6.1	4.2			
Benzo(a)anthracene	mg/kg	0.1	MCERTS	3.2	2.4			
Chrysene	mg/kg	0.05	MCERTS	2.4	1.6			
Benzo(b)fluoranthene	mg/kg	0.1	MCERTS	2.9	2.4			
Benzo(k)fluoranthene	mg/kg	0.1	MCERTS	1.7	1.2			
Benzo(a)pyrene	mg/kg	0.1	MCERTS	2.6	2.0			
Indeno(1,2,3-cd)pyrene	mg/kg	0.1	MCERTS	1.7	1.3			
Dibenz(a,h)anthracene	mg/kg	0.1	MCERTS	0.26	< 0.10			
Benzo(ghi)perylene	mg/kg	0.05	MCERTS	2.1	1.8			

Total PAH

Speciated Total EPA-16 PAHs	mg/kg	1.6	MCERTS	37.6	25.6			
-----------------------------	-------	-----	--------	------	------	--	--	--

Heavy Metals / Metalloids

Arsenic (aqua regia extractable)	mg/kg	1	MCERTS	12	14			
Beryllium (aqua regia extractable)	mg/kg	0.06	MCERTS	0.53	0.61			
Boron (water soluble)	mg/kg	0.2	MCERTS	2.9	2.1			
Cadmium (aqua regia extractable)	mg/kg	0.2	MCERTS	0.3	0.2			
Chromium (hexavalent)	mg/kg	4	MCERTS	< 4.0	< 4.0			
Chromium (aqua regia extractable)	mg/kg	1	MCERTS	17	24			
Copper (aqua regia extractable)	mg/kg	1	MCERTS	190	33			
Lead (aqua regia extractable)	mg/kg	1	MCERTS	330	170			
Mercury (aqua regia extractable)	mg/kg	0.3	MCERTS	0.5	0.4			
Nickel (aqua regia extractable)	mg/kg	1	MCERTS	19	20			
Selenium (aqua regia extractable)	mg/kg	1	MCERTS	< 1.0	< 1.0			
Vanadium (aqua regia extractable)	mg/kg	1	MCERTS	23	30			
Zinc (aqua regia extractable)	mg/kg	1	MCERTS	280	240			

Analytical Report Number: 16-27300

Project / Site name: Green Park Village

Your Order No: 1620009315

Lab Sample Number				626860	626861			
Sample Reference				P5_A	P5_B			
Sample Number				None Supplied	None Supplied			
Depth (m)				None Supplied	None Supplied			
Date Sampled				07/09/2016	07/09/2016			
Time Taken				None Supplied	None Supplied			
Analytical Parameter (Soil Analysis)				Units	Limit of detection	Accreditation Status		

Monoaromatics

Benzene	ug/kg	1	MCERTS	< 1.0	< 1.0			
Toluene	ug/kg	1	MCERTS	< 1.0	< 1.0			
Ethylbenzene	ug/kg	1	MCERTS	< 1.0	< 1.0			
p & m-xylene	ug/kg	1	MCERTS	< 1.0	< 1.0			
o-xylene	ug/kg	1	MCERTS	< 1.0	< 1.0			
MTBE (Methyl Tertiary Butyl Ether)	ug/kg	1	MCERTS	< 1.0	< 1.0			

Petroleum Hydrocarbons

TPH-CWG - Aliphatic >EC5 - EC6	mg/kg	0.1	MCERTS	< 0.1	< 0.1			
TPH-CWG - Aliphatic >EC6 - EC8	mg/kg	0.1	MCERTS	< 0.1	< 0.1			
TPH-CWG - Aliphatic >EC8 - EC10	mg/kg	0.1	MCERTS	< 0.1	< 0.1			
TPH-CWG - Aliphatic >EC10 - EC12	mg/kg	1	MCERTS	1.3	< 1.0			
TPH-CWG - Aliphatic >EC12 - EC16	mg/kg	2	MCERTS	9.6	9.9			
TPH-CWG - Aliphatic >EC16 - EC21	mg/kg	8	MCERTS	43	59			
TPH-CWG - Aliphatic >EC21 - EC35	mg/kg	8	MCERTS	190	210			
TPH-CWG - Aliphatic (EC5 - EC35)	mg/kg	10	MCERTS	250	280			

TPH-CWG - Aromatic >EC5 - EC7	mg/kg	0.1	MCERTS	< 0.1	< 0.1			
TPH-CWG - Aromatic >EC7 - EC8	mg/kg	0.1	MCERTS	< 0.1	< 0.1			
TPH-CWG - Aromatic >EC8 - EC10	mg/kg	0.1	MCERTS	< 0.1	< 0.1			
TPH-CWG - Aromatic >EC10 - EC12	mg/kg	1	MCERTS	< 1.0	< 1.0			
TPH-CWG - Aromatic >EC12 - EC16	mg/kg	2	MCERTS	17	7.5			
TPH-CWG - Aromatic >EC16 - EC21	mg/kg	10	MCERTS	120	74			
TPH-CWG - Aromatic >EC21 - EC35	mg/kg	10	MCERTS	360	230			
TPH-CWG - Aromatic (EC5 - EC35)	mg/kg	10	MCERTS	490	310			

Analytical Report Number: 16-27300
Project / Site name: Green Park Village
Your Order No: 1620009315

Lab Sample Number				626860	626861			
Sample Reference				P5_A	P5_B			
Sample Number				None Supplied	None Supplied			
Depth (m)				None Supplied	None Supplied			
Date Sampled				07/09/2016	07/09/2016			
Time Taken				None Supplied	None Supplied			
Analytical Parameter (Soil Analysis)	Units	Limit of detection	Accreditation Status					

VOCs

Chloromethane	µg/kg	1	ISO 17025	< 1.0	< 1.0			
Chloroethane	µg/kg	1	NONE	< 1.0	< 1.0			
Bromomethane	µg/kg	1	ISO 17025	< 1.0	< 1.0			
Vinyl Chloride	µg/kg	1	NONE	< 1.0	< 1.0			
Trichlorofluoromethane	µg/kg	1	NONE	< 1.0	< 1.0			
1,1-Dichloroethene	µg/kg	1	NONE	< 1.0	< 1.0			
1,1,2-Trichloro 1,2,2-Trifluoroethane	µg/kg	1	ISO 17025	< 1.0	< 1.0			
Cis-1,2-dichloroethene	µg/kg	1	MCERTS	< 1.0	< 1.0			
MTBE (Methyl Tertiary Butyl Ether)	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,1-Dichloroethane	µg/kg	1	MCERTS	< 1.0	< 1.0			
2,2-Dichloropropane	µg/kg	1	MCERTS	< 1.0	< 1.0			
Trichloromethane	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,1,1-Trichloroethane	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,2-Dichloroethane	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,1-Dichloropropene	µg/kg	1	MCERTS	< 1.0	< 1.0			
Trans-1,2-dichloroethene	µg/kg	1	NONE	< 1.0	< 1.0			
Benzene	µg/kg	1	MCERTS	< 1.0	< 1.0			
Tetrachloromethane	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,2-Dichloropropane	µg/kg	1	MCERTS	< 1.0	< 1.0			
Trichloroethene	µg/kg	1	MCERTS	< 1.0	< 1.0			
Dibromomethane	µg/kg	1	MCERTS	< 1.0	< 1.0			
Bromodichloromethane	µg/kg	1	MCERTS	< 1.0	< 1.0			
Cis-1,3-dichloropropene	µg/kg	1	ISO 17025	< 1.0	< 1.0			
Trans-1,3-dichloropropene	µg/kg	1	ISO 17025	< 1.0	< 1.0			
Toluene	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,1,2-Trichloroethane	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,3-Dichloropropane	µg/kg	1	ISO 17025	< 1.0	< 1.0			
Dibromochloromethane	µg/kg	1	ISO 17025	< 1.0	< 1.0			
Tetrachloroethene	µg/kg	1	NONE	< 1.0	< 1.0			
1,2-Dibromoethane	µg/kg	1	ISO 17025	< 1.0	< 1.0			
Chlorobenzene	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,1,1,2-Tetrachloroethane	µg/kg	1	MCERTS	< 1.0	< 1.0			
Ethylbenzene	µg/kg	1	MCERTS	< 1.0	< 1.0			
p & m-Xylene	µg/kg	1	MCERTS	< 1.0	< 1.0			
Styrene	µg/kg	1	MCERTS	< 1.0	< 1.0			
Tribromomethane	µg/kg	1	NONE	< 1.0	< 1.0			
o-Xylene	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,1,2,2-Tetrachloroethane	µg/kg	1	MCERTS	< 1.0	< 1.0			
Isopropylbenzene	µg/kg	1	MCERTS	< 1.0	< 1.0			
Bromobenzene	µg/kg	1	MCERTS	< 1.0	< 1.0			
n-Propylbenzene	µg/kg	1	ISO 17025	< 1.0	< 1.0			
2-Chlorotoluene	µg/kg	1	MCERTS	< 1.0	< 1.0			
4-Chlorotoluene	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,3,5-Trimethylbenzene	µg/kg	1	ISO 17025	< 1.0	< 1.0			
tert-Butylbenzene	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,2,4-Trimethylbenzene	µg/kg	1	ISO 17025	< 1.0	< 1.0			
sec-Butylbenzene	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,3-Dichlorobenzene	µg/kg	1	ISO 17025	< 1.0	< 1.0			
p-Isopropyltoluene	µg/kg	1	ISO 17025	< 1.0	< 1.0			
1,2-Dichlorobenzene	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,4-Dichlorobenzene	µg/kg	1	MCERTS	< 1.0	< 1.0			
Butylbenzene	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,2-Dibromo-3-chloropropane	µg/kg	1	ISO 17025	< 1.0	< 1.0			
1,2,4-Trichlorobenzene	µg/kg	1	MCERTS	< 1.0	< 1.0			
Hexachlorobutadiene	µg/kg	1	MCERTS	< 1.0	< 1.0			
1,2,3-Trichlorobenzene	µg/kg	1	ISO 17025	< 1.0	< 1.0			

Analytical Report Number: 16-27300
Project / Site name: Green Park Village
Your Order No: 1620009315

Lab Sample Number				626860	626861			
Sample Reference				P5_A	P5_B			
Sample Number				None Supplied	None Supplied			
Depth (m)				None Supplied	None Supplied			
Date Sampled				07/09/2016	07/09/2016			
Time Taken				None Supplied	None Supplied			
Analytical Parameter (Soil Analysis)	Units	Limit of detection	Accreditation Status					

SVOCs

Aniline	mg/kg	0.1	NONE	< 0.1	< 0.1			
Phenol	mg/kg	0.2	ISO 17025	< 0.2	< 0.2			
2-Chlorophenol	mg/kg	0.1	MCERTS	< 0.1	< 0.1			
Bis(2-chloroethyl)ether	mg/kg	0.2	MCERTS	< 0.2	< 0.2			
1,3-Dichlorobenzene	mg/kg	0.2	MCERTS	< 0.2	< 0.2			
1,2-Dichlorobenzene	mg/kg	0.1	MCERTS	< 0.1	< 0.1			
1,4-Dichlorobenzene	mg/kg	0.2	MCERTS	< 0.2	< 0.2			
Bis(2-chloroisopropyl)ether	mg/kg	0.1	MCERTS	< 0.1	< 0.1			
2-Methylphenol	mg/kg	0.3	MCERTS	< 0.3	< 0.3			
Hexachloroethane	mg/kg	0.05	MCERTS	< 0.05	< 0.05			
Nitrobenzene	mg/kg	0.3	MCERTS	< 0.3	< 0.3			
4-Methylphenol	mg/kg	0.2	NONE	< 0.2	< 0.2			
Isophorone	mg/kg	0.2	MCERTS	< 0.2	< 0.2			
2-Nitrophenol	mg/kg	0.3	MCERTS	< 0.3	< 0.3			
2,4-Dimethylphenol	mg/kg	0.3	MCERTS	< 0.3	< 0.3			
Bis(2-chloroethoxy)methane	mg/kg	0.3	MCERTS	< 0.3	< 0.3			
1,2,4-Trichlorobenzene	mg/kg	0.3	MCERTS	< 0.3	< 0.3			
Naphthalene	mg/kg	0.05	MCERTS	0.19	0.20			
2,4-Dichlorophenol	mg/kg	0.3	MCERTS	< 0.3	< 0.3			
4-Chloroaniline	mg/kg	0.1	NONE	< 0.1	< 0.1			
Hexachlorobutadiene	mg/kg	0.1	MCERTS	< 0.1	< 0.1			
4-Chloro-3-methylphenol	mg/kg	0.1	NONE	< 0.1	< 0.1			
2,4,6-Trichlorophenol	mg/kg	0.1	MCERTS	< 0.1	< 0.1			
2,4,5-Trichlorophenol	mg/kg	0.2	MCERTS	< 0.2	< 0.2			
2-Methylnaphthalene	mg/kg	0.1	NONE	0.5	0.5			
2-Chloronaphthalene	mg/kg	0.1	MCERTS	< 0.1	< 0.1			
Dimethylphthalate	mg/kg	0.1	MCERTS	< 0.1	< 0.1			
2,6-Dinitrotoluene	mg/kg	0.1	MCERTS	< 0.1	< 0.1			
Acenaphthylene	mg/kg	0.1	MCERTS	0.26	< 0.10			
Acenaphthene	mg/kg	0.1	MCERTS	0.28	0.41			
2,4-Dinitrotoluene	mg/kg	0.2	MCERTS	< 0.2	< 0.2			
Dibenzofuran	mg/kg	0.2	MCERTS	< 0.2	< 0.2			
4-Chlorophenyl phenyl ether	mg/kg	0.3	ISO 17025	< 0.3	< 0.3			
Diethyl phthalate	mg/kg	0.2	MCERTS	< 0.2	< 0.2			
4-Nitroaniline	mg/kg	0.2	MCERTS	< 0.2	< 0.2			
Fluorene	mg/kg	0.1	MCERTS	0.59	0.55			
Azobenzene	mg/kg	0.3	MCERTS	< 0.3	< 0.3			
Bromophenyl phenyl ether	mg/kg	0.2	MCERTS	< 0.2	< 0.2			
Hexachlorobenzene	mg/kg	0.3	MCERTS	< 0.3	< 0.3			
Phenanthrene	mg/kg	0.1	MCERTS	5.0	2.3			
Anthracene	mg/kg	0.1	MCERTS	1.0	0.59			
Carbazole	mg/kg	0.3	MCERTS	< 0.3	< 0.3			
Dibutyl phthalate	mg/kg	0.2	MCERTS	< 0.2	< 0.2			
Anthraquinone	mg/kg	0.3	MCERTS	0.5	0.5			
Fluoranthene	mg/kg	0.1	MCERTS	7.4	4.7			
Pyrene	mg/kg	0.1	MCERTS	6.1	4.2			
Butyl benzyl phthalate	mg/kg	0.3	ISO 17025	< 0.3	< 0.3			
Benzo(a)anthracene	mg/kg	0.1	MCERTS	3.2	2.4			
Chrysene	mg/kg	0.05	MCERTS	2.4	1.6			
Benzo(b)fluoranthene	mg/kg	0.1	MCERTS	2.9	2.4			
Benzo(k)fluoranthene	mg/kg	0.1	MCERTS	1.7	1.2			
Benzo(a)pyrene	mg/kg	0.1	MCERTS	2.6	2.0			
Indeno(1,2,3-cd)pyrene	mg/kg	0.1	MCERTS	1.7	1.3			
Dibenz(a,h)anthracene	mg/kg	0.1	MCERTS	0.26	< 0.10			
Benzo(ghi)perylene	mg/kg	0.05	MCERTS	2.1	1.8			



Analytical Report Number: 16-27300
Project / Site name: Green Park Village
Your Order No: 1620009315

Certificate of Analysis - Asbestos Quantification

Methods:

Qualitative Analysis

The samples were analysed qualitatively for asbestos by polarising light and dispersion staining as described by the Health and Safety Executive in HSG 248.

Quantitative Analysis

"The analysis was carried out using our documented in-house method A006 based on HSE Contract Research Report No: 83/1996: Development and Validation of an analytical method to determine the amount of asbestos in soils and loose aggregates (Davies et al, 1996) and HSG 248. Our method includes initial examination of the entire representative sample, then fractionation and detailed analysis of each fraction, with quantification by hand picking and weighing.

The limit of detection (reporting limit) of this method is 0.001 %.

The method has been validated using samples of at least 100 g, results for samples smaller than this should be interpreted with caution.

Both Qualitative and Quantitative Analyses are UKAS accredited.

Sample Number	Sample ID	Sample Depth (m)	Sample Weight (g)	Asbestos Containing Material Types Detected (ACM)	PLM Results	Asbestos by hand picking/weighing (%)	Total % Asbestos in Sample
626860	P5_A		114	Loose fibres	Chrysotile, Amosite	< 0.001	< 0.001
626861	P5_B		121	Hard/Cement type material	Chrysotile	< 0.001	< 0.001

Opinions and interpretations expressed herein are outside the scope of UKAS accreditation



Analytical Report Number : 16-27300

Project / Site name: Green Park Village

* These descriptions are only intended to act as a cross check if sample identities are questioned. The major constituent of the sample is intended to act with respect to MCERTS validation. The laboratory is accredited for sand, clay and loam (MCERTS) soil types. Data for unaccredited types of solid should be interpreted with care.

Stone content of a sample is calculated as the % weight of the stones not passing a 10 mm sieve. Results are not corrected for stone content.

Lab Sample Number	Sample Reference	Sample Number	Depth (m)	Sample Description *
626860	P5_A	None Supplied	None Supplied	Grey clay and gravel with vegetation.
626861	P5_B	None Supplied	None Supplied	Grey clay and gravel with vegetation.

Analytical Report Number : 16-27300

Project / Site name: Green Park Village

Water matrix abbreviations: Surface Water (SW) Potable Water (PW) Ground Water (GW)

Analytical Test Name	Analytical Method Description	Analytical Method Reference	Method number	Wet / Dry Analysis	Accreditation Status
Asbestos identification in soil	Asbestos Identification with the use of polarised light microscopy in conjunction with disperion staining techniques.	In house method based on HSG 248	A001-PL	D	ISO 17025
Asbestos Quantification - Gravimetric	Asbestos quantification by gravimetric method - in ouse method based on references.	HSE Report No: 83/1996, HSG 248, HSG 264 & SCA Blue Book (draft).	A006-PL	D	ISO 17025
Boron, water soluble, in soil	Determination of water soluble boron in soil by hot water extract followed by ICP-OES.	In-house method based on Second Site Properties version 3	L038-PL	D	MCERTS
BTEX and MTBE in soil (Monoaromatics)	Determination of BTEX in soil by headspace GC-MS.	In-house method based on USEPA8260	L073B-PL	W	MCERTS
D.O. for Gravimetric Quant if Screen/ID positive	Dependent option for Gravimetric Quant if Screen/ID positive scheduled.	In house asbestos methods A001 & A006.	A006-PL	D	NONE
Hexavalent chromium in soil	Determination of hexavalent chromium in soil by extraction in water then by acidification, addition of 1,5 diphenylcarbazine followed by colorimetry.	In-house method	L080-PL	W	MCERTS
Metals in soil by ICP-OES	Determination of metals in soil by aqua-regia digestion followed by ICP-OES.	In-house method based on MEWAM 2006 Methods for the Determination of Metals in Soil.	L038-PL	D	MCERTS
Moisture Content	Moisture content, determined gravimetrically.	In-house method based on BS1377 Part 3, 1990, Chemical and Electrochemical Tests	L019-UK/PL	W	NONE
Monohydric phenols in soil	Determination of phenols in soil by extraction with sodium hydroxide followed by distillation followed by colorimetry.	In-house method based on Examination of Water and Wastewater 20th Edition: Clesceri, Greenberg & Eaton (skalar)	L080-PL	W	MCERTS
pH in soil (automated)	Determination of pH in soil by addition of water followed by automated electrometric measurement.	In-house method based on BS1377 Part 3, 1990, Chemical and Electrochemical Tests	L099-PL	D	MCERTS
Semi-volatile organic compounds in soil	Determination of semi-volatile organic compounds in soil by extraction in dichloromethane and hexane followed by GC-MS.	In-house method based on USEPA 8270	L064-PL	D	MCERTS
Speciated EPA-16 PAHs in soil	Determination of PAH compounds in soil by extraction in dichloromethane and hexane followed by GC-MS with the use of surrogate and internal standards.	In-house method based on USEPA 8270	L064-PL	D	MCERTS
Stones content of soil	Standard preparation for all samples unless otherwise detailed. Gravimetric determination of stone > 10 mm as % dry weight.	In-house method based on British Standard Methods and MCERTS requirements.	L019-UK/PL	D	NONE
Sulphate, water soluble, in soil (16hr extraction)	Determination of water soluble sulphate by ICP-OES. Results reported directly (leachate equivalent) and corrected for extraction ratio (soil equivalent).	In-house method based on BS1377 Part 3, 1990, Chemical and Electrochemical Tests, 2:1 water:soil extraction, analysis by ICP-OES.	L038-PL	D	MCERTS
Total cyanide in soil	Determination of total cyanide by distillation followed by colorimetry.	In-house method based on Examination of Water and Wastewater 20th Edition: Clesceri, Greenberg & Eaton (Skalar)	L080-PL	W	MCERTS
TPHCWG (Soil)	Determination of hexane extractable hydrocarbons in soil by GC-MS/GC-FID.	In-house method	L076-PL	W	MCERTS
Volatile organic compounds in soil	Determination of volatile organic compounds in soil by headspace GC-MS.	In-house method based on USEPA8260	L073B-PL	W	MCERTS

Iss No 16-27300-1 Green Park Village

This certificate should not be reproduced, except in full, without the express permission of the laboratory.

The results included within the report are representative of the samples submitted for analysis.

Page 8 of 9



Analytical Report Number : 16-27300

Project / Site name: Green Park Village

Water matrix abbreviations: Surface Water (SW) Potable Water (PW) Ground Water (GW)

Analytical Test Name	Analytical Method Description	Analytical Method Reference	Method number	Wet / Dry Analysis	Accreditation Status
----------------------	-------------------------------	-----------------------------	---------------	--------------------	----------------------

For method numbers ending in 'UK' analysis have been carried out in our laboratory in the United Kingdom.

For method numbers ending in 'PL' analysis have been carried out in our laboratory in Poland.

Soil analytical results are expressed on a dry weight basis. Where analysis is carried out on as-received the results obtained are multiplied by a moisture correction factor that is determined gravimetrically using the moisture content which is carried out at a maximum of 30oC.

APPENDIX 3 – PHOTOGRAPHIC RECORD

Table A3 1: Photographic Record – Stage 1 Works

	
Plate 1 – Fenced off asbestos exclusion zone	Plate 2 – Turning over of Made Ground
	
Plate 3 – Implementation of dust suppression measures	Plate 4 - Removal of oversize material
	
Plate 3 – Removal of oversize material (2)	Plate 4 – Oversize material within area of deep Made Ground
	
Plate 5 – Area of deep Made Ground	Plate 6 – Area of deep Made Ground (2)



Plate 7 – Compaction of residual Made Ground



Plate 8 – Placement of orange marker layer



Plate 9 – Creation of clean service corridor



Plate 9 – Placement of orange marker layer

Table A3 2: Photographic Record – Stage 2 Works

	
Plate 1 – Turning over Made Ground	Plate 2 – Fenced off asbestos exclusion zone
	
Plate 3 – Turning over Made Ground and orange marker being laid	Plate 4 – Installed orange marker
	
Plate 5 – Wheel wash in operation	Plate 6 – Double bagged asbestos waste awaiting removal

Table A3 3: Photographic Record – Stage 3 Works

	
Plate 1 – Turning over of Made Ground	Plate 2 – Turning over of Made Ground and compaction
	
Plate 3 – Fenced off asbestos exclusion zone with compacted soil and membrane to be laid	Plate 4 – Membrane being laid to adjoin that installed during Stage 1 works
	
Plate 5 – Membrane being laid	

Table A3 4: Photographic Record – Additional Drainage Works

	
Plate 1 – Area to be excavated	Plate 2 – Extension of clean corridor
	
Plate 3 – Fenced off asbestos exclusion zone with decontamination unit and air monitoring unit	Plate 4 – Area post excavation (and pre-laying of the demarcation layer)
	
Plate 5 – Stockpile of arisings	

APPENDIX 4 – LUCION BULK SAMPLE ANALYSIS

Asbestos Fibre Identification Material Test Certificate

Job Ref No: **127573**, Account Ref No: **17752**, Contract Ref No: **16928**

This certificate is for the attention of	Andrew West Berkeley Homes (Western) Limited 200 Longwater Avenue Green Park Reading Berkshire RG2 6GB
Contract Title	Phase 5: Asbestos in Soils Support, Green Park Village
Site Address	Nearest postcode is: RG30 3UR. Refer to notes for directions.
Sampled Buildings	Berkeley Homes - Green Park Village, Berkeley Housing Development Site - Phase 5
Test material sampled by	Sean Sullivan
Sampling date	Thursday, 1st September, 2016
Analyst(s)	Stuart Hogg, Rachel Hutton, Matthew Chalmers, Freya Jones
Analyst signature(s)	
Analysis date	Tuesday, 6th September, 2016
Approved signatory	Peter Henshall
Approved signature	
Approval date	Tuesday, 6th September, 2016
Report Rendered on	Tue 13 Sep 2016 @ 10:11:24

Analysis method - In-house method TOP01.03 in accordance with HSG 248 - Asbestos: The Analysts' Guide For Sampling, Analysis and Clearance Procedures H.S.E. 2005. All analysis carried out at Lucion's Head Office laboratory.

Lucion bear no responsibility for sample collection or sample description related information provided by the client.

Where Lucion Environmental Ltd has not undertaken sampling; any prior sampling activity is beyond the company's responsibility. Where Lucion Environmental Ltd has sampled the test material, this has been done in accordance with in-house method TOP01.02. Any opinions and interpretations expressed herein are outside the scope of UKAS accreditation.

The results quoted in this report relate to:

1. Samples analysed in accordance with methods described above
2. Samples analysed and not necessarily to the material from which the samples were taken
3. The time during which sampling took place and to the conditions prevailing during that time

The samples referred to in this report will be retained for 6 months unless requested otherwise.

Total Samples	No Asbestos Detected	Asbestos-Containing Samples
10	8	2

Fibre Identification Analysis Results

Sample No.	Building	Level	Location	Item / Product Examined	Material Description	Analyst Comments	Fibre Identification
127573-1	Berkeley Housing Devolpment Site - Phase 5	0	Trial Pit RTP25	debris within soil	debris		NAD
127573-2	Berkeley Housing Devolpment Site - Phase 5	0	Trial Pit RTP25	board debris within soil	insulating board		NAD
127573-3	Berkeley Homes - Green Park Village	0	Phase 5 Earth Works	board debris within soil	Asbestos-containing insulating board		Amosite, Chrysotile
127573-4	Berkeley Homes - Green Park Village	0	Phase 5 Earth Works	board debris within soil	Asbestos-containing insulating board		Amosite, Chrysotile
127573-5	Berkeley Homes - Green Park Village	0	Phase 5 Earth Works	debris within soil	debris		NAD
127573-6	Berkeley Homes - Green Park Village	0	Phase 5 Earth Works	debris within soil	debris		NAD
127573-7	Berkeley Homes - Green Park Village	0	Phase 5 Earth Works	debris within soil	debris		NAD
127573-8	Berkeley Homes - Green Park Village	0	Phase 5 Earth Works	debris within soil	debris		NAD
127573-9	Berkeley Homes - Green Park Village	0	Phase 5 Earth Works	debris within soil	debris		NAD
127573-10	Berkeley Homes - Green Park Village	0	Phase 5 Earth Works	debris within soil	debris		NAD

APPENDIX 5 – LUCION BACKGROUND AIR MONITORING RESULTS

Asbestos Analyst's Job Summary Report

Job Ref No 123456, Account Ref No 123456, Contract Ref No 123456

Nearest postcode is: RG30 3UR Refer to notes for directions

Timeboundary, Assurance and Personal air testing



Photo Not Available



on site photo

Passed Certificates	Failed Certificates
3	0

Site visited on Wednesday, 4th August, 2016, and site visited Thursday, 9th September, 2016

Head Office

11 Park Place, Leeds, England,

LS1 1

E: enquiries@salbrookvance.co.uk

T: 01504 504030

Intro

This document is a summary of findings relating to asbestos analytical works at **Nearest postcode is: RG30 3UR** **Refer to notes for directions** from **Wednesday, 24th August, 2016 to Thursday, 29th September, 2016**. It is intended to give an overview of testing and must be read only in conjunction with the certificates it references. The document should never be read in isolation as asbestos analysts reports often contain additional notes and advice that should be referred to.

Furthermore, this document contains a summary of analyst notes and comments made in relation to works at this site.

Please note this document may contain findings from more than one analyst on more than one date.

Key to Air-Test Icons

To aid ease of reading the following icons have been used in this document to reference commonly undertaken activities.

-  Clearance Stage 1
-  Clearance Stage 2
-  Clearance Stage 3
-  Clearance Stage 4
-  DCU Stage 2
-  DCU Stage 3
-  Reassurance
-  Background
-  Leak Testing
-  Personal
-  Smoke Test Witness
-  Report Acknowledgement

A **WARNING** is used by the analyst to draw the readers attention to a particular area of the report.

Overview of Works

To view a complete air-certificate, follow the relevent link

 Certificate: Phase 5 West - Ground Investigation Earthworks

Building: Berkeley Homes - Green Park Village

Level: 0

Passed View the Full Certificate Here: http://web.lucion.co.uk/air_cert/22807?s=4a3d07fae0a01ca12ef26e1ac1f338ad

Type	Test-ID	Start Time	End Time	Date	Operative	# Samples	
 Personal	127574-29				 Mohammad Khan	2	
 Background	127574-30				 Mohammad Khan	9	
 Background	127574-1			24-08-2016	 Sean Sullivan	7	
 Reassurance	127574-4			26-08-2016	 Sean Sullivan	4	
 Background	127574-5			30-08-2016	 Promise Alioha	10	
 Background	127574-6			31-08-2016	 Promise Alioha	7	
 Personal	127574-7			31-08-2016	 Promise Alioha	2	
 Personal	127574-9			01-09-2016	 Sean Sullivan	2	
 Background	127574-8			01-09-2016	 Sean Sullivan	8	
 Reassurance	127574-10			02-09-2016	 Jonathan Bolton	9	
 Personal	127574-11			02-09-2016	 Jonathan Bolton	2	
 Background	127574-12			05-09-2016	 Stephanie Cave	10	
 Personal	127574-13			05-09-2016	 Stephanie Cave	3	
 Personal	127574-15			06-09-2016	 Stephanie Cave	3	
 Background	127574-14			06-09-2016	 Stephanie Cave	10	
 Personal	127574-17			07-09-2016	 Stephanie Cave	3	
 Background	127574-16			07-09-2016	 Stephanie Cave	10	
 Background	127574-18			08-09-2016	 Stephanie Cave	10	
 Personal	127574-19			08-09-2016	 Stephanie Cave	3	
 Background	127574-20			09-09-2016	 Jonathan Bolton	8	
 Personal	127574-21			09-09-2016	 Jonathan Bolton	2	
 Personal	127574-23			10-09-2016	 Kelvin Reynolds	2	
 Background	127574-22			10-09-2016	 Kelvin Reynolds	6	

Certificate: Phase 5 West - Ground Investigation Earthworks				Building: Berkeley Homes - Green Park Village		Level: 0	Passed 
Type	Test-ID	Start Time	End Time	Date	Operative	# Samples	
 Background	127574-24			12-09-2016	 Alf Browne	6	
 Personal	127574-25			12-09-2016	 Alf Browne	1	
 Personal	127574-27			13-09-2016	 Alf Browne	2	
 Background	127574-26			13-09-2016	 Alf Browne	6	
 Background	127574-32			15-09-2016	 Mohammad Khan	9	
 Personal	127574-31			15-09-2016	 Mohammad Khan	2	
 Background	127574-33			16-09-2016	 Mohammad Khan	3	
 Personal	127574-35			19-09-2016	 Alf Browne	1	
 Background	127574-34			19-09-2016	 Alf Browne	5	

Certificate: Phase 5 - Trial Pits

Building: Berkeley Homes - Green Park Village

Level: 0

Passed 

View the Full Certificate Here: http://web.lucion.co.uk/air_cert/22913?s=23357a77c18917d1ca48e24b429009b1

Type	Test-ID	Start Time	End Time	Date	Operative	# Samples	
 Personal	127574-3			26-08-2016	 Sean Sullivan	1	
 Background	127574-2			26-08-2016	 Sean Sullivan	7	
 Background	127574-28			14-09-2016	 Mohammad Khan	1	

 Certificate: Phase 5 East Earthworks

Building: Berkeley Homes - Green Park Village

Level: 0

Passed View the Full Certificate Here: http://web.lucion.co.uk/air_cert/23653?s=e50d406d0003e65914851c1d440826a0

Type	Test-ID	Start Time	End Time	Date	Operative	# Samples	
 Personal	127574-36			20-09-2016	 Promise Alioha	2	
 Background	127574-37			20-09-2016	 Promise Alioha	5	
 Background	127574-38			21-09-2016	 Promise Alioha	10	
 Background	127574-39			22-09-2016	 Promise Alioha	9	
 Personal	127574-40			22-09-2016	 Promise Alioha	1	
 Background	127574-41			23-09-2016	 Promise Alioha	10	
 Personal	127574-42			23-09-2016	 Promise Alioha	3	
 Background	127574-43			26-09-2016	 Jonathan Bolton	9	
 Background	127574-44			27-09-2016	 Jonathan Bolton	9	
 Background	127574-45			28-09-2016	 Jonathan Bolton	9	
 Background	127574-46			29-09-2016	 Jonathan Bolton	9	

Job Notes

Operative	Note	Date
 Sean Sullivan Senior Surveyor / Analyst	Lucion on site today to carry out background air tests during set up by Wooldridge (2 personnel), all overseen by Ramboll (2 personnel). Air test results below control limits.	Wednesday, 24th August, 2016
 Sean Sullivan Senior Surveyor / Analyst	Lucion on site to carry out (background & operational personal) air testing during investigation trial pits in Phase 5 with Woodbridge and Ramboll on site. All trial pits have now been investigated with various samples taken. All air testing results all below control limits of 0.01f/ccm. 	Friday, 26th August, 2016
 Promise Alioha Senior Surveyor / Analyst	PA on site. Had site induction and carried out background air monitoring during earthworks on Phase 5 Earthworks plan. 10 air samples were carried out mostly along the perimeter of Phase 5 Earthworks plan. Woodbridge and Ramboll were on site during works. The weather was sunny and windy with westerly wind direction during earthworks and air monitoring. All results are satisfactory <0.010f/ml.	Tuesday, 30th August, 2016
 Promise Alioha Senior Surveyor / Analyst	PA on site. Carried out background and personal air monitoring during earthworks on Phase 5 Earthworks plan. 9 samples were carried out mostly along the perimeter of Phase 5 Earthworks plan. Wooldridge and Ramboll engineers were on site during works. The weather was initially sunny then turned overcast and windy with southwesterly wind direction during earthworks and air monitoring. All results are satisfactory < 0.01f/ml	Wednesday, 31st August, 2016

Operative	Note	Date
 Sean Sullivan Senior Analyst	Lucion on site today to support Ramboll and Wooldridge in Phase 5 investigation works. Various air test samples taken including personals and backgrounds whilst operatives were turning material. All results to a satisfactory level <0.01f/ccm. 	Thursday, 1st September, 2016
 Mohammad Khan Senior Analyst	on site. waiting for the contact	Tuesday, 13th September, 2016
 Mohammad Khan Senior Analyst	on site. work to start.	Wednesday, 14th September, 2016
 Mohammad Khan Senior Analyst	on site. met supervisor. work like before	Thursday, 15th September, 2016
 Mohammad Khan Senior Analyst	On site at 8.15. There is no work going on due to raining. Spoke to supervisor Jorn, He said we just wait and see if we could work later got my contact.	Friday, 16th September, 2016
 Mohammad Khan Senior Analyst	contractor said no work will take place due to continuous rain. Carried out some backgrounds within the area. left site.	Friday, 16th September, 2016
 Promise Alioha Senior Surveyor Analyst	Lucion Analyst (PA) on site. Ramboll and Wooldridge on site. Analyst carried out 2 personal air test on Wooldridge operatives and 5 perimeter air monitoring during earthworks. The weather conditions were overcast and windy with easterly wind direction. All results are satisfactory <0.01f/ml	Tuesday, 20th September, 2016

Operative		Note	Date
	Promise Alioha Senior Surveyor Analyst	PA - Lucion Analyst arrived on site. Woodbridge and Ramboll engineers present on site. Analyst carried out 10 air test mostly along the perimeter of Phase 5 Earthworks plan during soil levelling. The weather conditions were dry and overcast and some sunny spells. The wind direction is Northeast. All results are satisfactory < 0.01f/ml	Wednesday, 21st September, 2016
	Promise Alioha Senior Surveyor Analyst	PA - Lucion Analyst arrived on site. Woodbridge operatives present on site. Analyst carried out 1 personal air test and 9 perimeter air monitoring during earthworks on Phase 5 Earthworks plan. The weather was initially overcast then sunny for the rest of the day. The wind direction is Northwest. All results are satisfactory < 0.01f /ml	Thursday, 22nd September, 2016
	Promise Alioha Senior Surveyor Analyst	PA - Lucion Analyst arrived on site. Woodbridge and Ramboll engineers present on site. Analyst carried out 3 personal air test and 10 perimeter air monitoring during earthworks on Phase 5 Earthworks plan. The weather was sunny and dry with westerly wind direction during earthworks. All results are satisfactory < 0.01f/ml	Friday, 23rd September, 2016

Attachments

The following documents accompany this report and should be regarded as an integral part of this report.

They can be downloaded from <http://web.lucion.co.uk/reports/127574/attachments>.

- [Method Statement \[http://web.lucion.co.uk/method_statements/127574?s=bcaaee0189f6b8a20c1354291ac56702 \]](http://web.lucion.co.uk/method_statements/127574?s=bcaaee0189f6b8a20c1354291ac56702)
- [Risk Assessment \[http://web.lucion.co.uk/risk_assessment/127574?s=d7f2d6d86e166bbb35c9964b2b642524 \]](http://web.lucion.co.uk/risk_assessment/127574?s=d7f2d6d86e166bbb35c9964b2b642524)

Asbestos Analyst's Certificate Report

Job Ref No 000000, Cert Ref No 000000, Account Ref No 000000, Contract Ref No 000000

St Edwards Homes, Green Park Village, Reading, RG30 3UR



Photo Not Available



on site photo

Building	Level	Works-Area	Enclosure Used	Certificate Issue Date
Berkeley Homes - Green Park Village	0	Phase 5 West - Ground Investigation Earthworks	No	Thursday, 20th October, 2016

Overall Certificate Status	Passed Tests	Failed Tests	WARNINGS
PASSED	0	0	0

Head Office

11 Park Place, Leeds, England,

LS1 1

E: enquiries@salbrookance.co

T: 0145 504030

Intro

This certificate is for the attention of

Andrew West
Berkeley Homes (Western) Limited
200 Longwater Avenue Green Park Reading Berkshire RG2 6GB

Sampling & Evaluation methods

In-house methods TOP02.08 & TOP02.09 in accordance with HSG 248 Asbestos - The Analyst's Guide to Sampling, Analysis and Clearance Procedures.

Notes: The samples referred to in this report will be retained for 6 months unless requested otherwise. Unless otherwise stated, there are no departures from the sampling and evaluation methods specified. Results detailed in this report relate only to the time, and corresponding conditions prevailing, when the sampling and examination were undertaken.

Notes to Test Accuracy

Airflow measured on site is recorded against a correction chart. Flow meters are calibrated against a UKAS certified master flow meter accurate to $\pm 0.5\%$. In accordance with HSG248, if the combined effect of ambient temperature and pressure between calibration and sampling location exceeds 5% a correction is applied to the air sample volume. The calculated fibre concentration is given for each air sample taken. Where the corresponding reported fibre concentration is preceded by "<", the lower limit of quantification (LOQ) of the method has not been reached. For a 480 litre air sample with 200 graticule areas counted, the (LOQ) of this method is 0.010 fibres per cubic centimetre of air; samples of less volume/graticules will be reported to a lower LOQ (refer count sheet). While counting randomly distributed fibres, an expected degree of variation of 1.5 standard deviations from the mean count may occur. At clearance indicator level (0.01 fibres per cubic centimetre of air) a 480-litre air sample yielding a count of 20 fibres over 200 fields would have an expected standard deviation of ± 8 fibres.

Sampling

When testing within an Enclosure and conducting a 4-Stage Clearance - the number of samples (Ns) is calculated by $A^{1/3}-1$. Where enclosure is less than 3m in height: A is denoted by area. Where enclosure is greater than 3m in height: A is denoted by volume/3. Refer air sampling and fibre counting sheet.

When testing within a decontamination unit (DCU) - where the combined floor area of shower and dirty areas is less than 10m²; 1 air test has been carried out. During this test the door between these areas has been propped open. For combined floor areas exceeding 10m² a sample in each area (i.e. shower and dirty end) will be taken.

For tests other than those associated with 4-Stage Clearance testing the analyst will apply the principles of current HSE guidance and experience combined with situational circumstances.

Where a photograph of the completed decontamination unit certificate appears in this report the analyst has completed an abridged report to be left inside the DCU; this abridged report should not be used in lieu of this comprehensive report.

Where sampling plans have been supplied; please note these are not to scale.

Where a sample filter has been deemed uncountable or biased the analyst will record this as "uncountable" in the count-sheet.

Field Blanks - Where site sampling and counting is carried out in a field laboratory a field blank is carried out by the analyst prior to the start of sampling and counting. The field blank constitutes a filter taken from a loaded but unused filter head that is mounted in the usual way and assigned a sample number which is recorded on the slide and the count sheet. Following sampling and analysis of the air tests, the results shall be assessed; where low counts ($<0.01 \text{ fcm}^{-3}$) are obtained from some of the field samples, analysis of the field blank will not be necessary. Where elevated counts ($>0.01 \text{ fcm}^{-3}$) are obtained on all field samples, then the field blank must be counted to exclude the possibility of contamination.

Disclaimers

Any opinions and interpretations expressed herein are outside the scope of UKAS accreditation. This certificate is valid only when it bears the signature of an authorised member of Lucion personnel. Please note the witnessing of smoke tests is outwith the scope of UKAS accreditation.

Representatives Signature - The signatory on report acknowledgement agrees to findings of this report being accurate and correct and Lucion Environmental Ltd issuing this report to the email address held on record for the job and does not require a copy of this report to be left on site. Furthermore Lucion Environmental Ltd cannot be held responsible for any actions undertaken following the issue of this report.

This certificate ☐ a ☐ be part of a series of works and should be read in conjunction with the Asbestos Analyst's Job Summary Report.

Report Contents

Test: Background (127574-1)	10
Sample: adjacent to perimeter - north east corner building material stock pile (127574-1-1)	11
Sample: adjacent to toilet compound - south east corner (127574-1-2)	11
Sample: adjacent to lake perimeter - south west corner (127574-1-3)	11
Sample: adjacent to lake - north west corner (127574-1-4)	11
Sample: adjacent to toilet cubical - south west corner (127574-1-5)	11
Sample: adjacent to access road/ storage materials - north east corner (127574-1-6)	11
Sample: adjacent to DCU (127574-1-7)	11
Test: Reassurance (127574-4)	12
Sample: Adjacent to perimeter fence - south west corner (127574-4-1)	13
Sample: Adjacent to perimeter fence - north west corner (127574-4-2)	13
Sample: Adjacent to perimeter fence - south east corner (127574-4-3)	13
Sample: Adjacent to perimeter fence - north east corner (127574-4-4)	13
Test: Background (127574-5)	14
Sample: Perimeter of Phase 5 Earthworks plan NE - Downwind (127574-5-1)	16
Sample: Perimeter of Phase 5 Earthworks plan NW - Upwind (127574-5-2)	16
Sample: Perimeter of Phase 5 Earthworks plan SE - Downwind (127574-5-3)	16
Sample: Perimeter of Phase 5 Earthworks plan SW - Upwind (127574-5-4)	16
Sample: Perimeter of Phase 5 Earthworks plan SE - Downwind (127574-5-5)	16
Sample: Perimeter of Phase 5 Earthworks plan SW - Upwind (127574-5-6)	16
Sample: Site lab test (127574-5-7)	16
Sample: Perimeter of Phase 5 Earthworks plan SE - Downwind (127574-5-8)	16
Sample: Perimeter of Phase 5 Earthworks plan SW - Upwind (127574-5-9)	16
Sample: Field Blank (127574-5-10)	16
Test: Background (127574-6)	18
Sample: Perimeter of Phase 5 Earthworks plan SW - Upwind (127574-6-1)	20
Sample: Perimeter of Phase 5 Earthworks plan SE - Downwind (127574-6-2)	20
Sample: Perimeter of Phase 5 Earthworks plan SE - Downwind (127574-6-3)	20
Sample: Perimeter of Phase 5 Earthworks plan SW - Upwind (127574-6-4)	20
Sample: Perimeter of Phase 5 Earthworks plan SE - Downwind (127574-6-5)	20
Sample: Perimeter of Phase 5 Earthworks plan SE - Downwind (127574-6-6)	20

Sample: Field Blank (127574-6-7)	20
Test: Personal (127574-7)	21
Sample: On Operative Will - applying dust suppression (Wooldridge banksman) during Phase 5 Earthworks (127574-7-1)	22
Sample: On Operative Richard - Excavation (Wooldridge Excavator) during Phase 5 Earthworks (127574-7-2)	22
Test: Background (127574-8)	23
Sample: Adjacent to perimeter fence - North East corner (127574-8-1)	24
Sample: Adjacent to perimeter fence - North West corner (127574-8-2)	24
Sample: Adjacent to perimeter fence - South East corner (127574-8-3)	24
Sample: Adjacent to perimeter fence - South West corner (127574-8-4)	24
Sample: Within Respirator Zone - lake side up on bank (127574-8-5)	24
Sample: Within Respirator Zone - adjacent to excavator (127574-8-6)	24
Sample: Adjacent to DCU - North West Corner (127574-8-7)	24
Sample: Adjacent to perimeter fence - North West Corner (127574-8-8)	24
Test: Personal (127574-9)	25
Sample: On Operative Sean Sullivan during Landscape Investigation Works (excavation) (127574-9-1)	26
Sample: On Ramboll Operative Chris Dawson during Landscape Investigation Works (excavation) (127574-9-2)	26
Test: Reassurance (127574-10)	27
Sample: Field Blank (127574-10-1)	28
Sample: Perimeter south east side (127574-10-2)	28
Sample: South side within perimeter (127574-10-3)	28
Sample: Perimeter east side adjacent dcu (127574-10-4)	28
Sample: South side within perimeter (127574-10-5)	28
Sample: Perimeter east side adjacent dcu (127574-10-6)	28
Sample: Perimeter south east side (127574-10-7)	28
Sample: Central debris pile within perimeter (127574-10-8)	28
Sample: South east side within perimeter (127574-10-9)	28
Test: Personal (127574-11)	30
Sample: South side- in jcb- Richard (127574-11-1)	31
Sample: Within perimeter - Banks man Will (127574-11-2)	31
Test: Background (127574-12)	32
Sample: Field Blank (127574-12-1)	33
Sample: Perimeter South (127574-12-2)	33
Sample: Perimeter East (127574-12-3)	33
Sample: Perimeter North-East (127574-12-4)	33

Sample: Perimeter South (127574-12-5)	33
Sample: Perimeter East (127574-12-6)	33
Sample: Perimeter North-East (127574-12-7)	33
Sample: Perimeter South (127574-12-8)	33
Sample: Perimeter East (127574-12-9)	33
Sample: Perimeter North-East (127574-12-10)	33
Test: Personal (127574-13)	35
Sample: On Chris Dawson (Ramboll), observation of work area (127574-13-1)	36
Sample: On Richard (Woolridge) operating digger (127574-13-2)	36
Sample: On Will (Woolridge) observation of work area (127574-13-3)	36
Test: Background (127574-14)	37
Sample: Field Blank (127574-14-1)	38
Sample: Perimeter South-East (127574-14-2)	38
Sample: Perimeter East (127574-14-3)	38
Sample: Perimeter East (127574-14-4)	38
Sample: Perimeter South-East (127574-14-5)	38
Sample: Perimeter East (127574-14-6)	38
Sample: Perimeter East (127574-14-7)	38
Sample: Perimeter South-East (127574-14-8)	38
Sample: Perimeter East (127574-14-9)	38
Sample: Perimeter East (127574-14-10)	38
Test: Personal (127574-15)	40
Sample: On Will (Woolridge) during observational brief (127574-15-1)	41
Sample: On Richard (Woolridge) during earth digging (127574-15-2)	41
Sample: On Yørn (Ramboll), during observational brief (127574-15-3)	41
Test: Background (127574-16)	42
Sample: Field Blank (127574-16-1)	43
Sample: Perimeter East (127574-16-2)	43
Sample: Perimeter West (127574-16-3)	43
Sample: Perimeter West (127574-16-4)	43
Sample: Perimeter East (127574-16-5)	43
Sample: Perimeter West (127574-16-6)	43
Sample: Perimeter West (127574-16-7)	43
Sample: Perimeter East (127574-16-8)	43

Sample: Perimeter West (127574-16-9)	43
Sample: Perimeter West (127574-16-10)	43
Test: Personal (127574-17)	45
Sample: On Yørn (Ramboll) during observational brief (127574-17-1)	46
Sample: On Will (Wooldridge) during wetting of dug earth (127574-17-2)	46
Sample: On Richard (Wooldridge) driving digger (127574-17-3)	46
Test: Background (127574-18)	47
Sample: Field Blank (127574-18-1)	48
Sample: Perimeter East (127574-18-2)	48
Sample: Perimeter East (127574-18-3)	48
Sample: Perimeter West (127574-18-4)	48
Sample: Perimeter West (127574-18-5)	48
Sample: Perimeter East (127574-18-6)	48
Sample: Perimeter East (127574-18-7)	48
Sample: Perimeter East (127574-18-8)	48
Sample: Perimeter East (127574-18-9)	48
Sample: Perimeter West (127574-18-10)	48
Test: Personal (127574-19)	50
Sample: On Yørn (Ramboll) during observational brief (127574-19-1)	51
Sample: On Will (Wooldridge) during wetting of dug earth (127574-19-2)	51
Sample: On Richard (Wooldridge) driving digger (127574-19-3)	51
Test: Background (127574-20)	52
Sample: Adjacent fence south east side (127574-20-1)	53
Sample: Adjacent fence south side (127574-20-2)	53
Sample: With perimeter (127574-20-3)	53
Sample: Within perimeter south east side (127574-20-4)	53
Sample: South east corner within perimeter (127574-20-5)	53
Sample: South east corner within perimeter (127574-20-6)	53
Sample: Adjacent DCU, East side (127574-20-7)	53
Sample: East side perimeter fence (127574-20-8)	53
Test: Personal (127574-21)	54
Sample: On Jorn, within perimeter (127574-21-1)	55
Sample: On Gavin operating jcb southern end. (127574-21-2)	55
Test: Background (127574-22)	56

Sample: south corner of work area (127574-22-1)	57
Sample: south west corner of work area (127574-22-2)	57
Sample: North corner of work area adjacent to DCU (127574-22-3)	57
Sample: south corner of work area outside the fence (127574-22-4)	57
Sample: East corner of work area outside of fence (127574-22-5)	57
Sample: North east of work area adjacent to DCU outside of fence (127574-22-6)	57
Test: Personal (127574-23)	58
Sample: on operative Matt driving the roller (127574-23-1)	59
Sample: on operative Gavin operating dozer and 360 (127574-23-2)	59
Test: Background (127574-24)	60
Sample: At North-Eastern end of compound (127574-24-1)	61
Sample: Along Eastern boundary of compound (127574-24-2)	61
Sample: Adjacent to DCU (127574-24-3)	61
Sample: At North Eastern end of compound (127574-24-4)	61
Sample: Along Eastern boundary of compound (127574-24-5)	61
Sample: Adjacent to DCU (127574-24-6)	61
Test: Personal (127574-25)	62
Sample: Within respirator zone of plant operator Rich (127574-25-1)	63
Test: Background (127574-26)	64
Sample: At North Eastern end of compound during spraying down of plant (127574-26-1)	65
Sample: Along Eastern boundary of compound (127574-26-2)	65
Sample: Adjacent to DCU (127574-26-3)	65
Sample: At Northern end of compound (127574-26-4)	65
Sample: Along Eastern boundary of compound (127574-26-5)	65
Sample: Adjacent to DCU (127574-26-6)	65
Test: Personal (127574-27)	66
Sample: Within plant operator Rich during groundworks (127574-27-1)	67
Sample: Within respirator zone of Jorn during groundworks (127574-27-2)	67
Test: Personal (127574-29)	68
Sample: on Richard Harding on digger (127574-29-1)	69
Sample: on Gavin Mayes Machine operator digging (127574-29-2)	69
Test: Background (127574-30)	70
Sample: Field Blank (127574-26-5)	71
Sample: Within respirator zone north corner (127574-30-1)	71

Sample: Within respirator zone rhs middle (127574-30-2)	71
Sample: Within respirator zone by dcu (127574-30-3)	71
Sample: Within respirator zone LHS south (127574-30-4)	71
Sample: Within respirator zone (127574-30-6)	71
Sample: Within respirator zone (127574-30-7)	71
Sample: Within respirator zone (127574-30-8)	71
Sample: Within respirator zone (127574-30-9)	71
Test: Personal (127574-31)	73
Sample: on Richard Harding while moving waste to skip (127574-31-1)	74
Sample: Within respirator zone on Jorn Pace (127574-31-2)	74
Test: Background (127574-32)	75
Sample: Within respirator zone (127574-32-1)	76
Sample: Within respirator zone (127574-32-2)	76
Sample: Within respirator zone (127574-32-3)	76
Sample: Within respirator zone (127574-32-4)	76
Sample: Field Blank (127574-32-5)	76
Sample: Within respirator zone (127574-32-6)	76
Sample: Within respirator zone (127574-32-7)	76
Sample: Within respirator zone (127574-32-8)	76
Sample: Within respirator zone (127574-32-9)	76
Test: Background (127574-33)	78
Sample: within the area prior to to work (127574-33-1)	79
Sample: within the area prior to work commences (127574-33-2)	79
Sample: Field Blank (127574-33-3)	79
Test: Background (127574-34)	80
Sample: At Eastern edge of exclusion zone (127574-34-1)	81
Sample: At Southern edge of exclusion zone (127574-34-2)	81
Sample: At Western edge of exclusion zone (127574-34-3)	81
Sample: Adjacent to DCU (127574-34-4)	81
Sample: At Eastern edge of exclusion zone (127574-34-5)	81
Test: Personal (127574-35)	82
Sample: Within respirator zone of plant operator Rich (127574-35-1)	83

Test: Background 127574-1

Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Wednesday, 24th August, 2016 @ 17:33:57
Additional Photo 1	 Plan of sample locations

Test: Background 127574-1 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-1		Wednesday, 24th August, 2016		Sean Sullivan		Sean Sullivan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				24		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1015		1		MS45		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS52		FM102		FM103		5739									
						Graticule Slide									
						SM41									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-1-1	adjacent to perimeter - north east corner building material stock pile	01	10	11:15:00	11:48:00	33	15.1		15.1	498	498	0.5	200	0.000	<0.01
127574-1-2	adjacent to toilet compound - south east corner	34	148	11:18:00	11:51:00	33	15.1		15.1	498	498	1.0	200	0.001	<0.01
127574-1-3	adjacent to lake perimeter - south west corner	231	164	11:20:00	11:54:00	34	15.1		15.1	513	513	1.0	200	0.000	<0.01
127574-1-4	adjacent to lake - north west corner	230	164	11:57:00	12:32:00	35	15.1		15.1	529	529	0.5	200	0.000	<0.01
127574-1-5	adjacent to toilet cubical - south west corner	34	148	13:30:00	14:04:00	34	15.1		15.1	513	513	1.0	200	0.000	<0.01
127574-1-6	adjacent to access road/ storage materials - north east corner	01	10	13:32:00	14:06:00	34	15.1		15.1	513	513	1.5	200	0.001	<0.01
127574-1-7	adjacent to DCU	231	148	14:10:00	14:42:00	32	15.1		15.1	483	483	1.0	200	0.001	<0.01

Test: Reassurance 127574-4

Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Friday, 26th August, 2016 @ 17:13:27

Test: Reassurance 127574-4 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-4		Friday, 26th August, 2016		Sean Sullivan		Sean Sullivan									
Air Volume Correction Detail															
T Cal °K		T Site °C		T Pcal hPa											
293		23		1013											
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro	Graticule Dia mm	Test Slide Result Grid		Filter Dia Exposed mm									
1016	1	MS41	100	5		22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi	Flow Low	HSE PL		Graticule Slide									
WS52		FM102	FM103	5739		SM41									
Sample Details															
Sample No	Sample Location	Head No	Pump No	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-4-1	Adjacent to perimeter fence - south west corner	250	148	09:45:00	10:19:00	34	15.1		15.1	513	513	1.0	200	0.000	<0.01
127574-4-2	Adjacent to perimeter fence - north west corner	231	109	09:49:00	10:23:00	34	15.1		15.1	513	513	1.0	200	0.000	<0.01
127574-4-3	Adjacent to perimeter fence - south east corner	40	148	13:04:00	13:38:00	34	15.1		15.1	513	513	1.0	200	0.000	<0.01
127574-4-4	Adjacent to perimeter fence - north east corner	189	109	12:50:00	13:24:00	34	15.1		15.1	513	513	0.0	200	0.000	<0.01

Test: Background 127574-5

Number of samples being taken	10
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 30th August, 2016 @ 10:12:20
Additional Photo 1	 Perimeter air monitoring downwind
Additional Photo 2	 Perimeter air monitoring Upwind

table continued from previous page...

Additional Photo 3



Site plan showing sample locations

Test: Background 127574-5 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-5		Tuesday, 30th August, 2016		Promise Alioha		Promise Alioha									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				33		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1016		1		MS		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS086		FM170		FM091		304									
						Graticule Slide									
						SM737									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-5-1	Perimeter of Phase 5 Earthworks plan NE - Downwind	611	331	10:54:00	12:00:00	66	8.0		8.0	528	528	3.0	200	0.001	<0.01
127574-5-2	Perimeter of Phase 5 Earthworks plan NW - Upwind	628	182	10:58:00	12:03:00	65	8.0		8.0	520	520	3.0	200	0.001	<0.01
127574-5-3	Perimeter of Phase 5 Earthworks plan SE - Downwind	706	1857	11:02:00	12:07:00	65	8.0		8.0	520	520	6.0	200	0.003	<0.01
127574-5-4	Perimeter of Phase 5 Earthworks plan SW - Upwind	704	442	11:06:00	12:10:00	64	8.0		8.0	512	512	2.0	200	0.001	<0.01
127574-5-5	Perimeter of Phase 5 Earthworks plan SE - Downwind	643	383	12:17:00	13:37:00	80	8.0	8.0	8.0	640	640	3.0	200	0.001	<0.01
127574-5-6	Perimeter of Phase 5 Earthworks plan SW - Upwind	705	442	12:19:00	13:39:00	80	8.0	8.0	8.0	640	640	2.5	200	0.001	<0.01
127574-5-7	Site lab test	611	1317	12:27:00	13:27:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01

table continued from previous page...

Sample Details															
127574-5-8	Perimeter of Phase 5 Earthworks plan SE - Downwind	628	182	14:09:00	15:09:00	60	8.0		8.0	480	480	3.0	200	0.002	<0.01
127574-5-9	Perimeter of Phase 5 Earthworks plan SW - Upwind	706	1857	14:12:00	15:12:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01
127574-5-10	Field Blank	704													

Test: Background 127574-6

Number of samples being taken	7
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Wednesday, 31st August, 2016 @ 08:44:24
Additional Photo 1	 Perimeter air monitoring Upwind
Additional Photo 2	 Perimeter air monitoring downwind

[table continued from previous page...](#)

Additional Photo 3



Perimeter air monitoring downwind

Additional Photo 4



Site plan showing sample locations

Test: Background 127574-6 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-6		Wednesday, 31st August, 2016		Promise Alioha		Promise Alioha									
Air Volume Correction Detail															
T Cal °K				T Site °C		T Pcal hPa									
293				21		1013									
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro	Graticule Dia mm	Test Slide Result Grid	Filter Dia Exposed mm										
1013	1	MS048	100	5	22.5										
Instrument Detail															
Thermometer, Barometer, Timepiece	Flow Hi	Flow Low	HSE PL	Graticule Slide											
WS086	FM170	FM091	304	SM737											
Sample Details															
Sample No	Sample Location	Head No	Pump No	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-6-1	Perimeter of Phase 5 Earthworks plan SW - Upwind	705	1317	08:15:00	10:25:00	130	4.0	4.0	4.0	520	520	1.5	200	0.001	<0.01
127574-6-2	Perimeter of Phase 5 Earthworks plan SE - Downwind	628	182	08:17:00	10:27:00	130	4.0	4.0	4.0	520	520	2.0	200	0.001	<0.01
127574-6-3	Perimeter of Phase 5 Earthworks plan SE - Downwind	643	383	08:20:00	10:29:00	129	4.0	4.0	4.0	516	516	2.0	200	0.001	<0.01
127574-6-4	Perimeter of Phase 5 Earthworks plan SW - Upwind	611	331	11:35:00	13:35:00	120	4.0	4.0	4.0	480	480	1.5	200	0.001	<0.01
127574-6-5	Perimeter of Phase 5 Earthworks plan SE - Downwind	704	442	11:37:00	13:37:00	120	4.0	4.0	4.0	480	480	2.0	200	0.001	<0.01
127574-6-6	Perimeter of Phase 5 Earthworks plan SE - Downwind	706	1857	11:38:00	13:38:00	120	4.0	4.0	4.0	480	480	1.5	200	0.001	<0.01
127574-6-7	Field Blank	705													

Test: Personal 127574-7

Number of samples being taken	2
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Wednesday, 31st August, 2016 @ 16:41:33

Test: Personal 127574-7 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-7		Wednesday, 31st August, 2016		Promise Alioha		Promise Alioha									
Air Volume Correction Detail															
T Cal K		T Site C		T Pcal hPa											
293		23		1013											
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro o	Graticule Dia mm		Test Slide Result Grid o		Filter Dia Exposed mm								
1013	1	MS048	100		5		22.5								
Instrument Detail															
Thermometer, Barometer, Timepiece	Flow Hi	Flow Low		HSE PL		Graticule Slide									
WS086	FM170	FM091		304		SM737									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-7-1	On Operative Will - applying dust suppression (Wooldridge banksman) during Phase 5 Earthworks	611	331	15:57:00	16:10:00	13	4.0		4.0	52	52	2.0	200	0.010	<0.01
127574-7-2	On Operative Richard - Excavation (Wooldridge Excavator) during Phase 5 Earthworks	704	442	15:59:00	16:12:00	13	4.0		4.0	52	52	1.0	200	0.005	<0.09

Test: Background 127574-8

Number of samples being taken	8
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Thursday, 1st September, 2016 @ 17:27:43

Test: Background 127574-8 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-8		Thursday, 1st September, 2016		Sean Sullivan		Sean Sullivan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				20		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1025		1		MS45		100									
						5									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS52		FM102		FM103		5739									
						SM41									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-8-1	Adjacent to perimeter fence - North East corner	230	109	08:25:00	08:59:00	34	15.1		15.1	513	513	3.5	200	0.002	<0.01
127574-8-2	Adjacent to perimeter fence - North West corner	231	10	08:36:00	09:10:00	34	15.1		15.1	513	513	0.5	200	0.000	<0.01
127574-8-3	Adjacent to perimeter fence - South East corner	01	80	08:27:00	09:01:00	34	15.1		15.1	513	513	1.5	200	0.001	<0.01
127574-8-4	Adjacent to perimeter fence - South West corner	199	164	08:29:00	09:03:00	34	15.1		15.1	513	513	1.0	200	0.000	<0.01
127574-8-5	Within Respirator Zone - lake side up on bank	123	80	09:30:00	10:04:00	34	15.1		15.1	513	513	0.0	200	0.000	<0.01
127574-8-6	Within Respirator Zone - adjacent to excavator	238	109	09:29:00	10:03:00	34	15.1		15.1	513	513	3.0	200	0.001	<0.01
127574-8-7	Adjacent to DCU - North West Corner	01	109	13:27:00	14:00:00	33	15.1		15.1	498	498	0.5	200	0.000	<0.01
127574-8-8	Adjacent to perimeter fence - North West Corner	123	148	13:29:00	14:02:00	33	15.1		15.1	498	498	1.0	200	0.001	<0.01

Test: Personal 127574-9

Number of samples being taken	2
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Thursday, 1st September, 2016 @ 17:27:15

Test: Personal 127574-9 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-9		Thursday, 1st September, 2016		Sean Sullivan		Sean Sullivan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				17		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1025		1		MS45		100									
						Test Slide Result Grid o									
						Filter Dia Exposed mm									
						5									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS52		FM102		FM103		5739									
						SM41									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ³	Report Conc Fibres cm ³
127574-9-1	On Operative Sean Sullivan during Landscape Investigation Works (excavation)	40	69	09:33:00	10:05:00	32	2.1		2.1	67	67	0.5	200	0.002	<0.07
127574-9-2	On Ramboll Operative Chris Dawson during Landscape Investigation Works (excavation)	230	69	13:26:00	13:59:00	33	2.1		2.1	69	69	0.5	200	0.002	<0.07

Test: Reassurance 127574-10

Number of samples being taken	9
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No

Test: Reassurance 127574-10 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-10		Friday, 2nd September, 2016		Jonathan Bolton		Jonathan Bolton									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				15		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1014		1		MS07		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS079		FM118		FM120		392									
						Graticule Slide									
						SM724									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-10-1	Field Blank	859													
127574-10-2	Perimeter south east side	858	1872	09:11:00	10:11:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
127574-10-3	South side within perimeter	791	1874	08:59:00	09:59:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
127574-10-4	Perimeter east side adjacent dcu	422	1875	09:10:00	10:10:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
127574-10-5	South side within perimeter	87	1877	08:59:00	09:59:00	60	8.0		8.0	480	480	1.5	200	0.001	<0.01
127574-10-6	Perimeter east side adjacent dcu	791	1876	11:59:00	12:59:00	60	8.0		8.0	480	480	1.5	200	0.001	<0.01
127574-10-7	Perimeter south east side	87	1875	11:58:00	12:58:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
127574-10-8	Central debris pile within perimeter	858	1872	12:01:00	13:01:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01
127574-10-9	South east side within perimeter	13	1874	12:05:00	13:05:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01


Test: Personal 127574-11

Number of samples being taken	2
Air sample results	All air samples gave results below 0.08 fibres per ccm of air.
Stage Warning?	No

Test: Personal 127574-11 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-11		Friday, 2nd September, 2016		Jonathan Bolton		Jonathan Bolton									
Air Volume Correction Detail															
T Cal K			T Site C			T Pcal hPa									
293			14			1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1015		1		MS07		100									
Test Slide Result Grid o		Filter Dia Exposed mm													
5		22.5													
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS079		FM118		FM120		392									
Graticule Slide		SM724													
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-11-1	South side- in jcb- Richard	859	481	09:00:00	10:00:00	60	2.0		2.0	120	120	1.0	100	0.004	<0.08
127574-11-2	Within perimeter - Banks man Will	859	481	12:05:00	13:05:00	60	2.0		2.0	120	120	1.0	100	0.004	<0.08

Test: Background 127574-12

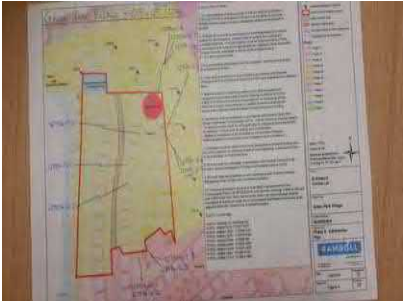Number of samples being taken	9
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Monday, 5th September, 2016 @ 16:22:46
Additional notes	Background air monitoring around perimeter of earth moving works
Additional Photo 1	 Site diagram with sample locations


Test: Background 127574-12 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-12		Monday, 5th September, 2016		Stephanie Cave		Stephanie Cave									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				22		1013									
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro o	Graticule Dia mm		Test Slide Result Grid o	Filter Dia Exposed mm									
1010	1	107	100		5	22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece	Flow Hi	Flow Low		HSE PL		Graticule Slide									
065	142	122		09		774									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-12-1	Field Blank	13													
127574-12-2	Perimeter South	346	1746	10:29:00	11:36:00	67	8.0		8.0	536	536	1.0	200	0.000	<0.01
127574-12-3	Perimeter East	370	1809	10:31:00	11:37:00	66	8.0		8.0	528	528	2.0	200	0.001	<0.01
127574-12-4	Perimeter North-East	534	1810	10:32:00	11:37:00	65	8.0		8.0	520	520	1.0	200	0.000	<0.01
127574-12-5	Perimeter South	346	1746	12:38:00	13:38:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01
127574-12-6	Perimeter East	370	1809	12:38:00	13:38:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
127574-12-7	Perimeter North-East	534	1810	12:39:00	13:39:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
127574-12-8	Perimeter South	346	1746	14:46:00	15:46:00	60	8.0		8.0	480	480	3.0	200	0.002	<0.01
127574-12-9	Perimeter East	370	1809	14:46:00	15:46:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01

[table continued from previous table...](#)

Sample Details															
127574-12-10	Perimeter North-East	534	1810	14:46:00	15:46:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01

Test: Personal 127574-13

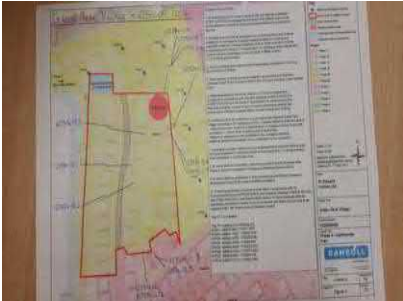Number of samples being taken	3
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Monday, 5th September, 2016 @ 16:23:44
Additional notes	Personal air monitoring on operatives conducting earth moving works
Additional Photo 1	 Site diagram with sample locations

Test: Personal 127574-13 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-13		Monday, 5th September, 2016		Stephanie Cave		Stephanie Cave									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				22		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1010		1		107		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
065		142		122		09									
						Graticule Slide									
						774									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-13-1	On Chris Dawson (Ramboll), observation of work area	630	503	11:36:00	12:33:00	57	2.0		2.0	114	114	2.0	200	0.004	<0.04
127574-13-2	On Richard (Woolridge) operating digger	636	503	12:37:00	13:17:00	40	2.0		2.0	80	80	1.0	200	0.003	<0.06
127574-13-3	On Will (Woolridge) observation of work area	630	503	14:46:00	15:16:00	30	2.0		2.0	60	60	1.0	200	0.004	<0.08

Test: Background 127574-14

Number of samples being taken	9
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 6th September, 2016 @ 16:54:29
Additional notes	Background air monitoring during earth moving works
Additional Photo 1	 Site diagram with sample locations

Test: Background 127574-14 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-14		Tuesday, 6th September, 2016		Stephanie Cave		Stephanie Cave									
Air Volume Correction Detail															
T Cal (K)				T Site (C)		T Pcal (hPa)									
293				21		1013									
Microscope Calculation Detail															
P Site (hPa)		Correction Required		Micro (o)		Graticule Dia (mm)									
1012		1		107		100									
						Test Slide Result (Grid (o))									
						5									
						Filter Dia (Exposed (mm))									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow (Hi)		Flow (Low)		HSE (PL)									
065		142		122		09									
						Graticule Slide									
						774									
Sample Details															
Sample (o)	Sample Location	Head (o)	Pump (o)	Time On (hh:mm)	Time Off (hh:mm)	Run Time (mins)	Start Flow (lmin-1)	Int Flow (lmin-1)	End Flow (lmin-1)	Calc Volume (l)	Corr Volume (l)	Fibres	Fields	Calc Conc (Fibres cm ⁻³)	Report Conc (Fibres cm ⁻³)
127574-14-1	Field Blank	13													
127574-14-2	Perimeter South-East	346	1746	08:21:00	09:45:00	84	8.0		8.0	672	672	1.0	200	0.000	<0.01
127574-14-3	Perimeter East	370	1809	08:23:00	09:47:00	84	8.0		8.0	672	672	2.0	200	0.001	<0.01
127574-14-4	Perimeter East	534	1810	08:23:00	09:47:00	84	8.0		9.0	714	714	1.0	200	0.000	<0.01
127574-14-5	Perimeter South-East	346	1746	11:15:00	12:32:00	77	8.0		8.0	616	616	3.0	200	0.001	<0.01
127574-14-6	Perimeter East	370	1809	11:17:00	12:32:00	75	8.0		8.0	600	600	2.0	200	0.001	<0.01
127574-14-7	Perimeter East	534	1810	11:17:00	12:32:00	75	8.0		8.0	600	600	3.0	200	0.001	<0.01
127574-14-8	Perimeter South-East	346	1746	14:05:00	15:11:00	66	8.0		8.0	528	528	2.0	200	0.001	<0.01
127574-14-9	Perimeter East	370	1809	14:07:00	15:09:00	62	8.0		8.0	496	496	3.0	200	0.002	<0.01

table continued from previous page...

Sample Details															
127574-14-10	Perimeter East	534	1810	14:07:00	15:09:00	62	8.0		8.0	496	496	2.0	200	0.001	<0.01

Test: Personal 127574-15

Number of samples being taken	3
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 6th September, 2016 @ 16:52:01
Additional notes	Personal air monitoring during earth moving works
Additional Photo 1	 Site diagram with sample locations

Test: Personal 127574-15 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-15		Tuesday, 6th September, 2016		Stephanie Cave		Stephanie Cave									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				21		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1012		1		107		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
065		142		122		09									
						Graticule Slide									
						774									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-15-1	On Will (Woolridge) during observational brief	630	503	08:18:00	09:01:00	43	2.0		2.0	86	86	1.0	200	0.003	<0.06
127574-15-2	On Richard (Wooldridge) during earth digging	630	803	12:32:00	13:00:00	28	2.0		2.0	56	56	1.0	200	0.005	<0.09
127574-15-3	On Yørn (Ramboll), during observational brief	630	503	14:02:00	15:09:00	67	2.0		2.0	134	134	2.0	200	0.004	<0.04

Test: Background 127574-16

Number of samples being taken	9
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Wednesday, 7th September, 2016 @ 16:38:44
Additional notes	Background air monitoring during earth moving works
Additional Photo 1	 Site diagram with sample locations

Test: Background 127574-16 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-16		Wednesday, 7th September, 2016		Stephanie Cave		Stephanie Cave									
Air Volume Correction Detail															
T Cal (K)				T Site (C)		T Pcal (hPa)									
293				21		1013									
Microscope Calculation Detail															
P Site (hPa)		Correction Required		Micro (o)		Graticule Dia (mm)									
1015		1		107		100									
Test Slide Result (Grid (o))		Filter Dia (Exposed (mm))													
5		22.5													
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow (Hi)		Flow (Low)		HSE (PL)									
065		142		122		219									
Graticule Slide		774													
Sample Details															
Sample (o)	Sample Location	Head (o)	Pump (o)	Time On (hh:mm)	Time Off (hh:mm)	Run Time (mins)	Start Flow (l/min-1)	Int Flow (l/min-1)	End Flow (l/min-1)	Calc Volume (l)	Corr Volume (l)	Fibres	Fields	Calc Conc (Fibres cm ⁻³)	Report Conc (Fibres cm ⁻³)
127574-16-1	Field Blank	13													
127574-16-2	Perimeter East	346	1811	08:43:00	09:49:00	66	8.0		8.0	528	528	2.0	200	0.001	<0.01
127574-16-3	Perimeter West	370	1888	08:46:00	09:52:00	66	8.0		8.0	528	528	2.0	200	0.001	<0.01
127574-16-4	Perimeter West	534	1319	08:47:00	09:53:00	66	8.0		8.0	528	528	4.5	200	0.002	<0.01
127574-16-5	Perimeter East	346	1811	11:37:00	12:40:00	63	8.0		8.0	504	504	2.0	200	0.001	<0.01
127574-16-6	Perimeter West	370	1888	11:44:00	12:44:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
127574-16-7	Perimeter West	534	1319	11:44:00	12:44:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01
127574-16-8	Perimeter East	346	1811	14:09:00	15:14:00	65	8.0		8.0	520	520	1.0	200	0.000	<0.01
127574-16-9	Perimeter West	370	1888	14:12:00	15:16:00	64	8.0		8.0	512	512	2.0	200	0.001	<0.01

table continued from previous page...

Sample Details															
127574-16-10	Perimeter West	534	1319	14:12:00	15:17:00	65	8.0		8.0	520	520	1.0	200	0.000	<0.01

Test: Personal 127574-17

Number of samples being taken	3
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Wednesday, 7th September, 2016 @ 16:38:18
Additional notes	Personal air monitoring during earth moving works
Additional Photo 1	 Site diagram with sample locations

Test: Personal 127574-17 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-17		Wednesday, 7th September, 2016		Stephanie Cave		Stephanie Cave									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				21		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1015		1		107		100									
Test Slide Result Grid o		Filter Dia Exposed mm													
5		22.5													
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
065		142		122		219									
Graticule Slide		774													
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-17-1	On Yørn (Ramboll) during observational brief	630	503	08:42:00	09:20:00	38	2.0		2.0	76	76	1.0	200	0.003	<0.06
127574-17-2	On Will (Wooldridge) during wetting of dug earth	630	503	11:41:00	12:34:00	53	6.0		2.0	212	212	2.0	200	0.002	<0.02
127574-17-3	On Richard (Wooldridge) driving digger	630	503	14:20:00	15:20:00	60	2.0		2.0	120	120	1.0	200	0.002	<0.04

Test: Background 127574-18

Number of samples being taken	9
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Thursday, 8th September, 2016 @ 16:48:11
Additional notes	Background air monitoring during earth moving works
Additional Photo 1	 Site diagram with sample locations

Test: Background 127574-18 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-18		Thursday, 8th September, 2016		Stephanie Cave		Stephanie Cave									
Air Volume Correction Detail															
T Cal (K)				T Site (C)		T Pcal (hPa)									
293				21		1013									
Microscope Calculation Detail															
P Site (hPa)		Correction Required		Micro (o)		Graticule Dia (mm)									
1015		1		107		100									
Test Slide Result (Grid (o))		Filter Dia (Exposed (mm))													
5		22.5													
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow (Hi)		Flow (Low)		HSE (PL)									
065		142		122		09									
Graticule Slide		774													
Sample Details															
Sample (o)	Sample Location	Head (o)	Pump (o)	Time On (hh:mm)	Time Off (hh:mm)	Run Time (mins)	Start Flow (l/min-1)	Int Flow (l/min-1)	End Flow (l/min-1)	Calc Volume (l)	Corr Volume (l)	Fibres	Fields	Calc Conc (Fibres cm ⁻³)	Report Conc (Fibres cm ⁻³)
127574-18-1	Field Blank	13													
127574-18-2	Perimeter East	346	1811	09:05:00	10:09:00	64	8.0		8.0	512	512	2.0	200	0.001	<0.01
127574-18-3	Perimeter East	370	1888	09:05:00	10:09:00	64	8.0		8.0	512	512	2.5	200	0.001	<0.01
127574-18-4	Perimeter West	534	1319	09:12:00	10:12:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01
127574-18-5	Perimeter West	346	1746	12:05:00	13:09:00	64	8.0		8.0	512	512	1.0	200	0.000	<0.01
127574-18-6	Perimeter East	370	1809	12:09:00	13:09:00	60	8.0		8.0	480	480	3.0	200	0.002	<0.01
127574-18-7	Perimeter East	534	1810	12:09:00	13:09:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01
127574-18-8	Perimeter East	346	1809	14:05:00	15:05:00	60	8.0		8.0	480	480	3.0	200	0.002	<0.01
127574-18-9	Perimeter East	370	1810	14:05:00	15:05:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01

table continued from previous table...

Sample Details															
127574-18-10	Perimeter West	534	1746	14:07:00	15:07:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01

Test: Personal 127574-19

Number of samples being taken	3
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Thursday, 8th September, 2016 @ 16:49:44
Additional notes	Personal air monitoring during earth moving works
Additional Photo 1	 Site diagram with sample locations

Test: Personal 127574-19 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-19		Thursday, 8th September, 2016		Stephanie Cave		Stephanie Cave									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				21		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1015		1		107		100									
Test Slide Result Grid o		Filter Dia Exposed mm													
5		22.5													
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
865		142		122		09									
Graticule Slide		774													
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-19-1	On Yørn (Ramboll) during observational brief	630	503	09:09:00	10:09:00	60	2.0		2.0	120	120	3.0	200	0.006	<0.04
127574-19-2	On Will (Wooldridge) during wetting of dug earth	630	503	12:05:00	13:05:00	60	2.0		2.0	120	120	1.0	200	0.002	<0.04
127574-19-3	On Richard (Wooldridge) driving digger	630	503	14:05:00	15:05:00	60	2.0		2.0	120	120	1.0	200	0.002	<0.04

Test: Background 127574-20

Number of samples being taken	8
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No

Test: Background 127574-20 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-20		Friday, 9th September, 2016		Jonathan Bolton		Jonathan Bolton									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				19		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1009		1		MS07		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS079		FM118		FM120		392									
						Graticule Slide									
						SM724									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-20-1	Adjacent fence south east side	13	1876	09:12:00	10:12:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01
127574-20-2	Adjacent fence south side	859	1875	09:12:00	10:12:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
127574-20-3	With perimeter	422	1874	09:10:00	10:10:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
127574-20-4	Within perimeter south east side	87	1873	09:10:00	10:10:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
127574-20-5	South east corner within perimeter	87	1873	12:32:00	14:10:00	98	8.0	8.0	8.0	784	784	1.5	122	0.001	<0.01
127574-20-6	South east corner within perimeter	422	1872	12:33:00	14:10:00	97	8.0	8.0	8.0	776	776	1.0	120	0.001	<0.01
127574-20-7	Adjacent DCU, East side	859	1875	12:36:00	14:12:00	96	8.0	8.0	8.0	768	768	1.0	126	0.001	<0.01
127574-20-8	East side perimeter fence	791	1876	12:37:00	14:12:00	95	8.0	8.0	8.0	760	760	1.0	126	0.001	<0.01

Test: Personal 127574-21

Number of samples being taken	2
Air sample results	All air samples gave results below 0.08 fibres per ccm of air.
Stage Warning?	No

Test: Personal 127574-21 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-21		Friday, 9th September, 2016		Jonathan Bolton		Jonathan Bolton									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				19		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1009		1		MS07		100									
						5									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS079		FM118		FM120		392									
						SM724									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-21-1	On Jorn, within perimeter	791	481	09:11:00	10:11:00	60	2.0		2.0	120	120	1.0	100	0.004	<0.08
127574-21-2	On Gavin operating jcb southern end.	13	481	12:30:00	13:30:00	60	2.0		2.0	120	120	1.5	100	0.006	<0.08

Test: Background 127574-22

Number of samples being taken	6
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Saturday, 10th September, 2016 @ 15:55:44

Test: Background 127574-22 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-22		Saturday, 10th September, 2016		Kelvin Reynolds		Kelvin Reynolds									
Air Volume Correction Detail															
T Cal (K)			T Site (C)			T Pcal (hPa)									
293			20			1013									
Microscope Calculation Detail															
P Site (hPa)		Correction Required		Micro (o)		Graticule Dia (mm)									
1013		1		MS07		100									
Test Slide Result (Grid (o))		Filter Dia (Exposed (mm))													
5		22.0													
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow (Hi)		Flow (Low)		HSE (PL)									
WS049		FM191		FM188		458									
Graticule Slide		SM760													
Sample Details															
Sample (o)	Sample Location	Head (o)	Pump (o)	Time On (hh:mm)	Time Off (hh:mm)	Run Time (mins)	Start Flow (lmin-1)	Int Flow (lmin-1)	End Flow (lmin-1)	Calc Volume (l)	Corr Volume (l)	Fibres	Fields	Calc Conc (Fibres cm ⁻³)	Report Conc (Fibres cm ⁻³)
127574-22-1	south corner of work area	987	1879	08:40:00	09:40:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01
127574-22-2	south west corner of work area	986	051	08:41:00	09:41:00	60	8.0		8.0	480	480	3.0	200	0.002	<0.01
127574-22-3	North corner of work area adjacent to DCU	982	02	08:43:00	09:43:00	60	8.0		8.0	480	480	5.0	200	0.003	<0.01
127574-22-4	south corner of work area outside the fence	982	051	10:55:00	11:55:00	60	8.0		8.0	480	480	2.5	200	0.001	<0.01
127574-22-5	East corner of work area outside of fence	983	1879	10:56:00	11:56:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
127574-22-6	North east of work area adjacent to DCU outside of fence	987	02	10:57:00	11:57:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01

Test: Personal 127574-23

Number of samples being taken	2
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Saturday, 10th September, 2016 @ 15:54:37

Test: Personal 127574-23 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-23		Saturday, 10th September, 2016		Kelvin Reynolds		Kelvin Reynolds									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				20		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1013		1		MS07		100									
						5									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS049		FM191		FM188		458									
						SM760									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-23-1	on operative Matt driving the roller	984	416	08:30:00	09:00:00	30	2.0		2.0	60	60	8.0	200	0.032	<0.08
127574-23-2	on operative Gavin operating dozer and 360	984	416	10:50:00	11:50:00	60	2.0		2.0	120	120	6.0	200	0.012	<0.04

Test: Background 127574-24

Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Monday, 12th September, 2016 @ 17:19:28

Test: Background 127574-24 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-24		Monday, 12th September, 2016		Alf Browne		Alf Browne									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				23		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro		Graticule Dia mm									
1020		1		MS12		100									
						Test Slide Result Grid									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS55		FM106		FM107		6154									
						Graticule Slide									
						SM30									
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
				hh:mm	hh:mm	mins	lmin-1	lmin-1	lmin-1	l	l			Fibres cm ⁻³	Fibres cm ⁻³
127574-24-1	At North-Eastern end of compound	231	101	10:57:00	11:29:00	32	15.1		15.1	483	483	2.0	200	0.001	<0.01
127574-24-2	Along Eastern boundary of compound	233	101	11:34:00	12:06:00	32	15.1		15.1	483	483	1.5	200	0.001	<0.01
127574-24-3	Adjacent to DCU	231	101	12:29:00	13:01:00	32	15.1		15.1	483	483	3.0	200	0.002	<0.01
127574-24-4	At North Eastern end of compound	233	101	13:32:00	14:04:00	32	15.1		15.1	483	483	2.0	200	0.001	<0.01
127574-24-5	Along Eastern boundary of compound	231	39	14:32:00	15:04:00	32	15.1		15.1	483	483	2.0	200	0.001	<0.01
127574-24-6	Adjacent to DCU	233	39	15:33:00	16:05:00	32	15.1		15.1	483	483	3.0	200	0.002	<0.01

Test: Personal 127574-25

Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Monday, 12th September, 2016 @ 17:24:19

Test: Personal 127574-25 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-25		Monday, 12th September, 2016		Alf Browne		Alf Browne									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				23		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1020		1		MS12		100									
						Test Slide Result Grid o									
						Filter Dia Exposed mm									
						5									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS55		FM106		FM107		6154									
						Graticule Slide									
						SM30									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-25-1	Within respirator zone of plant operator Rich	116	02	11:21:00	12:01:00	40	4.1		4.1	164	164	1.0	200	0.002	<0.03

Test: Background 127574-26

Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 13th September, 2016 @ 17:11:49

Test: Background 127574-26 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-26		Tuesday, 13th September, 2016		Alf Browne		Alf Browne									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				26		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1020		1		MS12		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS55		FM106		FM107		6154									
						Graticule Slide									
						SM30									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-26-1	At North Eastern end of compound during spraying down of plant	231	39	08:21:00	08:53:00	32	15.1		15.1	483	483	2.5	200	0.001	<0.01
127574-26-2	Along Eastern boundary of compound	233	39	09:29:00	10:01:00	32	15.1		15.1	483	483	1.0	200	0.001	<0.01
127574-26-3	Adjacent to DCU	231	39	10:32:00	11:04:00	32	15.1		15.1	483	483	2.0	200	0.001	<0.01
127574-26-4	At Northern end of compound	233	39	12:02:00	12:34:00	32	15.1		15.1	483	483	2.0	200	0.001	<0.01
127574-26-5	Along Eastern boundary of compound	231	71	13:37:00	14:37:00	60	8.1		8.1	486	486	3.0	200	0.002	<0.01
127574-26-6	Adjacent to DCU	233	71	14:59:00	15:59:00	60	8.1		8.1	486	486	1.5	200	0.001	<0.01

Test: Personal 127574-27

Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 13th September, 2016 @ 15:33:17

Test: Personal 127574-27 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-27		Tuesday, 13th September, 2016		Alf Browne		Alf Browne									
Air Volume Correction Detail															
T Cal K		T Site C		T Pcal hPa											
293		26		1013											
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro o	Graticule Dia mm		Test Slide Result Grid o		Filter Dia Exposed mm								
1025	1	MS12	100		5		22.5								
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS55		FM106		FM107		SM30									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-27-1	Within plant operator Rich during groundworks	116	02	09:30:00	10:51:00	81	2.1		2.1	170	170	2.0	200	0.003	<0.03
127574-27-2	Within respirator zone of Jorn during groundworks	116	02	12:31:00	13:36:00	65	2.1		2.1	137	137	3.0	200	0.006	<0.04

Test: Personal 127574-29

Number of samples being taken	2
Additional Photo 1	

Test: Personal 127574-29 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-29				Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				25		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1002		1		MS109		100									
						5									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS264		FM111		FM190		222									
						SM748									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-29-1	on Richard Harding on digger	635	20	08:08:00	10:10:00	122	1.0		1.0	122	122	2.0	200	0.004	<0.04
127574-29-2	on Gavin Mayes Machine operator digging	702	20	12:47:00	14:50:00	123	1.0		1.0	123	123	4.0	200	0.008	<0.04

Test: Background 127574-30

Number of samples being taken	9
Additional Photo 1	

Test: Background 127574-30 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-30				Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				25		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro		Graticule Dia mm									
1002		1		MS109		100									
						Test Slide Result Grid									
						5									
						Filter Dia Exposed mm									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS264		FM111		FM190		222									
						Graticule Slide									
						SM748									
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
				hh:mm	hh:mm	mins	lmin-1	lmin-1	lmin-1	l	l			Fibres cm ³	Fibres cm ³
127574-26-5	Field Blank	635										0.0	100		
127574-30-1	Within respirator zone north corner	535	1709	08:12:00	10:12:00	120	8.0		8.0	960	960	2.0	100	0.001	<0.01
127574-30-2	Within respirator zone rhs middle	80	1716	08:13:00	10:14:00	121	8.0		8.0	968	968	2.5	100	0.001	<0.01
127574-30-3	Within respirator zone by dcu	450	1709	08:14:00	10:16:00	122	8.0		8.0	976	976	3.0	100	0.001	<0.01
127574-30-4	Within respirator zone LHS south	517	1718	08:15:00	10:18:00	123	8.0		8.0	984	984	4.0	100	0.002	<0.01
127574-30-6	Within respirator zone	324	1709	12:48:00	14:51:00	123	8.0		8.0	984	984	3.0	100	0.001	<0.01
127574-30-7	Within respirator zone	301	1716	12:48:00	14:51:00	123	8.0		8.0	984	984	4.0	100	0.002	<0.01
127574-30-8	Within respirator zone	530	1708	12:49:00	14:52:00	123	8.0		8.0	984	984	3.0	100	0.001	<0.01
127574-30-9	Within respirator zone	600	1718	12:50:00	14:54:00	124	8.0		8.0	992	992	3.5	100	0.002	<0.01

Test: Personal 127574-31

Number of samples being taken	2
Air sample results	All final results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Thursday, 15th September, 2016 @ 16:02:18
Additional Photo 1	

Test: Personal 127574-31 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-31		Thursday, 15th September, 2016		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				18		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1003		1		MS109		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS264		FM111		FM190		222									
						Graticule Slide									
						SM748									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-31-1	on Richard Harding while moving waste to skip	600	20	08:25:00	10:21:00	116	1.0		1.0	116	116	2.0	200	0.004	<0.04
127574-31-2	Within respirator zone on Jorn Pace	450	20	11:48:00	12:58:00	70	1.0		1.0	70	70	1.0	200	0.003	<0.07

Test: Background 127574-32

Number of samples being taken	9
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Thursday, 15th September, 2016 @ 16:00:39

Test: Background 127574-32 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-32		Thursday, 15th September, 2016		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal °K		T Site °C		T Pcal hPa											
293		18		1013											
Microscope Calculation Detail															
P Site hPa	Correction Required	Microscope	Graticule Dia mm		Test Slide Result Grid		Filter Dia Exposed mm								
1003	1	MS109	100		5		22.0								
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS264		FM111		FM190		222									
Graticule Slide															
SM748															
Sample Details															
Sample No	Sample Location	Head No	Pump No	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-32-1	Within respirator zone	530	1718	08:16:00	10:15:00	119	8.0		8.0	952	952	3.0	100	0.002	<0.01
127574-32-2	Within respirator zone	301	1716	08:17:00	10:17:00	120	8.0		8.0	960	960	3.5	100	0.002	<0.01
127574-32-3	Within respirator zone	324	1721	08:18:00	10:19:00	121	8.0		8.0	968	968	5.5	100	0.003	<0.01
127574-32-4	Within respirator zone	635	1708	08:20:00	10:22:00	122	8.0		8.0	976	976	2.0	100	0.001	<0.01
127574-32-5	Field Blank	702										0.0	100		
127574-32-6	Within respirator zone	702	1718	12:58:00	14:59:00	121	8.0		8.0	968	968	2.0	100	0.001	<0.01
127574-32-7	Within respirator zone	438	1716	12:59:00	15:00:00	121	8.0		8.0	968	968	Uncountable			

table continued from previous table...

Sample Details															
127574-32-8	Within respirator zone	530	1708	13:00:00	15:02:00	122	8.0		8.0	976	976	4.0	100	0.002	<0.01
127574-32-9	Within respirator zone	517	1715	13:01:00	15:03:00	122	8.0		8.0	976	976	3.5	100	0.002	<0.01

Test: Background 127574-33

Number of samples being taken	2
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Friday, 16th September, 2016 @ 13:15:24
Additional notes	no work due to continuous rain. just background airtests within Harris fence
Additional Photo 1	

Test: Background 127574-33 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-33		Friday, 16th September, 2016		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				16		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1004		1		MS109		100									
						Test Slide Result Grid o									
						Filter Dia Exposed mm									
						5									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS264		FM111		FM190		222									
						Graticule Slide									
						SM748									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-33-1	within the area prior to to work	702	1708	09:40:00	10:45:00	65	8.0		8.0	520	520	2.0	200	0.001	<0.01
127574-33-2	within the area prior to work commences	517	1721	09:42:00	10:46:00	64	8.0		8.0	512	512	1.5	200	0.001	<0.01
127574-33-3	Field Blank	301										0.0	100		

Test: Background 127574-34

Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Monday, 19th September, 2016 @ 17:48:46

Test: Background 127574-34 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-34		Monday, 19th September, 2016		Alf Browne		Alf Browne									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				20		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1015		1		MS12		100									
Test Slide Result Grid o		Filter Dia Exposed mm													
5		22.5													
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS55		FM106		FM107		6154									
Graticule Slide		SM30													
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ³	Report Conc Fibres cm ³
127574-34-1	At Eastern edge of exclusion zone	231	39	09:29:00	10:29:00	60	8.1		8.1	486	486	1.0	200	0.001	<0.01
127574-34-2	At Southern edge of exclusion zone	233	39	11:08:00	12:08:00	60	8.1		8.1	486	486	2.0	200	0.001	<0.01
127574-34-3	At Western edge of exclusion zone	231	39	12:31:00	13:31:00	60	8.1		8.1	486	486	3.0	200	0.002	<0.01
127574-34-4	Adjacent to DCU	233	71	13:45:00	14:45:00	60	8.1		8.1	486	486	1.0	200	0.001	<0.01
127574-34-5	At Eastern edge of exclusion zone	231	71	15:00:00	16:00:00	60	8.1		8.1	486	486	0.5	200	0.000	<0.01

Test: Personal 127574-35

Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Monday, 19th September, 2016 @ 15:36:34

Test: Personal 127574-35 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-35		Monday, 19th September, 2016		Alf Browne		Alf Browne									
Air Volume Correction Detail															
T Cal K			T Site C			T Pcal hPa									
293			20			1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1012		1		MS12		100									
						5									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS55		FM106		FM107		6154									
						SM30									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-35-1	Within respirator zone of plant operator Rich	44	02	12:34:00	14:31:00	117	2.1		2.1	246	246	1.5	200	0.002	<0.02

Asbestos Analyst's Certificate Report

Job Ref No 000000, Cert Ref No 000000, Account Ref No 000000, Contract Ref No 000000

St Edwards Homes, Green Park Village, Reading, RG30 3UR



Photo Not Available



on site photo

Building	Level	Works-Area	Enclosure Used	Certificate Issue Date
Berkeley Homes - Green Park Village	0	Phase 5 - Trial Pits	No	Friday, 26th August, 2016

Overall Certificate Status	Passed Tests	Failed Tests	WARNINGS
PASSED	0	0	0

Intro

This certificate is for the attention of

Andrew West
Berkeley Homes (Western) Limited
200 Longwater Avenue Green Park Reading Berkshire RG2 6GB

Sampling & Evaluation methods

In-house methods TOP02.08 & TOP02.09 in accordance with HSG 248 Asbestos - The Analyst's Guide to Sampling, Analysis and Clearance Procedures.

Notes: The samples referred to in this report will be retained for 6 months unless requested otherwise. Unless otherwise stated, there are no departures from the sampling and evaluation methods specified. Results detailed in this report relate only to the time, and corresponding conditions prevailing, when the sampling and examination were undertaken.

Notes to Test Accuracy

Airflow measured on site is recorded against a correction chart. Flow meters are calibrated against a UKAS certified master flow meter accurate to $\pm 0.5\%$. In accordance with HSG248, if the combined effect of ambient temperature and pressure between calibration and sampling location exceeds 5% a correction is applied to the air sample volume. The calculated fibre concentration is given for each air sample taken. Where the corresponding reported fibre concentration is preceded by "<", the lower limit of quantification (LOQ) of the method has not been reached. For a 480 litre air sample with 200 graticule areas counted, the (LOQ) of this method is 0.010 fibres per cubic centimetre of air; samples of less volume/graticules will be reported to a lower LOQ (refer count sheet). While counting randomly distributed fibres, an expected degree of variation of 1.5 standard deviations from the mean count may occur. At clearance indicator level (0.01 fibres per cubic centimetre of air) a 480-litre air sample yielding a count of 20 fibres over 200 fields would have an expected standard deviation of ± 8 fibres.

Sampling

When testing within an Enclosure and conducting a 4-Stage Clearance - the number of samples (Ns) is calculated by $A^{1/3}-1$. Where enclosure is less than 3m in height: A is denoted by area. Where enclosure is greater than 3m in height: A is denoted by volume/3. Refer air sampling and fibre counting sheet.

When testing within a decontamination unit (DCU) - where the combined floor area of shower and dirty areas is less than 10m²; 1 air test has been carried out. During this test the door between these areas has been propped open. For combined floor areas exceeding 10m² a sample in each area (i.e. shower and dirty end) will be taken.

For tests other than those associated with 4-Stage Clearance testing the analyst will apply the principles of current HSE guidance and experience combined with situational circumstances.

Where a photograph of the completed decontamination unit certificate appears in this report the analyst has completed an abridged report to be left inside the DCU; this abridged report should not be used in lieu of this comprehensive report.

Where sampling plans have been supplied; please note these are not to scale.

Where a sample filter has been deemed uncountable or biased the analyst will record this as "uncountable" in the count-sheet.

Field Blanks - Where site sampling and counting is carried out in a field laboratory a field blank is carried out by the analyst prior to the start of sampling and counting. The field blank constitutes a filter taken from a loaded but unused filter head that is mounted in the usual way and assigned a sample number which is recorded on the slide and the count sheet. Following sampling and analysis of the air tests, the results shall be assessed; where low counts ($<0.01 \text{ fcm}^{-3}$) are obtained from some of the field samples, analysis of the field blank will not be necessary. Where elevated counts ($>0.01 \text{ fcm}^{-3}$) are obtained on all field samples, then the field blank must be counted to exclude the possibility of contamination.

Disclaimers

Any opinions and interpretations expressed herein are outside the scope of UKAS accreditation. This certificate is valid only when it bears the signature of an authorised member of Lucion personnel. Please note the witnessing of smoke tests is outwith the scope of UKAS accreditation.

Representatives Signature - The signatory on report acknowledgement agrees to findings of this report being accurate and correct and Lucion Environmental Ltd issuing this report to the email address held on record for the job and does not require a copy of this report to be left on site. Furthermore Lucion Environmental Ltd cannot be held responsible for any actions undertaken following the issue of this report.

This certificate ☐ a ☐ be part of a series of works and should be read in conjunction with the Asbestos Analyst's Job Summary Report.

Report Contents

Test: Background (127574-2)5

 Sample: Adjacent to trial pit RTP26 (127574-2-1)6

 Sample: Adjacent to trial pit RTP28 (127574-2-2)6

 Sample: Adjacent to trial pit RTP27 (127574-2-3)6

 Sample: Adjacent to trial pit RTP29 (127574-2-4)6

 Sample: Adjacent to trial pit RTP30 (127574-2-5)6

 Sample: Adjacent to trial pit RTP24 (127574-2-6)6

 Sample: Adjacent to trial pit RTP23 (127574-2-7)6

Test: Personal (127574-3)7

 Sample: On Operative Richard Harding during trial pit investigation RPT28 (127574-3-1)8

Test: Background (127574-28)9

 Sample: lab within site office (127574-28-1)10

Test: Background 127574-2

Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Friday, 26th August, 2016 @ 17:12:16

Test: Background 127574-2 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-2		Friday, 26th August, 2016		Sean Sullivan		Sean Sullivan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				23		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro		Graticule Dia mm									
1016		1		MS45		100									
						Test Slide Result Grid									
						Filter Dia Exposed mm									
						5									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS52		FM102		FM103		5739									
						SM41									
Sample Details															
Sample No	Sample Location	Head No	Pump No	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-2-1	Adjacent to trial pit RTP26	199	10	08:36:00	09:10:00	34	15.1		15.1	513	513	0.5	200	0.000	<0.01
127574-2-2	Adjacent to trial pit RTP28	01	164	09:10:00	09:44:00	34	15.1		15.1	513	513	2.0	200	0.001	<0.01
127574-2-3	Adjacent to trial pit RTP27	189	164	09:53:00	10:27:00	34	15.1		15.1	513	513	0.5	200	0.000	<0.01
127574-2-4	Adjacent to trial pit RTP29	189	10	12:00:00	12:34:00	34	15.1		15.1	513	513	0.5	200	0.000	<0.01
127574-2-5	Adjacent to trial pit RTP30	231	10	12:32:00	13:06:00	34	15.1		15.1	513	513	1.0	200	0.000	<0.01
127574-2-6	Adjacent to trial pit RTP24	199	164	13:13:00	13:47:00	34	15.1		15.1	513	513	1.0	200	0.000	<0.01
127574-2-7	Adjacent to trial pit RTP23	250	148	13:55:00	14:29:00	34	15.1		15.1	513	513	1.0	200	0.000	<0.01

Test: Personal 127574-3

Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Friday, 26th August, 2016 @ 13:27:24

Test: Personal 127574-3 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-3		Friday, 26th August, 2016		Sean Sullivan		Sean Sullivan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				23		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1016		1		MS45		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS52		FM102		FM103		5739									
						Graticule Slide									
						SM41									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-3-1	On Operative Richard Harding during trial pit investigation RPT28	230	69	09:15:00	09:50:00	35	2.1		2.1	74	74	0.5	200	0.002	<0.06

Test: Background 127574-28

Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Wednesday, 14th September, 2016 @ 09:17:06
Additional notes	this air test lab background done within the earlier phase of works on nextgen. I could not delete it, hence I left it here.
Additional Photo 1	

Test: Background 127574-28 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-28		Wednesday, 14th September, 2016		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K			T Site C			T Pcal hPa									
293			23			1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1002		1		MS109		100									
						Test Slide Result Grid o									
						Filter Dia Exposed mm									
						5									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS264		FM111		FM190		222									
						Graticule Slide									
						SM748									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-28-1	lab within site office	301	1721	08:00:00	09:01:00	61	8.0		8.0	488	488	2.0	200	0.001	<0.01

Asbestos Analyst's Certificate Report

Job Ref No 000000, Cert Ref No 000000, Account Ref No 000000, Contract Ref No 000000

St Edwards Homes, Green Park Village, Reading, RG30 3UR



Photo Not Available



on site photo

Building	Level	Works-Area	Enclosure Used	Certificate Issue Date
Berkeley Homes - Green Park Village	0	Phase 5 East Earthworks	No	Tuesday, 20th September, 2016

Overall Certificate Status	Passed Tests	Failed Tests	WARNINGS
PASSED	0	0	0

Intro

This certificate is for the attention of

Andrew West
Berkeley Homes (Western) Limited
200 Longwater Avenue Green Park Reading Berkshire RG2 6GB

Sampling & Evaluation methods

In-house methods TOP02.08 & TOP02.09 in accordance with HSG 248 Asbestos - The Analyst's Guide to Sampling, Analysis and Clearance Procedures.

Notes: The samples referred to in this report will be retained for 6 months unless requested otherwise. Unless otherwise stated, there are no departures from the sampling and evaluation methods specified. Results detailed in this report relate only to the time, and corresponding conditions prevailing, when the sampling and examination were undertaken.

Notes to Test Accuracy

Airflow measured on site is recorded against a correction chart. Flow meters are calibrated against a UKAS certified master flow meter accurate to $\pm 0.5\%$. In accordance with HSG248, if the combined effect of ambient temperature and pressure between calibration and sampling location exceeds 5% a correction is applied to the air sample volume. The calculated fibre concentration is given for each air sample taken. Where the corresponding reported fibre concentration is preceded by "<", the lower limit of quantification (LOQ) of the method has not been reached. For a 480 litre air sample with 200 graticule areas counted, the (LOQ) of this method is 0.010 fibres per cubic centimetre of air; samples of less volume/graticules will be reported to a lower LOQ (refer count sheet). While counting randomly distributed fibres, an expected degree of variation of 1.5 standard deviations from the mean count may occur. At clearance indicator level (0.01 fibres per cubic centimetre of air) a 480-litre air sample yielding a count of 20 fibres over 200 fields would have an expected standard deviation of ± 8 fibres.

Sampling

When testing within an Enclosure and conducting a 4-Stage Clearance - the number of samples (Ns) is calculated by $A^{1/3}-1$. Where enclosure is less than 3m in height: A is denoted by area. Where enclosure is greater than 3m in height: A is denoted by volume/3. Refer air sampling and fibre counting sheet.

When testing within a decontamination unit (DCU) - where the combined floor area of shower and dirty areas is less than 10m²; 1 air test has been carried out. During this test the door between these areas has been propped open. For combined floor areas exceeding 10m² a sample in each area (i.e. shower and dirty end) will be taken.

For tests other than those associated with 4-Stage Clearance testing the analyst will apply the principles of current HSE guidance and experience combined with situational circumstances.

Where a photograph of the completed decontamination unit certificate appears in this report the analyst has completed an abridged report to be left inside the DCU; this abridged report should not be used in lieu of this comprehensive report.

Where sampling plans have been supplied; please note these are not to scale.

Where a sample filter has been deemed uncountable or biased the analyst will record this as "uncountable" in the count-sheet.

Field Blanks - Where site sampling and counting is carried out in a field laboratory a field blank is carried out by the analyst prior to the start of sampling and counting. The field blank constitutes a filter taken from a loaded but unused filter head that is mounted in the usual way and assigned a sample number which is recorded on the slide and the count sheet. Following sampling and analysis of the air tests, the results shall be assessed; where low counts ($<0.01 \text{ fcm}^{-3}$) are obtained from some of the field samples, analysis of the field blank will not be necessary. Where elevated counts ($>0.01 \text{ fcm}^{-3}$) are obtained on all field samples, then the field blank must be counted to exclude the possibility of contamination.

Disclaimers

Any opinions and interpretations expressed herein are outside the scope of UKAS accreditation. This certificate is valid only when it bears the signature of an authorised member of Lucion personnel. Please note the witnessing of smoke tests is outwith the scope of UKAS accreditation.

Representatives Signature - The signatory on report acknowledgement agrees to findings of this report being accurate and correct and Lucion Environmental Ltd issuing this report to the email address held on record for the job and does not require a copy of this report to be left on site. Furthermore Lucion Environmental Ltd cannot be held responsible for any actions undertaken following the issue of this report.

This certificate ☐ a ☐ be part of a series of works and should be read in conjunction with the Asbestos Analyst's Job Summary Report.

Report Contents

Test: Personal (127574-36)	7
Sample: On Operative Richard Harding during turning of soil (127574-36-1)	8
Sample: On Operative Will Betson during turning of soil (127574-36-2)	8
Test: Background (127574-37)	9
Sample: Perimeter of Phase 5 East Earthworks - Upwind NE (127574-37-1)	11
Sample: Perimeter of Phase 5 East Earthworks plan - near work area (127574-37-2)	11
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NW (127574-37-3)	11
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NW (127574-37-4)	11
Sample: Field Blank (127574-37-5)	11
Test: Background (127574-38)	12
Sample: Perimeter of Phase 5 East Earthworks plan - Upwind NE (127574-38-1)	14
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NW (127574-38-2)	14
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NW (127574-38-3)	14
Sample: Perimeter of Phase 5 East Earthworks plan - Upwind NE (127574-38-4)	14
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NW (127574-38-5)	14
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NW (127574-38-6)	14
Sample: Perimeter of Phase 5 East Earthworks plan - Upwind NE (127574-38-7)	14
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NW (127574-38-8)	14
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NW (127574-38-9)	14
Sample: Field Blank (127574-38-10)	14
Test: Background (127574-39)	16
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NE (127574-39-1)	18
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NE (127574-39-2)	18
Sample: Perimeter of Phase 5 East Earthworks plan - Upwind NW (127574-39-3)	18
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NE (127574-39-4)	18
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NE (127574-39-5)	18
Sample: Perimeter of Phase 5 East Earthworks plan - Upwind NW (127574-39-6)	18
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NE (127574-39-7)	18
Sample: Perimeter of Phase 5 East Earthworks plan - Upwind NW (127574-39-8)	18
Sample: Field Blank (127574-39-9)	18
Test: Personal (127574-40)	20

Sample: On Operative Gavin during soil levelling (127574-40-1)	21
Test: Background (127574-41)	22
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NE (127574-41-1)	24
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NE (127574-41-2)	24
Sample: Perimeter of Phase 5 East Earthworks plan - Upwind NW (127574-41-3)	24
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NE (127574-41-4)	24
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NE (127574-41-5)	24
Sample: Perimeter of Phase 5 East Earthworks plan - Upwind NW (127574-41-6)	24
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NE (127574-41-7)	24
Sample: Perimeter of Phase 5 East Earthworks plan - Downwind NE (127574-41-8)	24
Sample: Perimeter of Phase 5 East Earthworks plan - Upwind NW (127574-41-9)	24
Sample: Field Blank (127574-41-10)	24
Test: Personal (127574-42)	26
Sample: On Operative Jorn during earthworks (127574-42-1)	27
Sample: On Operative Richard Harding during earthworks (127574-42-2)	27
Sample: On Operative Will Betson during earthworks (127574-42-3)	27
Test: Background (127574-43)	28
Sample: Field Blank (127574-43-1)	29
Sample: Adjacent dcu (127574-43-2)	29
Sample: East side of soil perimeter (127574-43-3)	29
Sample: South side of soil perimeter (127574-43-4)	29
Sample: West side of soil perimeter (127574-43-5)	29
Sample: Adjacent dcu (127574-43-6)	29
Sample: East side of soil perimeter (127574-43-7)	29
Sample: South side soil perimeter (127574-43-8)	29
Sample: South west soil perimeter (127574-43-9)	29
Test: Background (127574-44)	30
Sample: Adjacent dcu (127574-44-1)	31
Sample: South east perimeter of soil (127574-44-2)	31
Sample: South side perimeter of soil (127574-44-3)	31
Sample: West of perimeter of soil (127574-44-4)	31
Sample: Field Blank (127574-44-5)	31
Sample: Adjacent dcu (127574-44-6)	31
Sample: North side of perimeter (127574-44-7)	31

Sample: East side of perimeter soil (127574-44-8)	31
Sample: South side of soil perimeter (127574-44-9)	31
Test: Background (127574-45)	32
Sample: North side perimeter to soil (127574-45-1)	33
Sample: Adjacent DCU (127574-45-2)	33
Sample: South side perimeter to soil (127574-45-3)	33
Sample: East side perimeter to soil (127574-45-4)	33
Sample: Field Blank (127574-45-5)	33
Sample: East side perimeter to soil (127574-45-6)	33
Sample: South side perimeter to soil (127574-45-7)	33
Sample: Adjacent dcu (127574-45-8)	33
Sample: North side perimeter to soil (127574-45-9)	33
Test: Background (127574-46)	34
Sample: North east side of perimeter to soil (127574-46-1)	35
Sample: East side perimeter to soil (127574-46-2)	35
Sample: South east perimeter to soil (127574-46-3)	35
Sample: South perimeter to soil (127574-46-4)	35
Sample: Field Blank (127574-46-5)	35
Sample: North side perimeter to soil (127574-46-6)	35
Sample: East side perimeter to soil (127574-46-7)	35
Sample: South side perimeter to soil (127574-46-8)	35
Sample: South east side perimeter to soil (127574-46-9)	35

Test: Personal 127574-36

Number of samples being taken	2
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 20th September, 2016 @ 14:09:11

Test: Personal 127574-36 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-36		Tuesday, 20th September, 2016		Promise Alioha		Promise Alioha									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				21		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro		Graticule Dia mm									
1012		1		MS048		100									
Test Slide Result Grid		Filter Dia Exposed mm		5		22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS086		FM170		FM091		304									
Graticule Slide		SM737													
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
		mm	mm	hh:mm	hh:mm	mins	lmin-1	lmin-1	lmin-1	l	l			Fibres cm ⁻³	Fibres cm ⁻³
127574-36-1	On Operative Richard Harding during turning of soil	704	490	13:04:00	14:12:00	68	2.0		2.0	136	136	1.0	100	0.004	<0.07
127574-36-2	On Operative Will Betson during turning of soil	611	790	11:50:00	12:58:00	68	2.0		2.0	136	136	2.0	100	0.007	<0.07

Test: Background 127574-37

Number of samples being taken	5
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 20th September, 2016 @ 14:23:19
Additional Photo 1	 Background air monitoring Upwind
Additional Photo 2	 Background air monitoring downwind

[table continued from previous page...](#)

Additional Photo 3



Background air monitoring downwind

Additional Photo 4



Site plan showing sample locations

Test: Background 127574-37 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-37		Tuesday, 20th September, 2016		Promise Alioha		Promise Alioha									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				21		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro		Graticule Dia mm									
1012		1		MS048		100									
						Test Slide Result Grid									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS086		FM170		FM091		304									
						Graticule Slide									
						SM737									
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
		o	o	hh:mm	hh:mm	mins	lmin-1	lmin-1	lmin-1	l	l			Fibres cm ³	Fibres cm ³
127574-37-1	Perimeter of Phase 5 East Earthworks - Upwind NE	628	182	11:55:00	13:03:00	68	8.0		8.0	544	544	1.5	200	0.001	<0.01
127574-37-2	Perimeter of Phase 5 East Earthworks plan - near work area	705	1657	11:56:00	13:05:00	69	8.0		8.0	552	552	2.0	200	0.001	<0.01
127574-37-3	Perimeter of Phase 5 East Earthworks plan - Downwind NW	706	1882	12:06:00	13:12:00	66	8.0		8.0	528	528	2.0	200	0.001	<0.01
127574-37-4	Perimeter of Phase 5 East Earthworks plan - Downwind NW	643	442	12:07:00	13:13:00	66	8.0		8.0	528	528	2.0	200	0.001	<0.01
127574-37-5	Field Blank	704													

Test: Background 127574-38

Number of samples being taken	10
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Wednesday, 21st September, 2016 @ 11:03:00
Additional Photo 1	 Background air monitoring - NE Upwind
Additional Photo 2	 Background air monitoring - NW downwind


[table continued from previous page...](#)

Additional Photo 3



Background air monitoring - NW downwind

Additional Photo 4

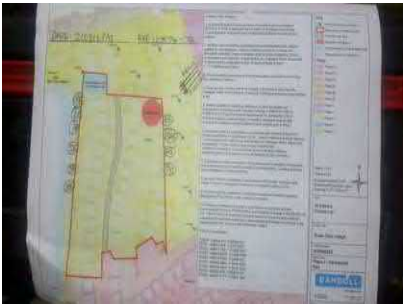

Site plan showing sample locations

Test: Background 127574-38 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-38		Wednesday, 21st September, 2016		Promise Alioha		Promise Alioha									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				20		1013									
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro o	Graticule Dia mm		Test Slide Result Grid o	Filter Dia Exposed mm									
1011	1	MS048	100		5	22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS086		FM170		FM091		304									
Graticule Slide															
SM737															
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-38-1	Perimeter of Phase 5 East Earthworks plan - Upwind NE	611	331	08:27:00	09:33:00	66	8.0		8.0	528	528	2.0	200	0.001	<0.01
127574-38-2	Perimeter of Phase 5 East Earthworks plan - Downwind NW	628	182	08:30:00	09:37:00	67	8.0		8.0	536	536	3.0	200	0.001	<0.01
127574-38-3	Perimeter of Phase 5 East Earthworks plan - Downwind NW	705	1885	08:32:00	09:38:00	66	8.0		8.0	528	528	3.0	200	0.001	<0.01
127574-38-4	Perimeter of Phase 5 East Earthworks plan - Upwind NE	611	331	11:17:00	12:27:00	70	8.0		8.0	560	560	2.0	200	0.001	<0.01
127574-38-5	Perimeter of Phase 5 East Earthworks plan - Downwind NW	628	182	11:20:00	12:30:00	70	8.0		8.0	560	560	3.0	200	0.001	<0.01
127574-38-6	Perimeter of Phase 5 East Earthworks plan - Downwind NW	706	442	11:22:00	12:31:00	69	8.0		8.0	552	552	3.0	200	0.001	<0.01
127574-38-7	Perimeter of Phase 5 East Earthworks plan - Upwind NE	643	1657	13:45:00	14:50:00	65	8.0		8.0	520	520	1.5	200	0.001	<0.01
127574-38-8	Perimeter of Phase 5 East Earthworks plan - Downwind NW	704	1882	13:48:00	14:55:00	67	8.0		8.0	536	536	2.0	200	0.001	<0.01

[table continued from previous table...](#)

Sample Details															
127574-38-9	Perimeter of Phase 5 East Earthworks plan - Downwind NW	706	442	13:49:00	14:56:00	67	8.0		8.0	536	536	2.0	200	0.001	<0.01
127574-38-10	Field Blank	704													

Test: Background 127574-39

Number of samples being taken	9
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Thursday, 22nd September, 2016 @ 08:42:40
Additional Photo 1	 Background air monitoring during earthworks
Additional Photo 2	 Background air monitoring during earthworks

[table continued from previous page...](#)

Additional Photo 3



Background air monitoring during earthworks

Additional Photo 4



Site plan showing sample locations

Test: Background 127574-39 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-39		Thursday, 22nd September, 2016		Promise Alioha		Promise Alioha									
Air Volume Correction Detail															
T Cal °K				T Site °C		T Pcal hPa									
293				18		1013									
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro	Graticule Dia mm	Test Slide Result Grid	Filter Dia Exposed mm										
1012	1	MS048	100	5	22.5										
Instrument Detail															
Thermometer, Barometer, Timepiece	Flow Hi	Flow Low	HSE PL	Graticule Slide											
WS086	FM170	FM091	304	SM737											
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
		mm	mm	hh:mm	hh:mm	mins	lmin-1	lmin-1	lmin-1	l	l			Fibres cm ⁻³	Fibres cm ⁻³
127574-39-1	Perimeter of Phase 5 East Earthworks plan - Downwind NE	611	331	08:43:00	09:49:00	66	8.0		8.0	528	528	2.5	200	0.001	<0.01
127574-39-2	Perimeter of Phase 5 East Earthworks plan - Downwind NE	628	182	08:44:00	09:50:00	66	8.0		8.0	528	528	2.0	200	0.001	<0.01
127574-39-3	Perimeter of Phase 5 East Earthworks plan - Upwind NW	705	1885	08:46:00	09:53:00	67	8.0		8.0	536	536	1.5	200	0.001	<0.01
127574-39-4	Perimeter of Phase 5 East Earthworks plan - Downwind NE	611	331	11:07:00	12:14:00	67	8.0		8.0	536	536	2.0	200	0.001	<0.01
127574-39-5	Perimeter of Phase 5 East Earthworks plan - Downwind NE	628	182	11:08:00	12:14:00	66	8.0		8.0	528	528	2.0	200	0.001	<0.01
127574-39-6	Perimeter of Phase 5 East Earthworks plan - Upwind NW	706	1885	11:12:00	12:17:00	65	8.0		8.0	520	520	1.5	200	0.001	<0.01
127574-39-7	Perimeter of Phase 5 East Earthworks plan - Downwind NE	628	442	13:37:00	14:45:00	68	8.0		8.0	544	544	2.5	200	0.001	<0.01
127574-39-8	Perimeter of Phase 5 East Earthworks plan - Upwind NW	643	1885	13:40:00	14:48:00	68	8.0		8.0	544	544	1.0	200	0.000	<0.01
127574-39-9	Field Blank	705													

Test: Personal 127574-40

Number of samples being taken	1
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Thursday, 22nd September, 2016 @ 15:21:22

Test: Personal 127574-40 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-40		Thursday, 22nd September, 2016		Promise Alioha		Promise Alioha									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				29		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1011		1		MS048		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS086		FM170		FM091		304									
						Graticule Slide									
						SM737									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-40-1	On Operative Gavin during soil levelling	704	490	14:55:00	15:55:00	60	2.0		2.0	120	120	2.0	100	0.008	<0.08

Test: Background 127574-41

Number of samples being taken	10
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Friday, 23rd September, 2016 @ 08:31:57
Additional Photo 1	 Background air monitoring during earthworks
Additional Photo 2	 Background air monitoring during earthworks

[table continued from previous page...](#)

Additional Photo 3



Background air monitoring during earthworks

Additional Photo 4



Site plan showing sample locations

Test: Background 127574-41 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-41		Friday, 23rd September, 2016		Promise Alioha		Promise Alioha									
Air Volume Correction Detail															
T Cal °K				T Site °C		T Pcal hPa									
293				18		1013									
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro	Graticule Dia mm	Test Slide Result Grid	Filter Dia Exposed mm										
1018	1	MS048	100	5	22.5										
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS086		FM170		FM091		304									
Graticule Slide															
SM737															
Sample Details															
Sample No	Sample Location	Head No	Pump No	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-41-1	Perimeter of Phase 5 East Earthworks plan - Downwind NE	611	331	08:04:00	09:12:00	68	8.0		8.0	544	544	3.0	200	0.001	<0.01
127574-41-2	Perimeter of Phase 5 East Earthworks plan - Downwind NE	705	1885	08:07:00	09:15:00	68	8.0		8.0	544	544	2.5	200	0.001	<0.01
127574-41-3	Perimeter of Phase 5 East Earthworks plan - Upwind NW	643	1667	08:11:00	09:19:00	68	8.0		8.0	544	544	1.5	200	0.001	<0.01
127574-41-4	Perimeter of Phase 5 East Earthworks plan - Downwind NE	611	331	09:50:00	10:59:00	69	8.0		8.0	552	552	2.0	200	0.001	<0.01
127574-41-5	Perimeter of Phase 5 East Earthworks plan - Downwind NE	628	182	09:52:00	11:02:00	70	8.0		8.0	560	560	2.0	200	0.001	<0.01
127574-41-6	Perimeter of Phase 5 East Earthworks plan - Upwind NW	706	1882	09:57:00	11:06:00	69	8.0		8.0	552	552	1.0	200	0.000	<0.01
127574-41-7	Perimeter of Phase 5 East Earthworks plan - Downwind NE	705	1657	11:49:00	12:56:00	67	8.0		8.0	536	536	3.0	200	0.001	<0.01
127574-41-8	Perimeter of Phase 5 East Earthworks plan - Downwind NE	643	442	11:50:00	12:58:00	68	8.0		8.0	544	544	3.0	200	0.001	<0.01

table continued from previous table...

Sample Details															
127574-41-9	Perimeter of Phase 5 East Earthworks plan - Upwind NW	706	1885	11:53:00	13:02:00	69	8.0		8.0	552	552	1.0	200	0.000	<0.01
127574-41-10	Field Blank	704													

Test: Personal 127574-42

Number of samples being taken	3
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Friday, 23rd September, 2016 @ 08:35:39

Test: Personal 127574-42 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-42		Friday, 23rd September, 2016		Promise Alioha		Promise Alioha									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				18		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1018		1		MS048		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS086		FM170		FM091		304									
						Graticule Slide									
						SM737									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-42-1	On Operative Jorn during earthworks	704	490	08:36:00	09:36:00	60	2.0		2.0	120	120	2.0	100	0.008	<0.08
127574-42-2	On Operative Richard Harding during earthworks	704	490	09:48:00	11:48:00	120	2.0		2.0	240	240	2.0	100	0.004	<0.04
127574-42-3	On Operative Will Betson during earthworks	704	490	12:10:00	13:23:00	73	2.0		2.0	146	146	3.0	100	0.010	<0.01

Test: Background 127574-43

Number of samples being taken	8
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No

Test: Background 127574-43 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-43		Monday, 26th September, 2016		Jonathan Bolton		Jonathan Bolton									
Air Volume Correction Detail															
T Cal K			T Site C			T Pcal hPa									
293			12			1013									
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro	Graticule Dia mm	Test Slide Result Grid	Filter Dia Exposed mm										
1021	1	MS07	100	5	22.5										
Instrument Detail															
Thermometer, Barometer, Timepiece	Flow Hi	Flow Low	HSE PL	Graticule Slide											
WS079	FM118	FM120	392	SM724											
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
127574-43-1	Field Blank	13													
127574-43-2	Adjacent dcu	858	1872	08:35:00	10:35:00	120	8.0		8.0	960	960	1.5	100	0.001	<0.01
127574-43-3	East side of soil perimeter	87	1874	08:38:00	10:38:00	120	8.0		8.0	960	960	1.0	100	0.001	<0.01
127574-43-4	South side of soil perimeter	859	1876	08:43:00	10:43:00	120	8.0		8.0	960	960	1.0	100	0.001	<0.01
127574-43-5	West side of soil perimeter	791	1877	08:44:00	10:44:00	120	8.0		8.0	960	960	1.0	100	0.001	<0.01
127574-43-6	Adjacent dcu	87	1872	11:41:00	13:41:00	120	8.0		8.0	960	960	1.0	100	0.001	<0.01
127574-43-7	East side of soil perimeter	859	1874	11:42:00	13:42:00	120	8.0		8.0	960	960	1.5	100	0.001	<0.01
127574-43-8	South side soil perimeter	858	1876	11:44:00	13:44:00	120	8.0		8.0	960	960	1.0	100	0.001	<0.01
127574-43-9	South west soil perimeter	791	1877	11:46:00	13:46:00	120	8.0		8.0	960	960	1.0	100	0.001	<0.01

Test: Background 127574-44

Number of samples being taken	9
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
	Site plan 27/9/16

Test: Background 127574-44 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-44		Tuesday, 27th September, 2016		Jonathan Bolton		Jonathan Bolton									
Air Volume Correction Detail															
T Cal K		T Site C		T Pcal hPa											
293		14		1013											
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro	Graticule Dia mm	Test Slide Result Grid		Filter Dia Exposed mm									
1021	1	MS07	100	5		22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS079		FM118		FM120		392									
Graticule Slide															
SM724															
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
		mm	mm	hh:mm	hh:mm	mins	lmin-1	lmin-1	lmin-1	ml	ml			Fibres cm ⁻³	Fibres cm ⁻³
127574-44-1	Adjacent dcu	859	1874	09:10:00	11:10:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01
127574-44-2	South east perimeter of soil	422	1875	09:11:00	11:11:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01
127574-44-3	South side perimeter of soil	13	1876	09:12:00	11:12:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01
127574-44-4	West of perimeter of soil	87	1877	09:14:00	11:14:00	120	8.0	8.0	8.0	960	960	1.5	100	0.001	<0.01
127574-44-5	Field Blank	791													
127574-44-6	Adjacent dcu	859	1872	12:00:00	14:00:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01
127574-44-7	North side of perimeter	422	1873	12:00:00	14:00:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01
127574-44-8	East side of perimeter soil	13	1874	12:02:00	14:02:00	120	8.0	8.0	8.0	960	960	1.5	100	0.001	<0.01
127574-44-9	South side of soil perimeter	87	1876	12:05:00	14:05:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01

Test: Background 127574-45

Number of samples being taken	9
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
	Site plan 28/09/16

Test: Background 127574-45 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-45		Wednesday, 28th September, 2016		Jonathan Bolton		Jonathan Bolton									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				12		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro		Graticule Dia mm									
1025		1		MS07		100									
						Test Slide Result Grid									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS795		FM118		FM120		392									
						Graticule Slide									
						SM724									
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
		mm	mm	hh:mm	hh:mm	mins	lmin-1	lmin-1	lmin-1	l	l			Fibres cm ⁻³	Fibres cm ⁻³
127574-45-1	North side perimeter to soil	13	1872	09:05:00	11:05:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01
127574-45-2	Adjacent DCU	87	1875	09:06:00	11:06:00	120	8.0	8.0	8.0	960	960	2.0	100	0.001	<0.01
127574-45-3	South side perimeter to soil	422	1876	09:08:00	11:08:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01
127574-45-4	East side perimeter to soil	859	1877	09:09:00	11:09:00	120	8.0	8.0	8.0	960	960	1.5	100	0.001	<0.01
127574-45-5	Field Blank	791													
127574-45-6	East side perimeter to soil	791	1877	11:33:00	13:33:00	120	8.0		8.0	960	960	1.0	100	0.001	<0.01
127574-45-7	South side perimeter to soil	858	1876	11:35:00	13:35:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01
127574-45-8	Adjacent dcu	87	1875	11:39:00	13:39:00	120	8.0	8.0	8.0	960	960	1.5	100	0.001	<0.01
127574-45-9	North side perimeter to soil	1872	13	11:41:00	13:41:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01

Test: Background 127574-46

Number of samples being taken	9
Air sample results	All air samples gave results below 0.02fibres per ccm of air.
Stage Warning?	No
	Site drawing 29/9/16

Test: Background 127574-46 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
127574-46		Thursday, 29th September, 2016		Jonathan Bolton		Jonathan Bolton									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				11		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1017		1		MS07		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS079		FM118		FM120		392									
						Graticule Slide									
						SM724									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
127574-46-1	North east side of perimeter to soil	87	1873	08:30:00	10:30:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01
127574-46-2	East side perimeter to soil	13	1874	08:32:00	10:32:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01
127574-46-3	South east perimeter to soil	858	1875	08:35:00	10:35:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01
127574-46-4	South perimeter to soil	791	1876	09:37:00	10:37:00	60	8.0	8.0	8.0	480	480	1.0	100	0.001	<0.02
127574-46-5	Field Blank	859													
127574-46-6	North side perimeter to soil	422	1873	10:55:00	12:55:00	120	8.0	8.0	8.0	960	960	1.5	100	0.001	<0.01
127574-46-7	East side perimeter to soil	13	1874	10:57:00	12:57:00	120	8.0	8.0	8.0	960	960	1.5	100	0.001	<0.01
127574-46-8	South side perimeter to soil	859	1876	10:57:00	12:57:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01
127574-46-9	South east side perimeter to soil	791	1875	10:58:00	12:58:00	120	8.0	8.0	8.0	960	960	1.0	100	0.001	<0.01

Asbestos Analyst's Job Summary Report

Job Ref No 00000000, Account Ref No 00000000, Contract Ref No 00000000

Nearest postcode is: RG30 3UR Refer to notes for directions

Time of day: 09:00, Air Monitoring during Phase 5 excavation works adjacent to stream.



on site photo

Passed Certificates	Failed Certificates
5	0

Site visit on 10th April, 2017, at 10:00 AM on Tuesday, 10th April, 2017

Intro

This document is a summary of findings relating to asbestos analytical works at **Nearest postcode is: RG30 3UR** **Refer to notes for directions** from **Monday, 10th April, 2017 to Tuesday, 2nd May, 2017**. It is intended to give an overview of testing and must be read only in conjunction with the certificates it references. The document should never be read in isolation as asbestos analysts reports often contain additional notes and advice that should be referred to.

Furthermore, this document contains a summary of analyst notes and comments made in relation to works at this site.

Please note this document may contain findings from more than one analyst on more than one date.

Key to Air-Test Icons

To aid ease of reading the following icons have been used in this document to reference commonly undertaken activities.

-  Clearance Stage 1
-  Clearance Stage 2
-  Clearance Stage 3
-  Clearance Stage 4
-  DCU Stage 2
-  DCU Stage 3
-  Reassurance
-  Background
-  Leak Testing
-  Personal
-  Smoke Test Witness
-  Report Acknowledgement

A **WARNING** is used by the analyst to draw the readers attention to a particular area of the report.

Overview of Works

To view a complete air-certificate, follow the relevant link

Certificate: phase 5

Building: green park village reading

Level: 0

View the Full Certificate Here: http://web.lucion.co.uk/air_cert/29915?s=ec2ab3296ba01d6e10a2c276d9f287a9

Type	Test-ID	Start Time	End Time	Date	Operative	# Samples	
 Reassurance	182918-10				 Aaron Garnett	1	
 Personal	182918-2			10-04-2017	 Kelvin Reynolds	1	
 Background	182918-1			10-04-2017	 Kelvin Reynolds	9	
 Personal	182918-4			11-04-2017	 Kelvin Reynolds	1	
 Reassurance	182918-3			11-04-2017	 Kelvin Reynolds	6	
 Personal	182918-5			11-04-2017	 Kelvin Reynolds	1	
 Personal	182918-7			12-04-2017	 Kelvin Reynolds	1	
 Reassurance	182918-6			12-04-2017	 Kelvin Reynolds	7	
 Personal	182918-9			13-04-2017	 Aaron Garnett	2	
 Reassurance	182918-8			13-04-2017	 Aaron Garnett	9	
 Reassurance	182918-11			19-04-2017	 Aaron Garnett	1	

Certificate: Phase 2

Building: green park village reading

Level: 0

View the Full Certificate Here: http://web.lucion.co.uk/air_cert/30155?s=dc804059ea4675e929ca1879f94ddcf3

Type	Test-ID	Start Time	End Time	Date	Operative	# Samples	
 Personal	182918-13			19-04-2017	 Aaron Garnett	1	
 Background	182918-13			19-04-2017	 Aaron Garnett	4	
 Reassurance	182918-14			19-04-2017	 Aaron Garnett	1	

Certificate: Phase 2		Building: The Green Park Village			Level: 0		Passed	
View the Full Certificate Here: http://web.lucion.co.uk/air_cert/30199?s=2b76d8b91da538395ff089d2548edb51								
Type	Test-ID	Start Time	End Time	Date	Operative	# Samples		
Personal	182918-15			20-04-2017	Mohammad Khan	1		
Background	182918-16			20-04-2017	Mohammad Khan	8		

Certificate:  North Lake Boundry area				Building: Green Park Village		Level: 0		Passed 	
View the Full Certificate Here: http://web.lucion.co.uk/air_cert/30267?s=15ccbdce7d18a78d88bf89d0008ed4fc									
Type		Test-ID	Start Time	End Time	Date	Operative		# Samples	
 Background		182918-18			21-04-2017	 Mohammad Khan		6	
 Personal		182918-17			21-04-2017	 Mohammad Khan		1	

Certificate: Phase 5

Building: Green Park Village Reading
RG12 3UR

Level: 0

Passed

View the Full Certificate Here: http://web.lucion.co.uk/air_cert/30334?s=d6fe1a17a420bac2629d7f306ce76de9

Type	Test-ID	Start Time	End Time	Date	Operative	# Samples	
Background	182918-19			24-04-2017	Mohammad Khan	5	
Personal	182918-20			25-04-2017	Mohammad Khan	2	
Background	182918-21			25-04-2017	Mohammad Khan	10	
Personal	182918-22			26-04-2017	Mohammad Khan	2	
Background	182918-23			26-04-2017	Mohammad Khan	9	
Personal	182918-24			27-04-2017	Mohammad Khan	2	
Background	182918-25			27-04-2017	Mohammad Khan	10	
Background	182918-27			28-04-2017	Mohammad Khan	9	
Personal	182918-26			28-04-2017	Mohammad Khan	2	
Reassurance	182918-31			02-05-2017	Kelvin Reynolds	4	

 Certificate: Envirograd SH400
Building: Green Park Village Reading
RG12 3UR

Level: 0

Passed View the Full Certificate Here: http://web.lucion.co.uk/air_cert/30481?s=53796bea9af0baf014490080ec929ce1

Type	Test-ID	Start Time	End Time	Date	Operative	# Samples	
 DCU Stage 2	182918-28	12:41:00	12:44:00	28-04-2017	 Mohammad Khan	--	Passed 
 DCU Stage 3	182918-29	12:46:00	14:09:00	28-04-2017	 Mohammad Khan	1	Passed 
 Report Acknowledgement	182918-30			28-04-2017	 Mohammad Khan	--	

 Certificate: DCU SH400
Building: Berkeley Homes - Green Park
Village

Level: 0

Passed View the Full Certificate Here: http://web.lucion.co.uk/air_cert/30537?s=c277cf7e837a14e809416e105a9d3f4f

Type	Test-ID	Start Time	End Time	Date	Operative	# Samples	
 DCU Stage 2	182918-32	12:10:00	12:16:00	02-05-2017	 Kelvin Reynolds	--	Passed 
 Report Acknowledgement	182918-34			02-05-2017	 Kelvin Reynolds	--	
 DCU Stage 3	182918-33	12:23:00	13:36:00	02-05-2017	 Kelvin Reynolds	1	Passed 

Job Notes

Operative	Note	Date
 Mohammad Khan Senior Analyst	It looks like that the work is not finished on Phase 5 area and they may need analyst on Tuesday 2nd May.	Friday, 28th April, 2017

Attachments

The following documents accompany this report and should be regarded as an integral part of this report.

They can be downloaded from <http://web.lucion.co.uk/reports/182918/attachments>.

- Method Statement [http://web.lucion.co.uk/method_statements/182918?s=bc361cdffb680826241aeba28d52bbf4]
- Risk Assessment [http://web.lucion.co.uk/risk_assessment/182918?s=b3d5ed62e1c01282fd6870c82684889c]

Asbestos Analyst's Certificate Report

Job Ref No 12345678, Cert Ref No 12345678, Account Ref No 12345678, Contract Ref No 12345678

St Edwards Homes, Green Park Village, Reading, RG30 3UR



on site photo



general works area photo

Building	Level	Works-Area	Enclosure Used
green park village reading	0	phase 5	No

Passed Tests	Failed Tests	WARNINGS
0	0	0

Intro

This certificate is for the attention of

Mr Martin Rutledge
Berkeley Homes (Western) Limited
200 Longwater Avenue Green Park Reading Berkshire RG2 6GB

Sampling and Evaluation methods

In-house methods TOP02.08 & TOP02.09 in accordance with HSG 248 Asbestos - The Analyst's Guide to Sampling, Analysis and Clearance Procedures.

Notes: The samples referred to in this report will be retained for 6 months unless requested otherwise. Unless otherwise stated, there are no departures from the sampling and evaluation methods specified. Results detailed in this report relate only to the time, and corresponding conditions prevailing, when the sampling and examination were undertaken.

Notes to Test Accuracy

Airflow measured on site is recorded against a correction chart. Flow meters are calibrated against a UKAS certified master flow meter accurate to $\pm 0.5\%$. In accordance with HSG248, if the combined effect of ambient temperature and pressure between calibration and sampling location exceeds 5% a correction is applied to the air sample volume. The calculated fibre concentration is given for each air sample taken. Where the corresponding reported fibre concentration is preceded by "<", the lower limit of quantification (LOQ) of the method has not been reached. For a 480 litre air sample with 200 graticule areas counted, the (LOQ) of this method is 0.010 fibres per cubic centimetre of air; samples of less volume/graticules will be reported to a lower LOQ (refer count sheet). While counting randomly distributed fibres, an expected degree of variation of 1.5 standard deviations from the mean count may occur. At clearance indicator level (0.01 fibres per cubic centimetre of air) a 480-litre air sample yielding a count of 20 fibres over 200 fields would have an expected standard deviation of ± 8 fibres.

Sampling

When testing within an Enclosure and conducting a 4-Stage Clearance - the number of samples (Ns) is calculated by $A^{1/3} - 1$. Where enclosure is less than 3m in height: A is denoted by area. Where enclosure is greater than 3m in height: A is denoted by volume/3. Refer air sampling and fibre counting sheet.

When testing within a decontamination unit (DCU) - where the combined floor area of shower and dirty areas is less than 10m²; 1 air test has been carried out. During this test the door between these areas has been propped open. For combined floor areas exceeding 10m² a sample in each area (i.e. shower and dirty end) will be taken.

For tests other than those associated with 4-Stage Clearance testing the analyst will apply the principles of current HSE guidance and experience combined with situational circumstances.

Where a photograph of the completed decontamination unit certificate appears in this report the analyst has completed an abridged report to be left inside the DCU; this abridged report should not be used in lieu of this comprehensive report.

Where sampling plans have been supplied; please note these are not to scale.

Where a sample filter has been deemed uncountable or biased the analyst will record this as "uncountable" in the count-sheet.

Field Blanks - Where site sampling and counting is carried out in a field laboratory a field blank is carried out by the analyst prior to the start of sampling and counting. The field blank constitutes a filter taken from a loaded but unused filter head that is mounted in the usual way and assigned a sample number which is recorded on the slide and the count sheet. Following sampling and analysis of the air tests, the results shall be assessed; where low counts ($<0.01 \text{ fcm}^{-3}$) are obtained from some of the field samples, analysis of the field blank will not be necessary. Where elevated counts ($>0.01 \text{ fcm}^{-3}$) are obtained on all field samples, then the field blank must be counted to exclude the possibility of contamination.

Disclaimers

Any opinions and interpretations expressed herein are outside the scope of UKAS accreditation. This certificate is valid only when it bears the signature of an authorised member of Lucion personnel. Please note the witnessing of smoke tests is outwith the scope of UKAS accreditation.

Representatives Signature - The signatory on report acknowledgement agrees to findings of this report being accurate and correct and Lucion Environmental Ltd issuing this report to the email address held on record for the job and does not require a copy of this report to be left on site. Furthermore Lucion Environmental Ltd cannot be held responsible for any actions undertaken following the issue of this report.

This certificate ☐ a ☐ be part of a series of works and should be read in conjunction with the Asbestos Analyst's Job Summary Report.

Report Contents

Test: Background (182918-1)	6
Sample: Field Blank (182918-1-1)	7
Sample: East side along perimeter fence (182918-1-2)	7
Sample: East side along perimeter fence (182918-1-3)	7
Sample: East side along perimeter fence (182918-1-4)	7
Sample: East side along perimeter fence (182918-1-5)	7
Sample: East side along perimeter fence. (182918-1-6)	7
Sample: East side along perimeter fence. (182918-1-7)	7
Sample: East side along perimeter fence. (182918-1-8)	7
Sample: East side along perimeter fence (182918-1-9)	7
Test: Personal (182918-2)	9
Sample: in fenced of area overwatching works (182918-2-1)	10
Test: Reassurance (182918-3)	11
Sample: south west corner of fence (182918-3-1)	12
Sample: south corner of fence (182918-3-2)	12
Sample: East along fence adjacent to works (182918-3-3)	12
Sample: East along fence adjacent to dcu (182918-3-4)	12
Sample: south west corner along fence (182918-3-5)	12
Sample: south corner of fence (182918-3-6)	12
Test: Personal (182918-4)	13
Sample: in side fenced area adjacent to 360 (182918-4-1)	14
Test: Personal (182918-5)	15
Sample: over watching works (182918-5-1)	16
Test: Reassurance (182918-6)	17
Sample: East side along perimeter fence (182918-6-1)	18
Sample: East side along perimeter fence. (182918-6-2)	18
Sample: East side along perimeter fence (182918-6-3)	18
Sample: East side along perimeter fence (182918-6-4)	18
Sample: East side along perimeter fence (182918-6-5)	18
Sample: East side along perimeter fence. (182918-6-6)	18
Sample: nerth end along fence (182918-6-7)	18

Test: Personal (182918-7)	19
Sample: driver of 360 (182918-7-1)	20
Test: Reassurance (182918-8)	21
Sample: southside of perimeter fence (182918-8-1)	22
Sample: southeast side of perimeter fence (182918-8-2)	22
Sample: eastern side of perimeter (182918-8-3)	22
Sample: eastern side of perimeter (182918-8-4)	22
Sample: eastern side of perimeter adjacent new soil location (182918-8-5)	22
Sample: adjacent DCU (182918-8-6)	22
Sample: eastern side of the perimeter (182918-8-7)	22
Sample: eastern side of the perimeter adjacent pile of soil (182918-8-8)	22
Sample: eastern side of the perimeter fence (182918-8-9)	22
Test: Personal (182918-9)	23
Sample: On Operative Chris dawson conducting a watch a brief (182918-9-1)	24
Sample: On Operative Figo frieghtf (182918-9-2)	24
Test: Reassurance (182918-10)	25
Sample: eastern boundary (182918-10-1)	26
Test: Reassurance (182918-11)	27
Sample: eastern perimeter adjacent soil heap (182918-11-1)	28

Test: Background 182918-1

Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Monday, 10th April, 2017 @ 16:54:25

Test: Background 182918-1 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-1		Monday, 10th April, 2017		Kelvin Reynolds		Kelvin Reynolds									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				19		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro		Graticule Dia mm									
1020		1		MS07		100									
						Test Slide Result Grid									
						5									
						Filter Dia Exposed mm									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS79		FM188		FM191		458									
						Graticule Slide									
						SM760									
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
no		no	no	hh:mm	hh:mm	mins	lmin-1	lmin-1	lmin-1	l	l			Fibres cm ⁻³	Fibres cm ⁻³
182918-1-1	Field Blank	986													
182918-1-2	East side along perimeter fence	982	1872	10:52:00	12:07:00	75	8.0		8.0	600	600	1.0	200	0.000	<0.01
182918-1-3	East side along perimeter fence	983	1771	10:53:00	12:08:00	75	8.0		8.0	600	600	1.0	200	0.000	<0.01
182918-1-4	East side along perimeter fence	984	1888	10:54:00	12:08:00	74	8.0		8.0	592	592	1.0	200	0.000	<0.01
182918-1-5	East side along perimeter fence	985	1879	10:55:00	12:09:00	74	8.0		8.0	592	592	1.0	200	0.000	<0.01
182918-1-6	East side along perimeter fence.	982	1872	12:57:00	13:57:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
182918-1-7	East side along perimeter fence.	983	1771	12:58:00	13:58:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
182918-1-8	East side along perimeter fence.	984	1888	12:59:00	13:59:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
182918-1-9	East side along perimeter fence	985	1879	12:59:00	13:59:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01

Test: Personal 182918-2

RPE used for works	Sundstrom SR100 P3 filter
Description of works / product removed	over watch
Asbestos Contractor	rambol
Client Representative or Contractor	Chris dawson
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Monday, 10th April, 2017 @ 16:28:47

Test: Personal 182918-2 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-2		Monday, 10th April, 2017		Kelvin Reynolds		Kelvin Reynolds									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				17		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1021		1		MS07		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS79		FM188		FM191		458									
						Graticule Slide									
						SM760									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ³	Report Conc Fibres cm ³
182918-2-1	in fenced of area overwatching works	986	503	14:09:00	14:33:00	24	2.0		2.0	48	48	2.0	100	0.020	<0.2

Test: Reassurance 182918-3

Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 11th April, 2017 @ 16:16:57

Test: Reassurance 182918-3 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-3		Tuesday, 11th April, 2017		Kelvin Reynolds		Kelvin Reynolds									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				16		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1022		1		MS07		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS79		FM188		FM191		458									
						Graticule Slide									
						SM760									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
182918-3-1	south west corner of fence	982	1879	09:42:00	10:58:00	76	8.0		8.0	608	608	1.0	200	0.000	<0.01
182918-3-2	south corner of fence	983	1888	09:44:00	10:59:00	75	8.0		8.0	600	600	1.0	200	0.000	<0.01
182918-3-3	East along fence adjacent to works	984	1872	09:45:00	10:59:00	74	8.0		8.0	592	592	1.0	200	0.000	<0.01
182918-3-4	East along fence adjacent to dcu	985	1771	09:45:00	11:00:00	75	8.0		8.0	600	600	1.0	200	0.000	<0.01
182918-3-5	south west corner along fence	982	1879	12:11:00	13:23:00	72	8.0		8.0	576	576	1.0	200	0.000	<0.01
182918-3-6	south corner of fence	983	1888	12:12:00	13:22:00	70	8.0		8.0	560	560	1.0	200	0.000	<0.01

Test: Personal 182918-4

RPE used for works	disposable mask
Description of works / product removed	banksman
Asbestos Contractor	wooldridge
Client Representative or Contractor	Jamie wilkinson
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 11th April, 2017 @ 16:16:00

Test: Personal 182918-4 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-4		Tuesday, 11th April, 2017		Kelvin Reynolds		Kelvin Reynolds									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				16		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1022		1		MS07		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS79		FM188		FM191		458									
						Graticule Slide									
						SM760									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
182918-4-1	in side fenced area adjacent to 360	986	503	12:26:00	13:09:00	43	2.0		2.0	86	86	0.0	100	0.000	<0.01

Test: Personal 182918-5

RPE used for works	Sundstrom SR100 P3 filter
Description of works / product removed	overwatch
Asbestos Contractor	rambol
Client Representative or Contractor	Chris dawson
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 11th April, 2017 @ 16:22:01

Test: Personal 182918-5 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-5		Tuesday, 11th April, 2017		Kelvin Reynolds		Kelvin Reynolds									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				16		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1022		1		MS07		100									
						Test Slide Result Grid o									
						Filter Dia Exposed mm									
						5									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS79		FM188		FM191		458									
						SM760									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
182918-5-1	over watching works	987	503	14:51:00	15:32:00	41	2.0		2.0	82	82	2.0	100	0.012	<0.12

Test: Reassurance 182918-6

Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Wednesday, 12th April, 2017 @ 16:40:14

Test: Reassurance 182918-6 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-6		Wednesday, 12th April, 2017		Kelvin Reynolds		Kelvin Reynolds									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				14		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1012		1		MS07		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS79		FM188		FM191		458									
						Graticule Slide									
						SM760									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
182918-6-1	East side along perimeter fence	982	1879	10:41:00	11:57:00	76	8.0		8.0	608	608	1.5	200	0.001	<0.01
182918-6-2	East side along perimeter fence.	983	1771	10:43:00	11:58:00	75	8.0		8.0	600	600	1.0	200	0.000	<0.01
182918-6-3	East side along perimeter fence	984	1888	10:44:00	11:59:00	75	8.0		8.0	600	600	1.0	200	0.000	<0.01
182918-6-4	East side along perimeter fence	985	1872	10:45:00	12:00:00	75	8.0		8.0	600	600	1.0	200	0.000	<0.01
182918-6-5	East side along perimeter fence	982	1888	14:36:00	15:36:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01
182918-6-6	East side along perimeter fence.	983	1872	14:38:00	15:38:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
182918-6-7	nerth end along fence	984	1771	14:39:00	15:39:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01

Test: Personal 182918-7

RPE used for works	disposable mask
Description of works / product removed	digging up contaminated soil
Asbestos Contractor	wooldridge
Client Representative or Contractor	joao freitas
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Wednesday, 12th April, 2017 @ 16:39:23

Test: Personal 182918-7 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-7		Wednesday, 12th April, 2017		Kelvin Reynolds		Kelvin Reynolds									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				16		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1011		1		MS07		100									
						5									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS79		FM188		FM191		458									
						SM760									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
182918-7-1	driver of 360	985	503	14:42:00	15:36:00	54	2.0		2.0	108	108	2.0	100	0.009	<0.09

Test: Reassurance 182918-8

Number of samples being taken	9
Air sample results	All final results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Thursday, 13th April, 2017 @ 16:30:47
Additional Photo 1	
Additional Photo 2	

Test: Reassurance 182918-8 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-8		Thursday, 13th April, 2017		Aaron Garnett		Aaron Garnett									
Air Volume Correction Detail															
T Cal (K)				T Site (C)		T Pcal (hPa)									
293				14		1013									
Microscope Calculation Detail															
P Site (hPa)		Correction Required		Micro (o)		Graticule Dia (mm)									
1011		1		MS90		100									
Test Slide Result (Grid (o))		Filter Dia (Exposed (mm))													
5		22.5													
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow (Hi)		Flow (Low)		HSE (PL)									
WS83		FM375		FM162		312									
Graticule Slide		SM754													
Sample Details															
Sample (o)	Sample Location	Head (o)	Pump (o)	Time On (hh:mm)	Time Off (hh:mm)	Run Time (mins)	Start Flow (lmin-1)	Int Flow (lmin-1)	End Flow (lmin-1)	Calc (Volume (l))	Corr (Volume (l))	Fibres	Fields	Calc (Conc (Fibres cm ⁻³))	Report (Conc (Fibres cm ⁻³))
182918-8-1	southside of perimeter fence	388	1873	10:28:00	11:28:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01
182918-8-2	southeast side of perimeter fence	727	1657	10:30:00	11:30:00	60	8.0		8.0	480	480	3.0	200	0.002	<0.01
182918-8-3	eastern side of perimeter	658	1657	12:43:00	13:43:00	60	8.0		8.0	480	480	3.0	200	0.002	<0.01
182918-8-4	eastern side of perimeter	727	1873	12:44:00	13:44:00	60	8.0		8.0	480	480	5.0	200	0.003	<0.01
182918-8-5	eastern side of perimeter adjacent new soil location	848	165	12:50:00	13:50:00	60	8.0		8.0	480	480	3.0	200	0.002	<0.01
182918-8-6	adjacent DCU	15	1885	12:52:00	13:52:00	60	8.0		8.0	480	480	3.0	200	0.002	<0.01
182918-8-7	eastern side of the perimeter	848	1657	15:10:00	16:10:00	60	8.0		8.0	480	480	3.0	200	0.002	<0.01
182918-8-8	eastern side of the perimeter adjacent pile of soil	500	165	15:10:00	16:10:00	60	8.0		8.0	480	480	1.0	200	0.001	<0.01
182918-8-9	eastern side of the perimeter fence	658	1873	15:12:00	16:12:00	60	8.0		8.0	480	480	3.0	200	0.002	<0.01

Test: Personal 182918-9

Number of samples being taken	2
RPE used for works	Sundstrom SR100 P3 filter
Description of works / product removed	watching brief
Asbestos Contractor	ramboll
Client Representative or Contractor	Chris dawson
Air sample results	All final results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Thursday, 13th April, 2017 @ 14:55:07

Test: Personal 182918-9 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-9		Thursday, 13th April, 2017		Aaron Garnett		Aaron Garnett									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				14		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1011		1		MS90		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS83		FM375		FM162		312									
						Graticule Slide									
						SM754									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
182918-9-1	On Operative Chris dawson conducting a watch a brief	500	416	10:35:00	11:05:00	30	2.0		8.0	150	150	1.0	100	0.003	<0.06
182918-9-2	On Operative Figo frieghtf	217	416	12:50:00	13:50:00	60	2.0		2.0	120	120	2.0	100	0.008	<0.08

Test: Reassurance 182918-10

Number of samples being taken

1

Test: Reassurance 182918-10 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-10				Aaron Garnett		Aaron Garnett									
Air Volume Correction Detail															
T Cal (K)				T Site (C)		T Pcal (hPa)									
293				14		1013									
Microscope Calculation Detail															
P Site (hPa)		Correction Required		Micro (o)		Graticule Dia (mm)									
1009		1		MS90		100									
						Test Slide Result (Grid (o))									
						5									
						Filter Dia (Exposed (mm))									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow (Hi)		Flow (Low)		HSE (PL)									
WS83		FM375		FM162		312									
						Graticule Slide									
						754									
Sample Details															
Sample (o)	Sample Location	Head (o)	Pump (o)	Time On (hh:mm)	Time Off (hh:mm)	Run Time (mins)	Start Flow (lmin-1)	Int Flow (lmin-1)	End Flow (lmin-1)	Calc Volume (l)	Corr Volume (l)	Fibres	Fields	Calc Conc (Fibres cm ⁻³)	Report Conc (Fibres cm ⁻³)
182918-10-1	eastern boundary	727	1885	13:46:00	14:46:00	60	8.0		8.0	480	480	3.0	200	0.002	<0.01

Test: Reassurance 182918-11

Number of samples being taken	1
Air sample results	All final results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Wednesday, 19th April, 2017 @ 12:17:05
Additional Photo 1	 11-1

Test: Reassurance 182918-11 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-11		Wednesday, 19th April, 2017		Aaron Garnett		Aaron Garnett									
Air Volume Correction Detail															
T Cal (K)				T Site (C)		T Pcal (hPa)									
293				4		1013									
Microscope Calculation Detail															
P Site (hPa)		Correction Required		Micro (o)		Graticule Dia (mm)									
1009		1		MS90		100									
						Test Slide Result (Grid (o))									
						5									
						Filter Dia (Exposed (mm))									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow (Hi)		Flow (Low)		HSE (PL)									
WS83		FM375		FM162		312									
						Graticule Slide									
						SM754									
Sample Details															
Sample (o)	Sample Location	Head (o)	Pump (o)	Time On (hh:mm)	Time Off (hh:mm)	Run Time (mins)	Start Flow (l/min-1)	Int Flow (l/min-1)	End Flow (l/min-1)	Calc Volume (l)	Corr Volume (l)	Fibres	Fields	Calc Conc (Fibres cm ⁻³)	Report Conc (Fibres cm ⁻³)
182918-11-1	eastern perimeter adjacent soil heap	15	153	08:50:00	09:50:00	60	8.0		8.0	480	480	4.0	200	0.002	<0.01

Asbestos Analyst's Certificate Report

Job Ref No 00000000, Cert Ref No 00000000, Account Ref No 00000000, Contract Ref No 00000000

St Edwards Homes, Green Park Village, Reading, RG30 3UR



on site photo



General works area photo

Building	Level	Works-Area	Enclosure Used	Certificate Issue Date
Green Park Village	0	North Lake Boundry area	No	Friday, 21st April, 2017

Overall Certificate Status	Passed Tests	Failed Tests	WARNINGS
PASSED	0	0	0

Intro

This certificate is for the attention of

Mr Martin Rutledge
Berkeley Homes (Western) Limited
200 Longwater Avenue Green Park Reading Berkshire RG2 6GB

Sampling and Evaluation methods

In-house methods TOP02.08 & TOP02.09 in accordance with HSG 248 Asbestos - The Analyst's Guide to Sampling, Analysis and Clearance Procedures.

Notes: The samples referred to in this report will be retained for 6 months unless requested otherwise. Unless otherwise stated, there are no departures from the sampling and evaluation methods specified. Results detailed in this report relate only to the time, and corresponding conditions prevailing, when the sampling and examination were undertaken.

Notes to Test Accuracy

Airflow measured on site is recorded against a correction chart. Flow meters are calibrated against a UKAS certified master flow meter accurate to $\pm 0.5\%$. In accordance with HSG248, if the combined effect of ambient temperature and pressure between calibration and sampling location exceeds 5% a correction is applied to the air sample volume. The calculated fibre concentration is given for each air sample taken. Where the corresponding reported fibre concentration is preceded by "<", the lower limit of quantification (LOQ) of the method has not been reached. For a 480 litre air sample with 200 graticule areas counted, the (LOQ) of this method is 0.010 fibres per cubic centimetre of air; samples of less volume/graticules will be reported to a lower LOQ (refer count sheet). While counting randomly distributed fibres, an expected degree of variation of 1.5 standard deviations from the mean count may occur. At clearance indicator level (0.01 fibres per cubic centimetre of air) a 480-litre air sample yielding a count of 20 fibres over 200 fields would have an expected standard deviation of ± 8 fibres.

Sampling

When testing within an Enclosure and conducting a 4-Stage Clearance - the number of samples (Ns) is calculated by $A^{1/3}-1$. Where enclosure is less than 3m in height: A is denoted by area. Where enclosure is greater than 3m in height: A is denoted by volume/3. Refer air sampling and fibre counting sheet.

When testing within a decontamination unit (DCU) - where the combined floor area of shower and dirty areas is less than 10m²; 1 air test has been carried out. During this test the door between these areas has been propped open. For combined floor areas exceeding 10m² a sample in each area (i.e. shower and dirty end) will be taken.

For tests other than those associated with 4-Stage Clearance testing the analyst will apply the principles of current HSE guidance and experience combined with situational circumstances.

Where a photograph of the completed decontamination unit certificate appears in this report the analyst has completed an abridged report to be left inside the DCU; this abridged report should not be used in lieu of this comprehensive report.

Where sampling plans have been supplied; please note these are not to scale.

Where a sample filter has been deemed uncountable or biased the analyst will record this as "uncountable" in the count-sheet.

Field Blanks - Where site sampling and counting is carried out in a field laboratory a field blank is carried out by the analyst prior to the start of sampling and counting. The field blank constitutes a filter taken from a loaded but unused filter head that is mounted in the usual way and assigned a sample number which is recorded on the slide and the count sheet. Following sampling and analysis of the air tests, the results shall be assessed; where low counts ($<0.01 \text{ fcm}^{-3}$) are obtained from some of the field samples, analysis of the field blank will not be necessary. Where elevated counts ($>0.01 \text{ fcm}^{-3}$) are obtained on all field samples, then the field blank must be counted to exclude the possibility of contamination.

Disclaimers

Any opinions and interpretations expressed herein are outside the scope of UKAS accreditation. This certificate is valid only when it bears the signature of an authorised member of Lucion personnel. Please note the witnessing of smoke tests is outwith the scope of UKAS accreditation.

Representatives Signature - The signatory on report acknowledgement agrees to findings of this report being accurate and correct and Lucion Environmental Ltd issuing this report to the email address held on record for the job and does not require a copy of this report to be left on site. Furthermore Lucion Environmental Ltd cannot be held responsible for any actions undertaken following the issue of this report.

This certificate ☐ **a** ☐ be part of a series of works and should be read in conjunction with the Asbestos Analyst's Job Summary Report.

Report Contents

Test: Personal (182918-17)5

 Sample: On Flori Pop while moving soil (182918-17-1)6

Test: Background (182918-18)7

 Sample: Adjacent to perimeter (182918-18-1)9

 Sample: Adjacent to perimeter (182918-18-2)9


 Sample: On the Perimeter (182918-18-3)9

 Sample: On the perimeter (182918-18-4)9

 Sample: On the Perimeter (182918-18-5)9

 Sample: Field Blank (182918-18-6)9

Test: Personal 182918-17

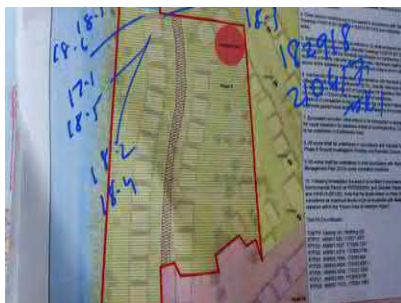Number of samples being taken	1
Description of works / product removed	Moving Soil
Asbestos Contractor	Wooldridge
Client Representative or Contractor	Flori Pop
Air sample results	All air samples gave results below 0.04 fibres per ccm of air.
Stage Warning?	No
Analyst Signature Signature Date	 Friday, 21st April, 2017 @ 12:26:04
Additional notes	satisfactory
Additional Photo 1	
Additional Photo 2	

Test: Personal 182918-17 - Count Sheet


Lucion Report Number		Test Date		Sampled By		Counted By									
182918-17		Friday, 21st April, 2017		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				12		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1027		1		MS059		100									
						Test Slide Result Grid o									
						Filter Dia Exposed mm									
						5									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS80		FM111		FM190		222									
						Graticule Slide									
						SM748									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
182918-17-1	On Flori Pop while moving soil	530	20	09:02:00	10:06:00	64	2.0		2.0	128	128	3.0	200	0.006	<0.04

Test: Background 182918-18

Number of samples being taken	6
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Friday, 21st April, 2017 @ 12:21:03
Additional notes	satisfactory
Additional Photo 1	
Additional Photo 2	

table continued from previous page...

Additional Photo 3

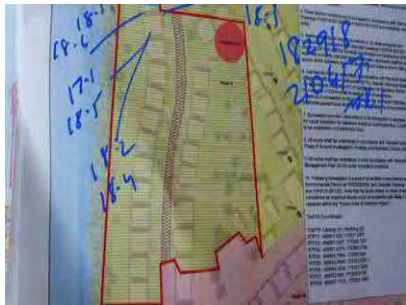

Test: Background 182918-18 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-18		Friday, 21st April, 2017		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				12		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro		Graticule Dia mm									
1027		1		MS059		100									
						Test Slide Result Grid									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS80		FM111		FM190		222									
						Graticule Slide									
						SM748									
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
				hh:mm	hh:mm	mins	lmin-1	lmin-1	lmin-1	l	l			Fibres cm ⁻³	Fibres cm ⁻³
182918-18-1	Adjacent to perimeter	80	1716	09:05:00	10:06:00	61	8.0		8.0	488	488	3.0	200	0.002	<0.01
182918-18-2	Adjacent to perimeter	301	1709	09:06:00	10:07:00	61	8.0		8.0	488	488	2.5	200	0.001	<0.01
182918-18-3	On the Perimeter	635	1716	10:43:00	11:44:00	61	8.0		8.0	488	488	2.0	200	0.001	<0.01
182918-18-4	On the perimeter	80	1709	10:45:00	11:46:00	61	8.0		8.0	488	488	1.5	200	0.001	<0.01
182918-18-5	On the Perimeter	324	1718	10:46:00	11:48:00	62	8.0		8.0	496	496	3.0	200	0.002	<0.01
182918-18-6	Field Blank	600										0.0	100		

Asbestos Analyst's Certificate Report

Job Ref No 000000, Cert Ref No 000000, Account Ref No 000000, Contract Ref No 000000

St Edwards Homes, Green Park Village, Reading, RG30 3UR



on site photo

Building	Level	Works-Area	Enclosure Used	Certificate Issue Date
Green Park Village Reading RG12 3UR	0	Phase 5	No	Tuesday, 2nd May, 2017

Overall Certificate Status	Passed Tests	Failed Tests	WARNINGS
PASSED	0	0	0

Intro

This certificate is for the attention of

Mr Martin Rutledge
Berkeley Homes (Western) Limited
200 Longwater Avenue Green Park Reading Berkshire RG2 6GB

Sampling and Evaluation methods

In-house methods TOP02.08 & TOP02.09 in accordance with HSG 248 Asbestos - The Analyst's Guide to Sampling, Analysis and Clearance Procedures.

Notes: The samples referred to in this report will be retained for 6 months unless requested otherwise. Unless otherwise stated, there are no departures from the sampling and evaluation methods specified. Results detailed in this report relate only to the time, and corresponding conditions prevailing, when the sampling and examination were undertaken.

Notes to Test Accuracy

Airflow measured on site is recorded against a correction chart. Flow meters are calibrated against a UKAS certified master flow meter accurate to $\pm 0.5\%$. In accordance with HSG248, if the combined effect of ambient temperature and pressure between calibration and sampling location exceeds 5% a correction is applied to the air sample volume. The calculated fibre concentration is given for each air sample taken. Where the corresponding reported fibre concentration is preceded by "<", the lower limit of quantification (LOQ) of the method has not been reached. For a 480 litre air sample with 200 graticule areas counted, the (LOQ) of this method is 0.010 fibres per cubic centimetre of air; samples of less volume/graticules will be reported to a lower LOQ (refer count sheet). While counting randomly distributed fibres, an expected degree of variation of 1.5 standard deviations from the mean count may occur. At clearance indicator level (0.01 fibres per cubic centimetre of air) a 480-litre air sample yielding a count of 20 fibres over 200 fields would have an expected standard deviation of ± 8 fibres.

Sampling

When testing within an Enclosure and conducting a 4-Stage Clearance - the number of samples (Ns) is calculated by $A^{1/3} - 1$. Where enclosure is less than 3m in height: A is denoted by area. Where enclosure is greater than 3m in height: A is denoted by volume/3. Refer air sampling and fibre counting sheet.

When testing within a decontamination unit (DCU) - where the combined floor area of shower and dirty areas is less than 10m²; 1 air test has been carried out. During this test the door between these areas has been propped open. For combined floor areas exceeding 10m² a sample in each area (i.e. shower and dirty end) will be taken.

For tests other than those associated with 4-Stage Clearance testing the analyst will apply the principles of current HSE guidance and experience combined with situational circumstances.

Where a photograph of the completed decontamination unit certificate appears in this report the analyst has completed an abridged report to be left inside the DCU; this abridged report should not be used in lieu of this comprehensive report.

Where sampling plans have been supplied; please note these are not to scale.

Where a sample filter has been deemed uncountable or biased the analyst will record this as "uncountable" in the count-sheet.

Field Blanks - Where site sampling and counting is carried out in a field laboratory a field blank is carried out by the analyst prior to the start of sampling and counting. The field blank constitutes a filter taken from a loaded but unused filter head that is mounted in the usual way and assigned a sample number which is recorded on the slide and the count sheet. Following sampling and analysis of the air tests, the results shall be assessed; where low counts ($<0.01 \text{ fcm}^{-3}$) are obtained from some of the field samples, analysis of the field blank will not be necessary. Where elevated counts ($>0.01 \text{ fcm}^{-3}$) are obtained on all field samples, then the field blank must be counted to exclude the possibility of contamination.

Disclaimers

Any opinions and interpretations expressed herein are outside the scope of UKAS accreditation. This certificate is valid only when it bears the signature of an authorised member of Lucion personnel. Please note the witnessing of smoke tests is outwith the scope of UKAS accreditation.

Representatives Signature - The signatory on report acknowledgement agrees to findings of this report being accurate and correct and Lucion Environmental Ltd issuing this report to the email address held on record for the job and does not require a copy of this report to be left on site. Furthermore Lucion Environmental Ltd cannot be held responsible for any actions undertaken following the issue of this report.

This certificate ☐ a ☐ be part of a series of works and should be read in conjunction with the Asbestos Analyst's Job Summary Report.

Report Contents

Test: Background (182918-19)	7
Sample: Adjacent to Perimeter (182918-19-1)	9
Sample: Adjacent to Perimeter (182918-19-2)	9
Sample: Adjacent to Perimeter (182918-19-3)	9
Sample: Adjacent to Perimeter (182918-19-4)	9
Sample: Field Blank (182918-19-5)	9
Test: Personal (182918-20)	10
Sample: On Chris Dawson as operative watering down (182918-20-1)	12
Sample: On Clive Curran Digger Operator (182918-20-2)	12
Test: Background (182918-21)	13
Sample: Adjacent to perimeter (182918-21-1)	15
Sample: Adjacent to Perimeter (182918-21-2)	15
Sample: Adjacent to Perimeter (182918-21-3)	15
Sample: Adjacent to Perimeter (182918-21-4)	15
Sample: Adjacent to Perimeter (182918-21-5)	15
Sample: Adjacent to Perimeter (182918-21-6)	15
Sample: Adjacent to perimeter (182918-21-7)	15
Sample: Adjacent to Perimeter (182918-21-8)	15
Sample: Adjacent to Perimeter (182918-21-9)	15
Sample: Field Blank (182918-21-10)	15
Test: Personal (182918-22)	17
Sample: On Chris Dawson spraying adjacent to soil moving (182918-22-1)	19
Sample: On Clive Curran Machine operator (182918-22-2)	19
Test: Background (182918-23)	20
Sample: Adjacent to Perimeter (182918-23-1)	21
Sample: Adjacent to perimeter (182918-23-2)	21
Sample: Adjacent to Perimeter (182918-23-3)	21
Sample: Adjacent to Perimeter (182918-23-4)	21
Sample: Adjacent to Perimeter (182918-23-5)	21
Sample: Adjacent to Perimeter (182918-23-6)	21
Sample: Adjacent to Perimeter (182918-23-7)	21

Sample: Adjacent to Perimeter (182918-23-8)	21
Sample: Field Blank (182918-23-9)	21
Test: Personal (182918-24)	23
Sample: On Chris Dawson Sifting through soil (182918-24-1)	25
Sample: On Clive Curran Machine operator (182918-24-2)	25
Test: Background (182918-25)	26
Sample: Adjacent to perimeter (182918-25-1)	27
Sample: Adjacent to Perimeter (182918-25-2)	27
Sample: Adjacent to Perimeter (182918-25-3)	27
Sample: Adjacent to Perimeter (182918-25-4)	27
Sample: Adjacent to Perimeter (182918-25-5)	27
Sample: Adjacent to Perimeter (182918-25-6)	27
Sample: Field Blank (182918-25-7)	27
Sample: Adjacent to Perimeter (182918-25-8)	27
Sample: Adjacent to Perimeter (182918-25-9)	27
Sample: Adjacent to Perimeter (182918-25-10)	27
Test: Personal (182918-26)	29
Sample: On Ollie Pangmore Operating Machine (182918-26-1)	30
Sample: On Chris Dawson While spraying (182918-26-2)	30
Test: Background (182918-27)	31
Sample: Adjacent to Perimeter (182918-27-1)	33
Sample: Adjacent to Perimeter (182918-27-2)	33
Sample: Adjacent to Perimeter (182918-27-3)	33
Sample: Adjacent to Perimeter (182918-27-4)	33
Sample: Adjacent to Perimeter (182918-27-5)	33
Sample: Field Blank (182918-27-6)	33
Sample: Adjacent to Perimeter (182918-27-7)	33
Sample: Adjacent to Perimeter (182918-27-8)	33
Sample: Adjacent to Perimeter (182918-27-9)	33
Test: Reassurance (182918-31)	35
Sample: adjacent to perimeter fence next to road (182918-31-1)	36
Sample: adjacent to perimeter fence next to road (182918-31-2)	36
Sample: along perimeter fence adjacent to foot path (182918-31-3)	36
Sample: entrance to site adjacent to road (182918-31-4)	36

Test: Background 182918-19


Number of samples being taken	5
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Monday, 24th April, 2017 @ 12:33:54
Additional notes	satisfactory
Additional Photo 1	
Additional Photo 2	

table continued from previous page...

Additional Photo 3



Additional Photo 4

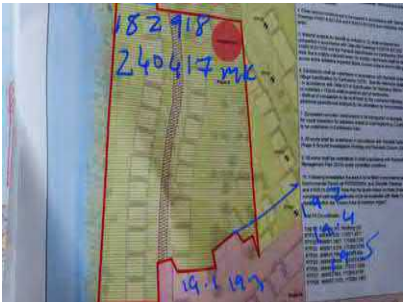

airtests


Test: Background 182918-19 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-19		Monday, 24th April, 2017		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				14		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro		Graticule Dia mm									
1011		1		MS059		100									
						Test Slide Result Grid									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS80		FM111		FM190		222									
						Graticule Slide									
						SM748									
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
				hh:mm	hh:mm	mins	lmin-1	lmin-1	lmin-1	l	l			Fibres cm ⁻³	Fibres cm ⁻³
182918-19-1	Adjacent to Perimeter	324	1716	08:45:00	09:47:00	62	8.0		8.0	496	496	1.0	194	0.001	<0.01
182918-19-2	Adjacent to Perimeter	635	1721	08:47:00	09:49:00	62	8.0		8.0	496	496	2.0	194	0.001	<0.01
182918-19-3	Adjacent to Perimeter	517	1716	11:01:00	12:02:00	61	8.0		8.0	488	488	1.5	200	0.001	<0.01
182918-19-4	Adjacent to Perimeter	530	1721	11:01:00	12:02:00	61	8.0		8.0	488	488	1.0	200	0.001	<0.01
182918-19-5	Field Blank	635										0.0	100		

Test: Personal 182918-20

Number of samples being taken	2
RPE used for works	Sundstrom SR100 P3 filter
Description of works / product removed	soil removal
Asbestos Contractor	Rambool
Client Representative or Contractor	Chris Dawson
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 25th April, 2017 @ 14:09:09
Additional notes	satisfactory
Additional Photo 1	

Additional Photo 2

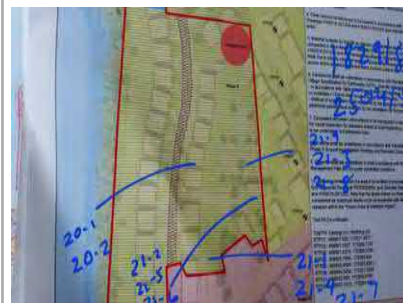

Airtests


Test: Personal 182918-20 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-20		Tuesday, 25th April, 2017		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				7		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1008		1		MS059		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS80		FM111		FM190		222									
						Graticule Slide									
						SM748									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
182918-20-1	On Chris Dawson as operative watering down	301	20	08:43:00	10:04:00	81	2.0		2.0	162	162	1.0	200	0.002	<0.03
182918-20-2	On Clive Curran Digger Operator	301	20	10:59:00	12:03:00	64	2.0		2.0	128	128	2.0	200	0.004	<0.04

Test: Background 182918-21

Number of samples being taken	9
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 25th April, 2017 @ 15:26:16
Additional notes	satisfactory
Additional Photo 1	
Additional Photo 2	

Additional Photo 3

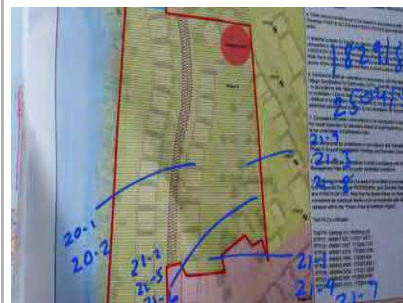

Airtests

Test: Background 182918-21 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-21		Tuesday, 25th April, 2017		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K		T Site C		T Pcal hPa											
293		7		1013											
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro o	Graticule Dia mm		Test Slide Result Grid o	Filter Dia Exposed mm									
1008	1	MS059	100		5	22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece	Flow Hi	Flow Low		HSE PL		Graticule Slide									
WS80	FM111	FM190		222		SM748									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
182918-21-1	Adjacent to perimeter	530	1708	08:45:00	10:02:00	77	8.0		8.0	616	616	2.0	156	0.001	<0.01
182918-21-2	Adjacent to Perimeter	80	1721	08:46:00	10:00:00	74	8.0		8.0	592	592	2.5	162	0.001	<0.01
182918-21-3	Adjacent to Perimeter	450	1716	08:47:00	10:00:00	73	8.0		8.0	584	584	3.0	164	0.002	<0.01
182918-21-4	Adjacent to Perimeter	635	1716	11:00:00	12:01:00	61	8.0		8.0	488	488	1.5	200	0.001	<0.01
182918-21-5	Adjacent to Perimeter	450	1708	11:01:00	12:02:00	61	8.0		8.0	488	488	ncountable			
182918-21-6	Adjacent to Perimeter	530	1721	11:01:00	12:02:00	61	8.0		8.0	488	488	3.0	200	0.002	<0.01
182918-21-7	Adjacent to perimeter	324	1709	13:56:00	14:58:00	62	8.0		8.0	496	496	3.0	200	0.002	<0.01
182918-21-8	Adjacent to Perimeter	635	1715	13:57:00	14:59:00	62	8.0		8.0	496	496	2.5	200	0.001	<0.01

table continued from previous page...


Sample Details															
182918-21-9	Adjacent to Perimeter	301	1721	13:59:00	15:01:00	62	8.0		8.0	496	496	2.0	200	0.001	<0.01
182918-21-10	Field Blank	530										0.0	100		

Test: Personal 182918-22

Number of samples being taken	2
RPE used for works	Sundstrom SR100 P3 filter
Description of works / product removed	Moving of Soil
Asbestos Contractor	Rambol
Client Representative or Contractor	Chris Dawson
Air sample results	All air samples gave results below 0.04 fibres per ccm of air.
Stage Warning?	No
Analyst Signature Signature Date	 Wednesday, 26th April, 2017 @ 13:27:06
Additional notes	satisfactory
Additional Photo 1	

table continued from previous page...

Additional Photo 2

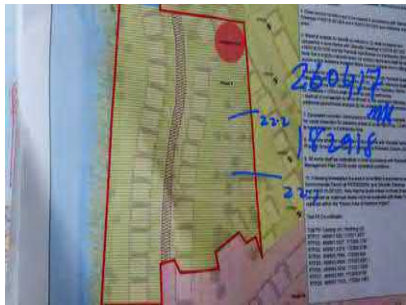


airtests

Test: Personal 182918-22 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-22		Wednesday, 26th April, 2017		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				10		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro		Graticule Dia mm									
1011		1		MS059		100									
						Test Slide Result Grid									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS80		FM111		FM190		222									
						Graticule Slide									
						SM748									
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
				hh:mm	hh:mm	mins	lmin-1	lmin-1	lmin-1	l	l			Fibres cm ⁻³	Fibres cm ⁻³
182918-22-1	On Chris Dawson spraying adjacent to soil moving	301	20	08:31:00	09:51:00	80	2.0		2.0	160	160	2.0	200	0.003	<0.03
182918-22-2	On Clive Curran Machine operator	530	20	10:59:00	12:30:00	91	2.0		2.0	182	182	1.0	200	0.001	<0.03

Test: Background 182918-23

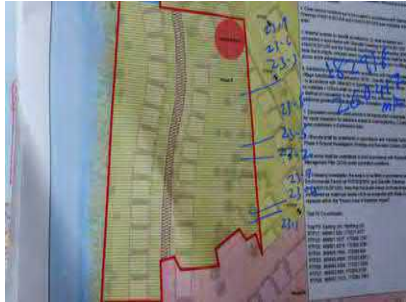Number of samples being taken	9
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Wednesday, 26th April, 2017 @ 15:19:23
Additional notes	satisfactory
Additional Photo 1	
Additional Photo 2	 airtests

Test: Background 182918-23 - Count Sheet


Lucion Report Number		Test Date		Sampled By		Counted By									
182918-23		Wednesday, 26th April, 2017		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K		T Site C		T Pcal hPa											
293		10		1013											
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro	Graticule Dia mm	Test Slide Result Grid		Filter Dia Exposed mm									
1011	1	MS059	100	5		22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi	Flow Low	HSE PL		Graticule Slide									
WS80		FM111	FM190	222		SM748									
Sample Details															
Sample	Sample Location	Head	Pump	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
182918-23-1	Adjacent to Perimeter	324	1708	08:38:00	09:51:00	73	8.0		8.0	584	584	3.0	164	0.002	<0.01
182918-23-2	Adjacent to perimeter	635	1721	08:38:00	09:49:00	71	8.0		8.0	568	568	3.0	169	0.002	<0.01
182918-23-3	Adjacent to Perimeter	450	1715	08:39:00	09:50:00	71	8.0		8.0	568	568	2.0	169	0.001	<0.01
182918-23-4	Adjacent to Perimeter	80	1716	11:01:00	12:05:00	64	8.0		8.0	512	512	3.0	200	0.001	<0.01
182918-23-5	Adjacent to Perimeter	702	1715	11:02:00	12:05:00	63	8.0		8.0	504	504	2.0	200	0.001	<0.01
182918-23-6	Adjacent to Perimeter	517	1709	11:03:00	12:06:00	63	8.0		8.0	504	504	2.5	200	0.001	<0.01
182918-23-7	Adjacent to Perimeter	702	1716	13:49:00	14:50:00	61	8.0		8.0	488	488	2.5	200	0.001	<0.01
182918-23-8	Adjacent to Perimeter	324	1709	13:50:00	14:50:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01
182918-23-9	Field Blank	530										0.0	100		

Test: Personal 182918-24

Number of samples being taken	2
RPE used for works	Sundstrom SR100 P3 filter
Description of works / product removed	Sifting through soil while machine operator move
Asbestos Contractor	Rambool
Client Representative or Contractor	Chris Dawson
Air sample results	All air samples gave results below 0.04 fibres per ccm of air.
Stage Warning?	No
Analyst Signature Signature Date	 Thursday, 27th April, 2017 @ 13:35:22
Additional notes	satisfactory
Additional Photo 1	
Additional Photo 2	

table continued from previous page...

Additional Photo 3

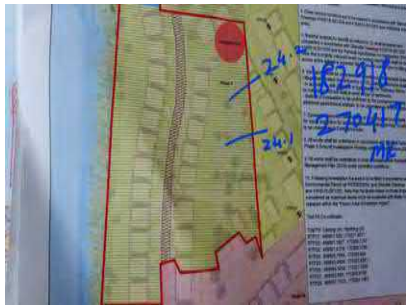


Airtests

Test: Personal 182918-24 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-24		Thursday, 27th April, 2017		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				8		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1014		1		MS059		100									
						Test Slide Result Grid o									
						Filter Dia Exposed mm									
						5									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS80		FM111		FM190		222									
						Graticule Slide									
						SM748									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow l/min-1	Int Flow l/min-1	End Flow l/min-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
182918-24-1	On Chris Dawson Sifting through soil	324	20	08:51:00	10:15:00	84	2.0		2.0	168	168	1.5	200	0.002	<0.03
182918-24-2	On Clive Curran Machine operator	600	20	11:01:00	12:16:00	75	2.0		2.0	150	150	2.0	200	0.003	<0.03

Test: Background 182918-25

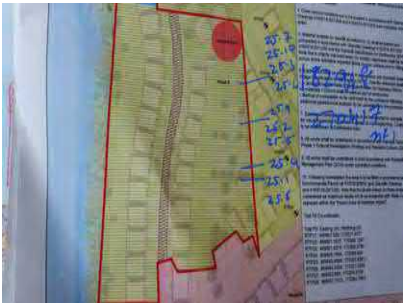Number of samples being taken	10
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Thursday, 27th April, 2017 @ 15:15:49
Additional notes	satisfactory
Additional Photo 1	
Additional Photo 2	 Airtests

Test: Background 182918-25 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-25		Thursday, 27th April, 2017		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				8		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1014		1		MS059		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS80		FM111		FM190		222									
						Graticule Slide									
						SM748									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
182918-25-1	Adjacent to perimeter	80	1716	08:52:00	09:54:00	62	8.0		8.0	496	496	1.5	200	0.001	<0.01
182918-25-2	Adjacent to Perimeter	450	1715	08:59:00	10:00:00	61	8.0		8.0	488	488	2.0	200	0.001	<0.01
182918-25-3	Adjacent to Perimeter	301	1709	08:59:00	10:00:00	61	8.0		8.0	488	488	2.0	200	0.001	<0.01
182918-25-4	Adjacent to Perimeter	80	1721	11:03:00	12:06:00	63	8.0		8.0	504	504	1.5	200	0.001	<0.01
182918-25-5	Adjacent to Perimeter	530	1716	11:03:00	12:08:00	65	8.0		8.0	520	520	3.0	200	0.001	<0.01
182918-25-6	Adjacent to Perimeter	635	1708	11:04:00	12:08:00	64	8.0		8.0	512	512	2.0	200	0.001	<0.01
182918-25-7	Field Blank	702										0.0	100		
182918-25-8	Adjacent to Perimeter	635	1716	13:53:00	14:54:00	61	8.0		8.0	488	488	2.5	200	0.001	<0.01
182918-25-9	Adjacent to Perimeter	702	1715	13:53:00	15:53:00	120	8.0		8.0	960	960	2.0	200	0.001	<0.01

table continued from previous table...

Sample Details															
182918-25-10	Adjacent to Perimeter	80	1709	13:54:00	14:55:00	61	8.0		8.0	488	488	3.0	200	0.002	<0.01

Test: Personal 182918-26

Number of samples being taken	2
RPE used for works	Sundstrom SR100 P3 filter
Description of works / product removed	Moving soil
Asbestos Contractor	Woolridge
Client Representative or Contractor	Ollie Pangmore
Air sample results	All air samples gave results below 0.04 fibres per ccm of air.
Stage Warning?	No
Analyst Signature Signature Date	 Friday, 28th April, 2017 @ 14:18:52
Additional notes	satisfactory
Additional Photo 1	 Airtests

Test: Personal 182918-26 - Count Sheet


Lucion Report Number		Test Date		Sampled By		Counted By									
182918-26		Friday, 28th April, 2017		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				9		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1011		1		MS059		100									
						Test Slide Result Grid o									
						Filter Dia Exposed mm									
						5									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS80		FM111		FM190		222									
						Graticule Slide									
						SM748									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
182918-26-1	On Ollie Pangmore Operating Machine	635	20	08:15:00	09:30:00	75	2.0		2.0	150	150	1.0	200	0.002	<0.03
182918-26-2	On Chris Dawson While spraying	450	20	11:28:00	12:30:00	62	2.0		2.0	124	124	2.0	200	0.004	<0.04

Test: Background 182918-27

Number of samples being taken	9
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Friday, 28th April, 2017 @ 14:18:02
Additional notes	satisfactory
Additional Photo 1	
Additional Photo 2	

table continued from previous page...

Additional Photo 3

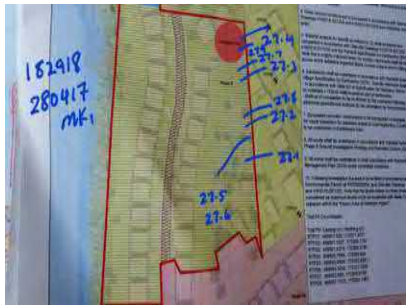

Airtests

Test: Background 182918-27 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-27		Friday, 28th April, 2017		Mohammad Khan		Mohammad Khan									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				9		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro		Graticule Dia mm									
1011		1		MS059		100									
						Test Slide Result Grid									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS80		FM111		FM190		222									
						Graticule Slide									
						SM748									
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
				hh:mm	hh:mm	mins	lmin-1	lmin-1	lmin-1	l	l			Fibres cm ⁻³	Fibres cm ⁻³
182918-27-1	Adjacent to Perimeter	600	1721	08:16:00	09:17:00	61	8.0		8.0	488	488	1.0	200	0.001	<0.01
182918-27-2	Adjacent to Perimeter	702	1708	08:16:00	09:18:00	62	8.0		8.0	496	496	2.0	200	0.001	<0.01
182918-27-3	Adjacent to Perimeter	450	1709	08:17:00	09:18:00	61	8.0		8.0	488	488	3.0	200	0.002	<0.01
182918-27-4	Adjacent to Perimeter	517	1715	08:17:00	09:20:00	63	8.0		8.0	504	504	3.0	200	0.002	<0.01
182918-27-5	Adjacent to Perimeter	324	1718	09:05:00	10:06:00	61	8.0		8.0	488	488	2.0	200	0.001	<0.01
182918-27-6	Field Blank	530										0.0	100		
182918-27-7	Adjacent to Perimeter	635	1716	11:28:00	12:28:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01
182918-27-8	Adjacent to Perimeter	301	1709	11:30:00	12:30:00	60	8.0		8.0	480	480	3.0	200	0.002	<0.01
182918-27-9	Adjacent to Perimeter	530	1715	11:30:00	12:30:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01

Test: Reassurance 182918-31

Number of samples being taken	4
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 2nd May, 2017 @ 13:35:00

Test: Reassurance 182918-31 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
182918-31		Tuesday, 2nd May, 2017		Kelvin Reynolds		Kelvin Reynolds									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				20		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro		Graticule Dia mm									
1013		1		MS07		100									
						Test Slide Result Grid									
						5									
						Filter Dia Exposed mm									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS79		FM188		FM191		458									
						Graticule Slide									
						SM760									
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
		o	o	hh:mm	hh:mm	mins	lmin-1	lmin-1	lmin-1	l	l			Fibres cm ⁻³	Fibres cm ⁻³
182918-31-1	adjacent to perimeter fence next to road	982	1879	10:49:00	11:59:00	70	8.0		8.0	560	560	1.0	171	0.001	<0.01
182918-31-2	adjacent to perimeter fence next to road	983	1837	10:50:00	12:00:00	70	8.0		8.0	560	560	1.0	171	0.001	<0.01
182918-31-3	along perimeter fence adjacent to foot path	985	1888	10:53:00	12:02:00	69	8.0		8.0	552	552	1.0	174	0.001	<0.01
182918-31-4	entrance to site adjacent to road	984	1872	10:54:00	12:03:00	69	8.0		8.0	552	552	2.0	174	0.001	<0.01

Hygiene Facility Inspection Certificate

Job Ref No, Cert Ref No, Account Ref No, Contract Ref No

Hygiene Facility: Envirograd SH400

Asbestos Contractor & Address(using facility)

Rambool

Asbestos Contractor Representative on Site

Chris Wilson

Asbestos Contractor Representative Signature (confirming test outcome)



Site Name / Building (where inspection has been performed)

St Edwards Homes, Green Park Village, Reading, RG30 3UR

Inspection Requirement

Hygiene Facility leaving site

Report Issue and Inspection Completion Date / Time

Fri 28 Apr 2017 @ 14:18:00

Lucion Analyst(s) on Site

Mohammad Khan

Lucion Analyst(s) signature(s)



Thorough Visual Inspection of Hygiene Facility

Passed 

Stage 2 - Start Time: 12:41:00 - End Time: 12:44:00

The following were found to be satisfactory:

The hygiene facility is dust and debris free

(check door seals, grilles, walls, floors, ceilings and drains for ground-in dirt/dust and mould/slime)

Yes

All waste and non-essential equipment removed

(Towels, filters, overalls, nail brushes etc)

Yes

Hygiene unit is dry

Yes

Analyst

Mohammad Khan

Analyst signature



Additional Notes 

satisfactory

Clearance Air Monitoring Inside Hygiene Facility

Passed 

Stage 3 - Start Time: 12:46:00 - End Time: 14:09:00

The following were found to be satisfactory:

NPU / Extractor isolated and sealed

Yes

Surface disturbance method used

Brushing

Head Office

7 Halifax Court, Dunston,
Gateshead, NE11 9JT

E:

info@innov8safetysolutions.co.uk

T: 01454 411974

Duration of disturbance (minutes)	1:30
Shower and dirty end area combined (m ²)	(m ²)
Number of clearance samples required	
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Analyst	Mohammad Khan
Analyst signature	
Additional Notes 	satisfactory

Hygiene Facility Photo

Clean End Photo



Shower Photo (from clean end)

Dirty End Photo



Additional Information

Sampling & Evaluation Methods - In-house methods TOP02.08 & TOP02.09 in accordance with HSG 248 Asbestos - The Analysts' Guide to Sampling, Analysis and Clearance Procedures. Notes: The samples referred to in this report will be retained for 6 months unless requested otherwise. Unless otherwise stated, there are no departures from the sampling and evaluation methods specified. Results detailed in this report relate only to the time, and corresponding conditions prevailing, when the sampling and examination were undertaken. Note: HSG248 requires that only stages 2 and 3 of the 4 stage clearance procedure need be undertaken in issuing a hygiene facility inspection certificate.

Notes to Test Accuracy - Airflow measured on site is recorded against a correction chart. Flow meters are calibrated against a UKAS certified master flow meter accurate to $\pm 0.5\%$. In accordance with HSG248, if the combined effect of ambient temperature and pressure between calibration and sampling location exceeds 5% a correction is applied to the air sample volume. The calculated fibre concentration is given for each air sample taken. Where the corresponding reported fibre concentration is preceded by "<", the lower limit of quantification (LOQ) of the method has not been reached. For a 480 litre air sample with 200 graticule areas counted, the (LOQ) of this method is 0.010 fibres per cubic centimetre of air; samples of less volume/graticules will be reported to a lower LOQ (refer count sheet). While counting randomly distributed fibres, an expected degree of variation of 1.5 standard deviations from the mean count may occur. At clearance indicator level (0.01 fibres per cubic centimetre of air) a 480-litre air sample yielding a count of 20 fibres over 200 fields would have an expected standard deviation of ± 8 fibres.

Sampling - When testing within a hygiene facility (also termed a decontamination unit (DCU)) - where the combined floor area of shower and dirty areas is less than 10m²; 1 air test has been carried out. During this test the door between these areas has been propped open and sample head positioned in the doorway. For combined floor areas exceeding 10m² a sample in each area (i.e. shower and dirty end) will be taken.

Field Blanks - Where site sampling and counting is carried out in a field laboratory a field blank is carried out by the analyst prior to the start of sampling and counting. The field blank constitutes a filter taken from a loaded but unused filter head that is mounted in the usual way and assigned a sample number which is recorded on the slide and the count sheet. Following sampling and analysis of the air tests, the results shall be assessed; where low counts ($< 0.01 \text{ fcm}^{-3}$) are obtained from some of the field samples, analysis of the field blank will not be necessary. Where elevated counts ($> 0.01 \text{ fcm}^{-3}$) are obtained on all field samples, then the field blank must be counted to exclude the possibility of contamination.

Disclaimers - Any opinions and interpretations expressed herein are outside the scope of UKAS accreditation. This certificate is valid only when it bears the signature of an authorised member of Lucion personnel. This certificate ☐ a ☐ be part of a series of works and should be read in conjunction with the Asbestos Analyst's Job Summary Report.

Hygiene Facility Inspection Certificate

Job Ref No, Cert Ref No, Account Ref No, Contract Ref No

Hygiene Facility: DCU SH400

Asbestos Contractor & Address(using facility)

wooldridge

Asbestos Contractor Representative on Site

wooldridge Jamie wilkinson

Asbestos Contractor Representative Signature (confirming test outcome)



Site Name / Building (where inspection has been performed)

St Edwards Homes, Green Park Village, Reading, RG30 3UR

Inspection Requirement

Hygiene Facility leaving site

Report Issue and Inspection Completion Date / Time

Tue 2 May 2017 @ 13:36:43

Lucion Analyst(s) on Site

Kelvin Reynolds

Lucion Analyst(s) signature(s)



Thorough Visual Inspection of Hygiene Facility

Passed 

Stage 2 - Start Time: 12:10:00 - End Time: 12:16:00

The following were found to be satisfactory:

The hygiene facility is dust and debris free

(check door seals, grilles, walls, floors, ceilings and drains for ground-in dirt/dust and mould/slime)

Yes

All waste and non-essential equipment removed

(Towels, filters, overalls, nail brushes etc)

Yes

Hygiene unit is dry

Yes

Analyst

Kelvin Reynolds

Analyst signature



Clearance Air Monitoring Inside Hygiene Facility

Passed 

Stage 3 - Start Time: 12:23:00 - End Time: 13:36:00

The following were found to be satisfactory:

NPU / Extractor isolated and sealed

Yes

Surface disturbance method used

Brushing

Duration of disturbance (minutes)

1:30

Head Office

7 Halifax Court, Dunston,
Gateshead, NE11 9JT

E:

info@innov8safetysolutions.co.uk

T: 01454 411974

Shower and dirty end area combined (m ²)	6 (m ²)
Number of clearance samples required	1
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Analyst	Kelvin Reynolds
Analyst signature	


Hygiene Facility Photo



Clean End Photo



Shower Photo (from clean end)

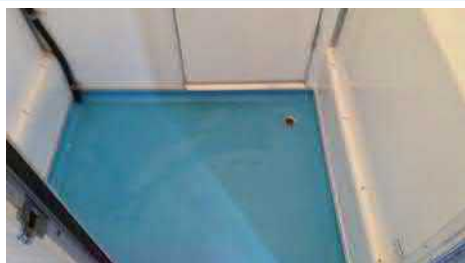

Dirty End Photo



Additional Information

Sampling & Evaluation Methods - In-house methods TOP02.08 & TOP02.09 in accordance with HSG 248 Asbestos - The Analysts' Guide to Sampling, Analysis and Clearance Procedures. Notes: The samples referred to in this report will be retained for 6 months unless requested otherwise. Unless otherwise stated, there are no departures from the sampling and evaluation methods specified. Results detailed in this report relate only to the time, and corresponding conditions prevailing, when the sampling and examination were undertaken. Note: HSG248 requires that only stages 2 and 3 of the 4 stage clearance procedure need be undertaken in issuing a hygiene facility inspection certificate.

Notes to Test Accuracy - Airflow measured on site is recorded against a correction chart. Flow meters are calibrated against a UKAS certified master flow meter accurate to $\pm 0.5\%$. In accordance with HSG248, if the combined effect of ambient temperature and pressure between calibration and sampling location exceeds 5% a correction is applied to the air sample volume. The calculated fibre concentration is given for each air sample taken. Where the corresponding reported fibre concentration is preceded by "<", the lower limit of quantification (LOQ) of the method has not been reached. For a 480 litre air sample with 200 graticule areas counted, the (LOQ) of this method is 0.010 fibres per cubic centimetre of air; samples of less volume/graticules will be reported to a lower LOQ (refer count sheet). While counting randomly distributed fibres, an expected degree of variation of 1.5 standard deviations from the mean count may occur. At clearance indicator level (0.01 fibres per cubic centimetre of air) a 480-litre air sample yielding a count of 20 fibres over 200 fields would have an expected standard deviation of ± 8 fibres.

Sampling - When testing within a hygiene facility (also termed a decontamination unit (DCU)) - where the combined floor area of shower and dirty areas is less than 10m²; 1 air test has been carried out. During this test the door between these areas has been propped open and sample head positioned in the doorway. For combined floor areas exceeding 10m² a sample in each area (i.e. shower and dirty end) will be taken.

Field Blanks - Where site sampling and counting is carried out in a field laboratory a field blank is carried out by the analyst prior to the start of sampling and counting. The field blank constitutes a filter taken from a loaded but unused filter head that is mounted in the usual way and assigned a sample number which is recorded on the slide and the count sheet. Following sampling and analysis of the air tests, the results shall be assessed; where low counts ($< 0.01 \text{ fcm}^{-3}$) are obtained from some of the field samples, analysis of the field blank will not be necessary. Where elevated counts ($> 0.01 \text{ fcm}^{-3}$) are obtained on all field samples, then the field blank must be counted to exclude the possibility of contamination.

Disclaimers - Any opinions and interpretations expressed herein are outside the scope of UKAS accreditation. This certificate is valid only when it bears the signature of an authorised member of Lucion personnel. This certificate ☐ a ☐ be part of a series of works and should be read in conjunction with the Asbestos Analyst's Job Summary Report.

Asbestos Analyst's Job Summary Report

Job Ref No 00000000, Account Ref No 00000000, Contract Ref No 00000000

St Edwards Homes, Green Park Village, Reading, RG30 3UR

Time boundary air monitoring during phase 5 excavation works June 2017



on site photo

Passed Certificates	Failed Certificates
2	0

Site visit on 06th June, 2017, at 10:00 AM on Wednesday, 06th June, 2017

Intro

This document is a summary of findings relating to asbestos analytical works at **St Edwards Homes, Green Park Village, Reading, RG30 3UR** from **Monday, 26th June, 2017 to Wednesday, 28th June, 2017**. It is intended to give an overview of testing and must be read only in conjunction with the certificates it references. The document should never be read in isolation as asbestos analysts reports often contain additional notes and advice that should be referred to.

A report is provided electronically via the NexGen web-portal. Rendering of the report will create a unique pdf version identified in the the footer of the document where date and time of rendering is recorded. Document history can be reviewed via the 'View File History' when viewing the report online. Prior to commencing any works or review of the report, the most current version should be obtained via the link to the NexGen web-portal; any local pdf copies should not be relied on as containing the most current information.

Furthermore, this document contains a summary of analyst notes and comments made in relation to works at this site.

Please note this document may contain findings from more than one analyst on more than one date.

Key to Air-Test Icons

To aid ease of reading the following icons have been used in this document to reference commonly undertaken activities.

-  Clearance Stage 1
-  Clearance Stage 2
-  Clearance Stage 3
-  Clearance Stage 4
-  DCU Stage 2
-  DCU Stage 3
-  Reassurance
-  Background
-  Leak Testing
-  Personal
-  Smoke Test Witness
-  Report Acknowledgement

A **WARNING** is used by the analyst to draw the readers attention to a particular area of the report.

Attachments

The following documents accompany this report and should be regarded as an integral part of this report.

They can be downloaded from <http://web.lucion.co.uk/reports/206471/attachments>.

- [Method Statement \[http://web.lucion.co.uk/method_statements/206471?s=15a58847dc8c66ce3c91a031c5530c4c \]](http://web.lucion.co.uk/method_statements/206471?s=15a58847dc8c66ce3c91a031c5530c4c)
- [Risk Assessment \[http://web.lucion.co.uk/risk_assessment/206471?s=8224776cd82059be8b318929f4784499 \]](http://web.lucion.co.uk/risk_assessment/206471?s=8224776cd82059be8b318929f4784499)

Asbestos Analyst's Certificate Report

Job Ref No, Cert Ref No, Account Ref No, Contract Ref No

St Edwards Homes, Green Park Village, Reading, RG30 3UR



on site photo



General works area photo

Building	Level	Works-Area	Enclosure Used	Certificate Issue Date
St Edwards Homes, Green Park Village, Reading	0	Phase 5 - Air monitoring during soil remediation works	No	Wednesday, 28th June, 2017

Overall Certificate Status	Passed Tests	Failed Tests	WARNINGS
PASSED	0	0	0

Intro

This certificate is for the attention of

Mr Martin Rutledge
Berkeley Homes (Western) Limited
200 Longwater Avenue Green Park Reading Berkshire RG2 6GB

Sampling and Evaluation methods

In-house methods TOP02.08 & TOP02.09 in accordance with HSG 248 Asbestos - The Analyst's Guide to Sampling, Analysis and Clearance Procedures.

Notes: The samples referred to in this report will be retained for 6 months unless requested otherwise. Unless otherwise stated, there are no departures from the sampling and evaluation methods specified. Results detailed in this report relate only to the time, and corresponding conditions prevailing, when the sampling and examination were undertaken.

Notes to Test Accuracy

Airflow measured on site is recorded against a correction chart. Flow meters are calibrated against a UKAS certified master flow meter accurate to $\pm 0.5\%$. In accordance with HSG248, if the combined effect of ambient temperature and pressure between calibration and sampling location exceeds 5% a correction is applied to the air sample volume. The calculated fibre concentration is given for each air sample taken. Where the corresponding reported fibre concentration is preceded by "<", the lower limit of quantification (LOQ) of the method has not been reached. For a 480 litre air sample with 200 graticule areas counted, the (LOQ) of this method is 0.010 fibres per cubic centimetre of air; samples of less volume/graticules will be reported to a lower LOQ (refer count sheet). While counting randomly distributed fibres, an expected degree of variation of 1.5 standard deviations from the mean count may occur. At clearance indicator level (0.01 fibres per cubic centimetre of air) a 480-litre air sample yielding a count of 20 fibres over 200 fields would have an expected standard deviation of ± 8 fibres.

Sampling

When testing within an Enclosure and conducting a 4-Stage Clearance - the number of samples (Ns) is calculated by $A^{1/3} - 1$. Where enclosure is less than 3m in height: A is denoted by area. Where enclosure is greater than 3m in height: A is denoted by volume/3. Refer air sampling and fibre counting sheet.

When testing within a decontamination unit (DCU) - where the combined floor area of shower and dirty areas is less than 10m²; 1 air test has been carried out. During this test the door between these areas has been propped open. For combined floor areas exceeding 10m² a sample in each area (i.e. shower and dirty end) will be taken.

For tests other than those associated with 4-Stage Clearance testing the analyst will apply the principles of current HSE guidance and experience combined with situational circumstances.

Where a photograph of the completed decontamination unit certificate appears in this report the analyst has completed an abridged report to be left inside the DCU; this abridged report should not be used in lieu of this comprehensive report.

Where sampling plans have been supplied; please note these are not to scale.

Where a sample filter has been deemed uncountable or biased the analyst will record this as "uncountable" in the count-sheet.

Field Blanks - Where site sampling and counting is carried out in a field laboratory a field blank is carried out by the analyst prior to the start of sampling and counting. The field blank constitutes a filter taken from a loaded but unused filter head that is mounted in the usual way and assigned a sample number which is recorded on the slide and the count sheet. Following sampling and analysis of the air tests, the results shall be assessed; where low counts ($<0.01 \text{ fcm}^{-3}$) are obtained from some of the field samples, analysis of the field blank will not be necessary. Where elevated counts ($>0.01 \text{ fcm}^{-3}$) are obtained on all field samples, then the field blank must be counted to exclude the possibility of contamination.

Disclaimers

Any opinions and interpretations expressed herein are outside the scope of UKAS accreditation. This certificate is valid only when it bears the signature of an authorised member of Lucion personnel. Please note the witnessing of smoke tests is outwith the scope of UKAS accreditation.

Representatives Signature - The signatory on report acknowledgement agrees to findings of this report being accurate and correct and Lucion Environmental Ltd issuing this report to the email address held on record for the job and does not require a copy of this report to be left on site. Furthermore Lucion Environmental Ltd cannot be held responsible for any actions undertaken following the issue of this report.

This certificate ☐ a ☐ be part of a series of works and should be read in conjunction with the Asbestos Analyst's Job Summary Report.

Report Contents

Test: Background (206471-1)	5
Sample: Within Phase 5 - Adjacent to DCU (206471-1-1)	7
Sample: Within Phase 5 - South east corner adjacent site walkway to Phase 1 (206471-1-2)	7
Sample: Within Phase 5 - South edge adjacent site walkway to Phase 1 (206471-1-3)	7
Sample: Within Phase 5 - Along west boundary of proposed work area (downwind) (206471-1-4)	7
Sample: Within Phase 5 - Along west boundary of proposed work area (downwind) (206471-1-5)	7
Sample: Within Phase 5 - Along west boundary of proposed work area (downwind) (206471-1-6)	7
Sample: Within Phase 5 - To east side during 360 excavator trial pit excavation (downwind) (206471-1-7)	7
Sample: Within Phase 5 - To east side during 360 excavator trial pit excavation (downwind) (206471-1-8)	7
Sample: Within Phase 5 - To west side during 360 excavator trial pit excavation (206471-1-9)	7
Sample: Field Blank (206471-1-10)	7
Test: Personal (206471-2)	9
Sample: On Operative Oliver Pangborn during operation of 360 excavator to dig trial pits (206471-2-1)	10
Test: Background (206471-3)	11
Sample: Within Phase 5 - Along west boundary of work area (downwind) (206471-3-1)	13
Sample: Within Phase 5 - Along west boundary of work area (downwind) (206471-3-2)	13
Sample: Within Phase 5 - Along west boundary of work area (downwind) (206471-3-3)	13
Sample: Within Phase 5 - Along west boundary of work area (downwind) (206471-3-4)	13
Sample: Within Phase 5 - Along west boundary of work area during 360 excavator operation (downwind) (206471-3-5)	13
Sample: Within Phase 5 - Along west boundary of work area during 360 excavator operation (downwind) (206471-3-6)	13
Test: Personal (206471-4)	14
Sample: On Operative Joao Freitas during operation of 360 excavator (206471-4-1)	15
Test: Reassurance (206471-5)	16
Sample: Within Phase 5 - Along east boundary (206471-5-1)	18
Sample: Within Phase 5 - Along south boundary (206471-5-2)	18
Sample: Within Phase 5 - Along west boundary (206471-5-3)	18
Sample: Field Blank (206471-5-4)	18

Test: Background 206471-1

Number of samples being taken	9
Stage Warning?	No
Analyst Signature Signature Date	 Monday, 26th June, 2017 @ 17:00:38
Additional notes	Air monitoring during site boundary setup for segregation during ACM remediation works to section of Phase 5
Additional Photo 1	 Example of air monitoring to boundary during setup of Heras fencing
Additional Photo 2	 Air monitoring adjacent to 360 excavator prior to soil remediation

table continued from previous page...

Additional Photo 3



Air monitoring adjacent to DCU

Additional Photo 4



Air sampling locations

Test: Background 206471-1 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
206471-1		Monday, 26th June, 2017		Damian Rowland		Damian Rowland									
Air Volume Correction Detail															
T Cal (K)		T Site (C)		T Pcal (hPa)											
293		18		1013											
Microscope Calculation Detail															
P Site (hPa)	Correction Required	Micro (o)	Graticule Dia (mm)		Test Slide Result (Grid (o))		Filter Dia (Exposed (mm))								
1007	1	MS048	100		5		22.0								
Instrument Detail															
Thermometer, Barometer, Timepiece	Flow (Hi)	Flow (Low)		HSE (PL)		Graticule Slide									
WS90	FM399	FM337		302		SM767									
Sample Details															
Sample (o)	Sample Location	Head (o)	Pump (o)	Time On (hh:mm)	Time Off (hh:mm)	Run Time (mins)	Start Flow (lmin-1)	Int Flow (lmin-1)	End Flow (lmin-1)	Calc Volume (l)	Corr Volume (l)	Fibres	Fields	Calc Conc (Fibres cm ⁻³)	Report Conc (Fibres cm ⁻³)
206471-1-1	Within Phase 5 - Adjacent to DCU	306	1897	09:35:00	10:31:00	56	10.0		10.0	560	560	2.0	171	0.001	<0.01
206471-1-2	Within Phase 5 - South east corner adjacent site walkway to Phase 1	975	1898	09:39:00	10:33:00	54	10.0		9.8	535	535	0.5	179	0.000	<0.01
206471-1-3	Within Phase 5 - South edge adjacent site walkway to Phase 1	980	1899	09:41:00	10:36:00	55	10.0		9.8	545	545	1.0	176	0.001	<0.01
206471-1-4	Within Phase 5 - Along west boundary of proposed work area (downwind)	974	1897	10:32:00	11:22:00	50	10.0		10.0	500	500	1.5	192	0.001	<0.01
206471-1-5	Within Phase 5 - Along west boundary of proposed work area (downwind)	655	1898	10:40:00	11:30:00	50	10.0		10.0	500	500	1.0	192	0.001	<0.01
206471-1-6	Within Phase 5 - Along west boundary of proposed work area (downwind)	978	1899	10:39:00	11:32:00	53	10.0		9.9	527	527	1.0	182	0.001	<0.01
206471-1-7	Within Phase 5 - To east side during 360 excavator trial pit excavation (downwind)	980	1897	14:34:00	15:24:00	50	10.0		10.0	500	500	0.5	192	0.000	<0.01
206471-1-8	Within Phase 5 - To east side during 360 excavator trial pit excavation (downwind)	655	1898	14:35:00	15:25:00	50	10.0		10.0	500	500	1.0	192	0.001	<0.01
206471-1-9	Within Phase 5 - To west side during 360 excavator trial pit excavation	975	1899	14:30:00	15:20:00	50	10.0		9.8	495	495	0.5	194	0.000	<0.01

[table continued from previous page...](#)

Sample Details														
206471-1-10	Field Blank	1124												

Test: Personal 206471-2

Number of samples being taken	1
RPE used for works	N/A
Description of works / product removed	Trial excavation pits in 360 excavator
Asbestos Contractor	Wooldridge
Client Representative or Contractor	Oliver Pangborn
Air sample results	All air samples gave results below 0.07 fibres per ccm of air.
Stage Warning?	No
Analyst Signature Signature Date	 Monday, 26th June, 2017 @ 17:01:15
Additional notes	Air monitoring during trial pit excavation using 360 excavator
Additional Photo 1	 Air sampling location

Test: Personal 206471-2 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
206471-2		Monday, 26th June, 2017		Damian Rowland		Damian Rowland									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				20		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1008		1		MS048		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS90		FM399		FM337		302									
						Graticule Slide									
						SM767									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
206471-2-1	On Operative Oliver Pangborn during operation of 360 excavator to dig trial pits	974	519	14:36:00	15:11:00	35	2.0		2.0	70	70	1.5	200	0.005	<0.07

Test: Background 206471-3

Number of samples being taken	6
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 27th June, 2017 @ 17:00:26
Additional notes	Boundary air monitoring during soil excavation within Phase 5.
Additional Photo 1	 Example of air monitoring to boundary adjacent site walkway and construction transit route
Additional Photo 2	 Example of air monitoring to boundary

[table continued from previous page...](#)

Additional Photo 3



Additional example of air monitoring to boundary

Additional Photo 4



Air sampling locations

Test: Background 206471-3 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
206471-3		Tuesday, 27th June, 2017		Damian Rowland		Damian Rowland									
Air Volume Correction Detail															
T Cal °K		T Site °C		T Pcal hPa											
293		18		1013											
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro	Graticule Dia mm	Test Slide Result Grid		Filter Dia Exposed mm									
999	1	MS048	100	5		22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece	Flow Hi	Flow Low	HSE PL		Graticule Slide										
WS90	FM399	FM337	302		SM767										
Sample Details															
Sample No	Sample Location	Head No	Pump No	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
206471-3-1	Within Phase 5 - Along west boundary of work area (downwind)	980	1897	08:21:00	10:11:00	110	8.0	8.0	8.0	880	880	1.5	109	0.001	<0.01
206471-3-2	Within Phase 5 - Along west boundary of work area (downwind)	979	1899	08:22:00	10:12:00	110	8.0	8.0	7.9	876	876	1.0	110	0.001	<0.01
206471-3-3	Within Phase 5 - Along west boundary of work area (downwind)	272	1898	08:24:00	10:14:00	110	8.0	8.0	8.0	880	880	1.0	109	0.001	<0.01
206471-3-4	Within Phase 5 - Along west boundary of work area (downwind)	978	1902	08:26:00	10:17:00	111	8.0	7.8	7.8	873	873	0.5	110	0.000	<0.01
206471-3-5	Within Phase 5 - Along west boundary of work area during 360 excavator operation (downwind)	974	1897	10:22:00	11:25:00	63	8.0		8.0	504	504	0.5	190	0.000	<0.01
206471-3-6	Within Phase 5 - Along west boundary of work area during 360 excavator operation (downwind)	975	1899	10:25:00	11:28:00	63	8.0		7.8	498	498	2.0	193	0.001	<0.01

Test: Personal 206471-4

Number of samples being taken	1
RPE used for works	n/a
Description of works / product removed	Operation of excavator
Asbestos Contractor	Wooddridge
Client Representative or Contractor	Joao Freitas
Air sample results	All air samples gave results below 0.03 fibres per ccm of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 27th June, 2017 @ 17:01:17
Additional notes	Personal air monitoring during soil works
Additional Photo 1	 Air sampling location

Test: Personal 206471-4 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
206471-4		Tuesday, 27th June, 2017		Damian Rowland		Damian Rowland									
Air Volume Correction Detail															
T Cal K		T Site C		T Pcal hPa											
293		19		1013											
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro	Graticule Dia mm	Test Slide Result Grid		Filter Dia Exposed mm									
999	1	MS048	100	5		22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece	Flow Hi	Flow Low	HSE PL		Graticule Slide										
WS90	FM399	FM337	302		SM767										
Sample Details															
Sample	Sample Location	Head	Pump	Time On	Time Off	Run Time	Start Flow	Int Flow	End Flow	Calc Volume	Corr Volume	Fibres	Fields	Calc Conc	Report Conc
no		no	no	hh:mm	hh:mm	mins	lmin-1	lmin-1	lmin-1	l	l			Fibres cm ⁻³	Fibres cm ⁻³
206471-4-1	On Operative Joao Freitas during operation of 360 excavator	655	519	08:28:00	09:38:00	70	2.0		2.0	140	140	1.0	200	0.002	<0.03

Test: Reassurance 206471-5

Number of samples being taken	3
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Tuesday, 27th June, 2017 @ 17:03:55
Additional notes	Reassurance air monitoring after soil remediation works to phase 5
Additional Photo 1	 Example of air monitoring to east side boundary
Additional Photo 2	 Example of air monitoring to south boundary of phase 5

table continued from previous page...

Additional Photo 3



Example of air monitoring to west boundary of phase 5

Additional Photo 4



Air sampling locations

Test: Reassurance 206471-5 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
206471-5		Tuesday, 27th June, 2017		Damian Rowland		Damian Rowland									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				21		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
998		1		MS048		100									
Test Slide Result Grid o		Filter Dia Exposed mm		5		22.0									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS90		FM399		FM337		302									
Graticule Slide		SM767													
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
206471-5-1	Within Phase 5 - Along east boundary	655	1897	13:20:00	14:09:00	49	10.0		10.0	490	490	1.5	196	0.001	<0.01
206471-5-2	Within Phase 5 - Along south boundary	975	1898	13:22:00	14:12:00	50	10.0		9.9	497	497	1.5	193	0.001	<0.01
206471-5-3	Within Phase 5 - Along west boundary	974	1899	13:25:00	14:15:00	50	10.0		10.0	500	500	1.0	192	0.001	<0.01
206471-5-4	Field Blank	1124													

Hygiene Facility Inspection Certificate

Job Ref No [REDACTED], Cert Ref No [REDACTED], Account Ref No [REDACTED], Contract Ref No [REDACTED]

Hygiene Facility: DCU - H360

Asbestos Contractor & Address(using facility)

Wooldridge

Asbestos Contractor Representative on Site

Jamie Wilkinson - Wooldridge

Asbestos Contractor Representative Signature (confirming test outcome)



Site Name / Building (where inspection has been performed)

St Edwards Homes, Green Park Village, Reading, RG30 3UR

Inspection Requirement

Hygiene Facility leaving site

Report Issue and Inspection Completion Date / Time

Wed 28 Jun 2017 @ 09:20:13

Lucion Analyst(s) on Site

Damian Rowland

Lucion Analyst(s) signature(s)



Thorough Visual Inspection of Hygiene Facility

Stage 2 - Start Time: 07:57:00 - End Time: 08:05:00

Passed 

The following were found to be satisfactory:

The hygiene facility is dust and debris free
(check door seals, grilles, walls, floors, ceilings and drains for ground-in dirt/dust and mould/slime)

Yes

All waste and non-essential equipment removed
(Towels, filters, overalls, nail brushes etc)

Yes

Hygiene unit is dry

Yes

Analyst

Damian Rowland

Analyst signature



Additional Notes 

DCU unused for duration of works.

Clearance Air Monitoring Inside Hygiene Facility

Stage 3 - Start Time: 08:06:00 - End Time: 09:08:00

Passed 

The following were found to be satisfactory:

NPU / Extractor isolated and sealed

Yes

Surface disturbance method used

Brushing

Duration of disturbance (minutes)	1:30
Shower and dirty end area combined (m ²)	4 (m ²)
Number of clearance samples required	1
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Analyst	Damian Rowland
Analyst signature	

Hygiene Facility Photo



Clean End Photo



Shower Photo (from clean end)



Dirty End Photo



Additional Information

Sampling & Evaluation Methods - In-house methods TOP02.08 & TOP02.09 in accordance with HSG 248 Asbestos - The Analysts' Guide to Sampling, Analysis and Clearance Procedures. Notes: The samples referred to in this report will be retained for 6 months unless requested otherwise. Unless otherwise stated, there are no departures from the sampling and evaluation methods specified. Results detailed in this report relate only to the time, and corresponding conditions prevailing, when the sampling and examination were undertaken. Note: HSG248 requires that only stages 2 and 3 of the 4 stage clearance procedure need be undertaken in issuing a hygiene facility inspection certificate.

Notes to Test Accuracy - Airflow measured on site is recorded against a correction chart. Flow meters are calibrated against a UKAS certified master flow meter accurate to $\pm 0.5\%$. In accordance with HSG248, if the combined effect of ambient temperature and pressure between calibration and sampling location exceeds 5% a correction is applied to the air sample volume. The calculated fibre concentration is given for each air sample taken. Where the corresponding reported fibre concentration is preceded by "<", the lower limit of quantification (LOQ) of the method has not been reached. For a 480 litre air sample with 200 graticule areas counted, the (LOQ) of this method is 0.010 fibres per cubic centimetre of air; samples of less volume/graticules will be reported to a lower LOQ (refer count sheet). While counting randomly distributed fibres, an expected degree of variation of 1.5 standard deviations from the mean count may occur. At clearance indicator level (0.01 fibres per cubic centimetre of air) a 480-litre air sample yielding a count of 20 fibres over 200 fields would have an expected standard deviation of ± 8 fibres.

Sampling - When testing within a hygiene facility (also termed a decontamination unit (DCU)) - where the combined floor area of shower and dirty areas is less than 10m²; 1 air test has been carried out. During this test the door between these areas has been propped open and sample head positioned in the doorway. For combined floor areas exceeding 10m² a sample in each area (i.e. shower and dirty end) will be taken.

Field Blanks - Where site sampling and counting is carried out in a field laboratory a field blank is carried out by the analyst prior to the start of sampling and counting. The field blank constitutes a filter taken from a loaded but unused filter head that is mounted in the usual way and assigned a sample number which is recorded on the slide and the count sheet. Following sampling and analysis of the air tests, the results shall be assessed; where low counts ($<0.01 \text{ fcm}^{-3}$) are obtained from some of the field samples, analysis of the field blank will not be necessary. Where elevated counts ($>0.01 \text{ fcm}^{-3}$) are obtained on all field samples, then the field blank must be counted to exclude the possibility of contamination.


Disclaimers - Any opinions and interpretations expressed herein are outside the scope of UKAS accreditation. This certificate is valid only when it bears the signature of an authorised member of Lucion personnel. This certificate ☐ a ☐ be part of a series of works and should be read in conjunction with the Asbestos Analyst's Job Summary Report.

Asbestos Analyst's Job Summary Report

Job Ref No: **219796**, Account Ref No: **17752**, Contract Ref No: **28790**

St Edwards Homes, Green Park Village, Reading, Berkshire, RG30 3UR

Title: Air testing during drainage run works

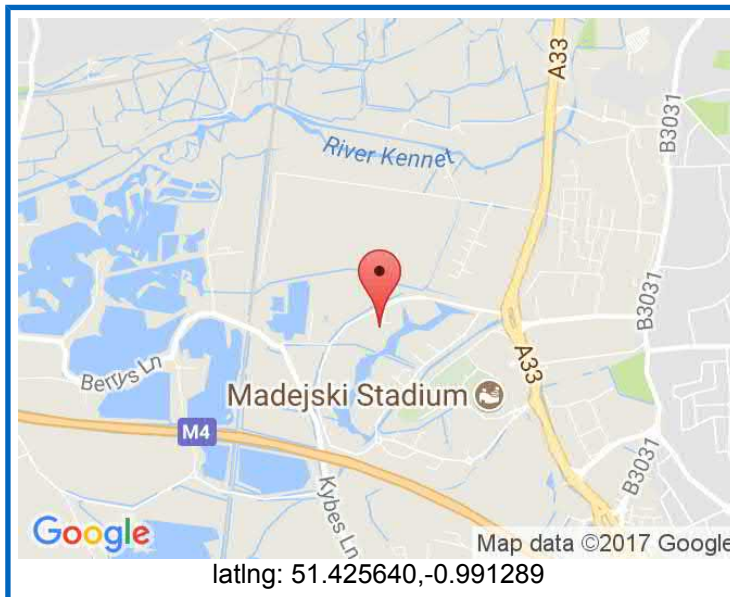

on site photo

Passed Certificates	Failed Certificates
2	0

First Visit to Site: Wednesday, 20th September, 2017, **Last Visit to Site:** Friday, 22nd September, 2017

Intro

This document is a summary of findings relating to asbestos analytical works at **St Edwards Homes, Green Park Village, Reading, Berkshire, RG30 3UR** from **Wednesday, 20th September, 2017 to Friday, 22nd September, 2017**. It is intended to give an overview of testing and must be read only in conjunction with the certificates it references. The document should never be read in isolation as asbestos analysts reports often contain additional notes and advice that should be referred to.

A report is provided electronically via the NexGen web-portal. Rendering of the report will create a unique pdf version identified in the the footer of the document where date and time of rendering is recorded. Document history can be reviewed via the 'View File History' when viewing the report online. Prior to commencing any works or review of the report, the most current version should be obtained via the link to the NexGen web-portal; any local pdf copies should not be relied on as containing the most current information.

Furthermore, this document contains a summary of analyst notes and comments made in relation to works at this site.

Please note this document may contain findings from more than one analyst on more than one date.

Key to Air-Test Icons

To aid ease of reading the following icons have been used in this document to reference commonly undertaken activities.

-  Clearance Stage 1
-  Clearance Stage 2
-  Clearance Stage 3
-  Clearance Stage 4
-  DCU Stage 2
-  DCU Stage 3
-  Reassurance
-  Background
-  Leak Testing
-  Personal
-  Smoke Test Witness
-  Report Acknowledgement

A **WARNING** is used by the analyst to draw the readers attention to a particular area of the report.

Overview of Works

To view a complete air-certificate, follow the relevant link

Certificate: Phase 5 Drainage Ditch				Building: Berkeley Homes - Green Park Village		Level: 0		Passed	
View the Full Certificate Here: http://web.lucion.co.uk/air_cert/35656?s=c79e396617fd50d503499193f30448eb									
Type	Test-ID	Start Time	End Time	Date	Operative	# Samples			
Personal	219796-4				Lewis Bowles	1			
Background	219796-1			20-09-2017	Rupert Anderson	5			
Personal	219796-2			20-09-2017	Rupert Anderson	1			
Background	219796-3			21-09-2017	Lewis Bowles	5			
Background	219796-8			22-09-2017	Lewis Bowles	6			

 Certificate: DCU 12243				Building: Berkeley Homes - Green Park Village		Level: 0	Passed 
View the Full Certificate Here: http://web.lucion.co.uk/air_cert/35673?s=5156496fc86e24f5943ba543d288c335							
Type	Test-ID	Start Time	End Time	Date	Operative	# Samples	
 DCU Stage 2	219796-5	10:35:00	10:42:00	21-09-2017	 Lewis Bowles	--	Passed 
 DCU Stage 3	219796-6	10:44:00	11:41:00	21-09-2017	 Lewis Bowles	2	Passed 
 Report Acknowledgement	219796-7			21-09-2017	 Lewis Bowles	--	

Attachments

The following documents accompany this report and should be regarded as an integral part of this report.


They can be downloaded from <http://web.lucion.co.uk/reports/219796/attachments>.

- [Method Statement \[http://web.lucion.co.uk/method_statements/219796?s=feff8f0a8b7f98128ac240d5595a24e8 \]](http://web.lucion.co.uk/method_statements/219796?s=feff8f0a8b7f98128ac240d5595a24e8)
- [Risk Assessment \[http://web.lucion.co.uk/risk_assessment/219796?s=e572bcf246799cc28c293a78ad63d9fd \]](http://web.lucion.co.uk/risk_assessment/219796?s=e572bcf246799cc28c293a78ad63d9fd)

Asbestos Analyst's Certificate Report

Job Ref No: **219796**, Cert Ref No: **35656**, Account Ref No: **17752**, Contract Ref No: **28790**

St Edwards Homes, Green Park Village, Reading, Berkshire, RG30 3UR

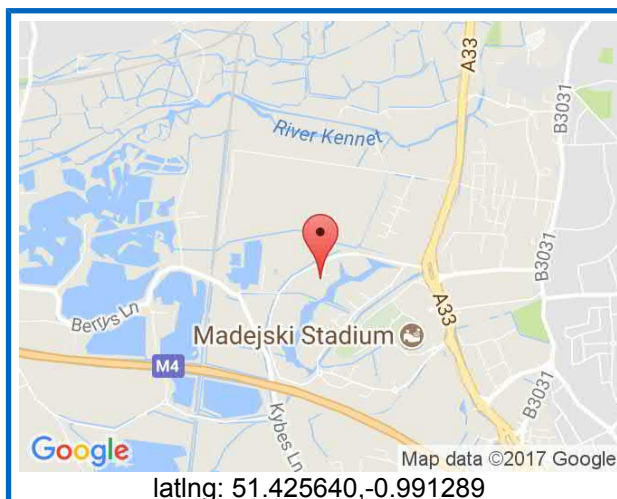

on site photo



general works area photo

Building	Level	Works-Area	Enclosure Used ☐	Certificate Issue Date
Berkeley Homes - Green Park Village	0	Phase 5 Drainage Ditch	No	Friday, 22nd September, 2017

Overall Certificate Status	Passed Tests	Failed Tests	WARNINGS
PASSED	0	0	0

Intro

This certificate is for the attention of

Tim Salt
Berkeley Homes Western Limited
200 Longwater Avenue Green Park Reading Berkshire RG2 6GB

Sampling Evaluation methods

In-house methods TOP02.08 & TOP02.09 in accordance with HSG 248 Asbestos - The Analyst's Guide to Sampling, Analysis and Clearance Procedures.

Notes: The samples referred to in this report will be retained for 6 months unless requested otherwise. Unless otherwise stated, there are no departures from the sampling and evaluation methods specified. Results detailed in this report relate only to the time, and corresponding conditions prevailing, when the sampling and examination were undertaken.

Notes to Test Accuracy

Airflow measured on site is recorded against a correction chart. Flow meters are calibrated against a UKAS certified master flow meter accurate to $\pm 0.5\%$. In accordance with HSG248, if the combined effect of ambient temperature and pressure between calibration and sampling location exceeds 5% a correction is applied to the air sample volume. The calculated fibre concentration is given for each air sample taken. Where the corresponding reported fibre concentration is preceded by "<", the lower limit of quantification (LOQ) of the method has not been reached. For a 480 litre air sample with 200 graticule areas counted, the (LOQ) of this method is 0.010 fibres per cubic centimetre of air; samples of less volume/graticules will be reported to a lower LOQ (refer count sheet). While counting randomly distributed fibres, an expected degree of variation of 1.5 standard deviations from the mean count may occur. At clearance indicator level (0.01 fibres per cubic centimetre of air) a 480-litre air sample yielding a count of 20 fibres over 200 fields would have an expected standard deviation of ± 8 fibres.

Sampling

When testing within an Enclosure and conducting a 4-Stage Clearance - the number of samples (Ns) is calculated by $A^{1/3}-1$. Where enclosure is less than 3m in height: A is denoted by area. Where enclosure is greater than 3m in height: A is denoted by volume/3. Refer air sampling and fibre counting sheet.

When testing within a decontamination unit (DCU) - where the combined floor area of shower and dirty areas is less than 10m²; 1 air test has been carried out. During this test the door between these areas has been propped open. For combined floor areas exceeding 10m² a sample in each area (i.e. shower and dirty end) will be taken.

For tests other than those associated with 4-Stage Clearance testing the analyst will apply the principles of current HSE guidance and experience combined with situational circumstances.

Where a photograph of the completed decontamination unit certificate appears in this report the analyst has completed an abridged report to be left inside the DCU; this abridged report should not be used in lieu of this comprehensive report.

Where sampling plans have been supplied; please note these are not to scale.

Where a sample filter has been deemed uncountable or biased the analyst will record this as "uncountable" in the count-sheet.

Field Blanks - Where site sampling and counting is carried out in a field laboratory a field blank is carried out by the analyst prior to the start of sampling and counting. The field blank constitutes a filter taken from a loaded but unused filter head that is mounted in the usual way and assigned a sample number which is recorded on the slide and the count sheet. Following sampling and analysis of the air tests, the results shall be assessed; where low counts ($<0.01 \text{ fcm}^{-3}$) are obtained from some of the field samples, analysis of the field blank will not be necessary. Where elevated counts ($>0.01 \text{ fcm}^{-3}$) are obtained on all field samples, then the field blank must be counted to exclude the possibility of contamination.

Disclaimers

Any opinions and interpretations expressed herein are outside the scope of UKAS accreditation. This certificate is valid only when it bears the signature of an authorised member of Lucion personnel. Please note the witnessing of smoke tests is outwith the scope of UKAS accreditation.

Representatives Signature - The signatory on report acknowledgement agrees to findings of this report being accurate and correct and Lucion Environmental Ltd issuing this report to the email address held on record for the job and does not require a copy of this report to be left on site. Furthermore Lucion Environmental Ltd cannot be held responsible for any actions undertaken following the issue of this report.

This certificate ☐ a ☐ be part of a series of works and should be read in conjunction with the Asbestos Analyst's Job Summary Report.

Report Contents

Test: Background (219796-1)	5
Sample: North boundary of work area (219796-1-1)	6
Sample: West boundary of work area (219796-1-2)	6
Sample: West boundary of work area (219796-1-3)	6
Sample: West boundary of work area (219796-1-4)	6
Sample: Field Blank (219796-1-5)	6
Test: Personal (219796-2)	7
Sample: On Clive Curran manoeuvring digger (219796-2-1)	8
Test: Background (219796-3)	9
Sample: Field Blank (219796-3-1)	10
Sample: West boundary of work area during digging (219796-3-2)	10
Sample: East boundary of work area during digging (219796-3-3)	10
Sample: South boundary of work area during digging (219796-3-4)	10
Sample: East boundary of work area during digging (219796-3-5)	10
Test: Personal (219796-4)	11
Sample: On C. Curran during digging of suspected contaminated soil (219796-4-1)	12
Test: Background (219796-8)	13
Sample: West boundary of work area during laying down gravel membrane (219796-8-1)	14
Sample: South boundary of work area during laying down gravel membrane (219796-8-2)	14
Sample: West boundary of work area during laying down gravel membrane (219796-8-3)	14
Sample: South boundary of work area during laying down gravel membrane (219796-8-4)	14
Sample: West boundary of work area during laying down gravel membrane (219796-8-5)	14
Sample: South boundary of work area during laying down gravel membrane (219796-8-6)	14

Test: Background 219796-1

Number of samples being taken	4
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Wednesday, 20th September, 2017 @ 15:05:10
Additional Photo 1	 Site Plan and Sample Point Locations

Test: Background 219796-1 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
219796-1		Wednesday, 20th September, 2017		Rupert Anderson		Rupert Anderson									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				15		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1014		1		MS073		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS98		FM135		FM080		318									
						Graticule Slide									
						SM08									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
219796-1-1	North boundary of work area	787	1732	11:44:00	12:44:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01
219796-1-2	West boundary of work area	780	278	11:47:00	12:47:00	60	8.0		8.0	480	480	2.0	200	0.001	<0.01
219796-1-3	West boundary of work area	723	278	13:33:00	14:36:00	63	8.0		8.0	504	504	1.0	190	0.001	<0.01
219796-1-4	West boundary of work area	771	1732	13:34:00	14:36:00	62	8.0		8.0	496	496	1.5	194	0.001	<0.01
219796-1-5	Field Blank	787										0.0	100		

Test: Personal 219796-2

Number of samples being taken	1
RPE used for works	Sundstrom SR100 P3 filter
Description of works / product removed	Operating digger moving material
Asbestos Contractor	Wooldridge
Client Representative or Contractor	Clive Curran
Air sample results	All final results below 0.09 fibres per ccm of air.
Stage Warning?	No
Analyst Signature Signature Date	 Wednesday, 20th September, 2017 @ 15:07:30

Test: Personal 219796-2 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
219796-2		Wednesday, 20th September, 2017		Rupert Anderson		Rupert Anderson									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293				15		1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
1014		1		MS073		100									
						Test Slide Result Grid o									
						5									
						Filter Dia Exposed mm									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS98		FM135		FM080		318									
						Graticule Slide									
						SM08									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
219796-2-1	On Clive Curran manoeuvring digger	775	394	11:41:00	12:35:00	54	2.0		2.0	108	108	1.0	100	0.005	<0.09

Test: Background 219796-3

Number of samples being taken	4
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Thursday, 21st September, 2017 @ 15:01:43

Test: Background 219796-3 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
219796-3		Thursday, 21st September, 2017		Lewis Bowles		Lewis Bowles									
Air Volume Correction Detail															
T Cal (K)				T Site (C)		T Pcal (hPa)									
293				22		1013									
Microscope Calculation Detail															
P Site (hPa)	Correction Required	Micro (o)	Graticule Dia (mm)		Test Slide Result (Grid (o))	Filter Dia (Exposed (mm))									
1011	1	MS080	100		5	22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow (Hi)		Flow (Low)		HSE (PL)									
WS37		FM221		FM191		SM760									
Sample Details															
Sample (o)	Sample Location	Head (o)	Pump (o)	Time On (hh:mm)	Time Off (hh:mm)	Run Time (mins)	Start Flow (lmin-1)	Int Flow (lmin-1)	End Flow (lmin-1)	Calc Volume (l)	Corr Volume (l)	Fibres	Fields	Calc Conc (Fibres cm ⁻³)	Report Conc (Fibres cm ⁻³)
219796-3-1	Field Blank	653													
219796-3-2	West boundary of work area during digging	645	1655	09:23:00	10:11:00	48	10.0		10.0	480	0	1.0	200		
219796-3-3	East boundary of work area during digging	616	05	09:28:00	10:16:00	48	10.0		10.0	480	0	1.0	200		
219796-3-4	South boundary of work area during digging	113	1655	13:43:00	14:36:00	53	10.0		10.0	530	0	1.0	200		
219796-3-5	East boundary of work area during digging	616	05	13:45:00	14:38:00	53	10.0		10.0	530	0	1.0	200		

Test: Personal 219796-4

Number of samples being taken	1
-------------------------------	---

Test: Personal 219796-4 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
219796-4				Lewis Bowles		Lewis Bowles									
Air Volume Correction Detail															
T Cal K				T Site C		T Pcal hPa									
293						1013									
Microscope Calculation Detail															
P Site hPa		Correction Required		Micro o		Graticule Dia mm									
				MS080		100									
						5									
						22.5									
Instrument Detail															
Thermometer, Barometer, Timepiece		Flow Hi		Flow Low		HSE PL									
WS37		FM221		FM191		458									
						SM760									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
219796-4-1	On C. Curran during digging of suspected contaminated soil	17	490	09:12:00	10:31:00	79	2.0		2.0	158	0	2.0	200		

Test: Background 219796-8

Number of samples being taken	6
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Stage Warning?	No
Analyst Signature Signature Date	 Friday, 22nd September, 2017 @ 14:13:58

Test: Background 219796-8 - Count Sheet

Lucion Report Number		Test Date		Sampled By		Counted By									
219796-8		Friday, 22nd September, 2017		Lewis Bowles		Lewis Bowles									
Air Volume Correction Detail															
T Cal K		T Site C		T Pcal hPa											
293		21		1013											
Microscope Calculation Detail															
P Site hPa	Correction Required	Micro o	Graticule Dia mm		Test Slide Result Grid o		Filter Dia Exposed mm								
1010	1	MS080	100		5		22.5								
Instrument Detail															
Thermometer, Barometer, Timepiece	Flow Hi	Flow Low		HSE PL		Graticule Slide									
WS37	FM221	FM191		458		SM760									
Sample Details															
Sample o	Sample Location	Head o	Pump o	Time On hh:mm	Time Off hh:mm	Run Time mins	Start Flow lmin-1	Int Flow lmin-1	End Flow lmin-1	Calc Volume l	Corr Volume l	Fibres	Fields	Calc Conc Fibres cm ⁻³	Report Conc Fibres cm ⁻³
219796-8-1	West boundary of work area during laying down gravel membrane	653	052	09:09:00	09:58:00	49	10.0		10.0	490	0	1.0	200		
219796-8-2	South boundary of work area during laying down gravel membrane	645	05	09:11:00	10:04:00	53	10.0		10.0	530	0	1.0	200		
219796-8-3	West boundary of work area during laying down gravel membrane	17	05	11:07:00	12:00:00	53	10.0		10.0	530	0	1.0	200		
219796-8-4	South boundary of work area during laying down gravel membrane	645	1655	11:09:00	12:01:00	52	10.0		10.0	520	0	1.0	200		
219796-8-5	West boundary of work area during laying down gravel membrane	113	05	12:51:00	13:48:00	57	10.0		10.0	570	0	1.0	200		
219796-8-6	South boundary of work area during laying down gravel membrane	113	03	12:53:00	13:51:00	58	10.0		10.0	580	0	1.0	200		

Hygiene Facility Inspection Certificate

Job Ref No: **219796**, Cert Ref No: **35673**, Account Ref No: **17752**, Contract Ref No: **28790**

Hygiene Facility: DCU 12243

Asbestos Contractor & Address(using facility)	Wooldridge
Asbestos Contractor Representative on Site	W. Gallagher
Asbestos Contractor Representative Signature (confirming test outcome)	
Site Name / Building (where inspection has been performed)	St Edwards Homes, Green Park Village, Reading, Berkshire, RG30 3UR
Inspection Requirement	Hygiene Facility leaving site
Report Issue and Inspection Completion Date / Time	Thu 21 Sep 2017 @ 13:24:16
Lucion Analyst(s) on Site	Lewis Bowles
Lucion Analyst(s) signature(s)	

Thorough Visual Inspection of Hygiene Facility

Stage 2 - Start Time: 10:35:00 - End Time: 10:42:00

Passed 

The following were found to be satisfactory:

The hygiene facility is dust and debris free
(check door seals, grilles, walls, floors, ceilings and drains for ground-in dirt/dust and mould/slime)

Yes

All waste and non-essential equipment removed
(Towels, filters, overalls, nail brushes etc)

Yes

Hygiene unit is dry

Yes

Analyst

Lewis Bowles

Analyst signature



Clearance Air Monitoring Inside Hygiene Facility

Stage 3 - Start Time: 10:44:00 - End Time: 11:41:00

Passed 

The following were found to be satisfactory:

NPU / Extractor isolated and sealed

Yes

Surface disturbance method used

Brushing

Duration of disturbance (minutes)

1:30

Shower and dirty end area combined (m²)

(m²)

Head Office

7 Halifax Court, Dunston,
Gateshead, NE11 9JT
E: enquiries@lucion.co.uk
T: 0345 5040 303

Number of clearance samples required	
Air sample results	All air samples gave results below 0.01 fibres per cc of air.
Analyst	Lewis Bowles
Analyst signature	


Hygiene Facility Photo



Clean End Photo



Shower Photo (from clean end)

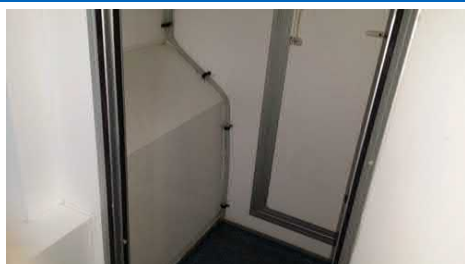

Dirty End Photo



Additional Information

Sampling & Evaluation Methods - In-house methods TOP02.08 & TOP02.09 in accordance with HSG 248 Asbestos - The Analysts' Guide to Sampling, Analysis and Clearance Procedures. Notes: The samples referred to in this report will be retained for 6 months unless requested otherwise. Unless otherwise stated, there are no departures from the sampling and evaluation methods specified. Results detailed in this report relate only to the time, and corresponding conditions prevailing, when the sampling and examination were undertaken. Note: HSG248 requires that only stages 2 and 3 of the 4 stage clearance procedure need be undertaken in issuing a hygiene facility inspection certificate.

Notes to Test Accuracy - Airflow measured on site is recorded against a correction chart. Flow meters are calibrated against a UKAS certified master flow meter accurate to $\pm 0.5\%$. In accordance with HSG248, if the combined effect of ambient temperature and pressure between calibration and sampling location exceeds 5% a correction is applied to the air sample volume. The calculated fibre concentration is given for each air sample taken. Where the corresponding reported fibre concentration is preceded by "<", the lower limit of quantification (LOQ) of the method has not been reached. For a 480 litre air sample with 200 graticule areas counted, the (LOQ) of this method is 0.010 fibres per cubic centimetre of air; samples of less volume/graticules will be reported to a lower LOQ (refer count sheet). While counting randomly distributed fibres, an expected degree of variation of 1.5 standard deviations from the mean count may occur. At clearance indicator level (0.01 fibres per cubic centimetre of air) a 480-litre air sample yielding a count of 20 fibres over 200 fields would have an expected standard deviation of ± 8 fibres.

Sampling - When testing within a hygiene facility (also termed a decontamination unit (DCU)) - where the combined floor area of shower and dirty areas is less than 10m²; 1 air test has been carried out. During this test the door between these areas has been propped open and sample head positioned in the doorway. For combined floor areas exceeding 10m² a sample in each area (i.e. shower and dirty end) will be taken.

Field Blanks - Where site sampling and counting is carried out in a field laboratory a field blank is carried out by the analyst prior to the start of sampling and counting. The field blank constitutes a filter taken from a loaded but unused filter head that is mounted in the usual way and assigned a sample number which is recorded on the slide and the count sheet. Following sampling and analysis of the air tests, the results shall be assessed; where low counts ($<0.01 \text{ fcm}^{-3}$) are obtained from some of the field samples, analysis of the field blank will not be necessary. Where elevated counts ($>0.01 \text{ fcm}^{-3}$) are obtained on all field samples, then the field blank must be counted to exclude the possibility of contamination.

Disclaimers - Any opinions and interpretations expressed herein are outside the scope of UKAS accreditation. This certificate is valid only when it bears the signature of an authorised member of Lucion personnel. This certificate ☐ a ☐ be part of a series of works and should be read in conjunction with the Asbestos Analyst's Job Summary Report.

APPENDIX 6 – DUTY OF CARE INFORMATION

Permit FP3694VC/A001 – Asbestos Waste Solutions Llp

Permit number	FP3694VC/A001
Waste Management Licence No.	101371
Licence Holder Name	Asbestos Waste Solutions Llp

Site

Site name	Asbestos Waste Solutions
Site type	S0809 No 9: Asbestos Waste Transfer Station
Site Address	27a, Oliver Close, West Thurrock, Essex, RM20 3EE
Site Postcode	RM20 3EE
Site Grid Reference	TQ5764677131
Easting	557646
Northing	177131
Local Authority	Thurrock

Status

Status Description	Issued
Issued Date	25/01/2010

Bugle Nurseries

Permit number EPR/BB3105HY

Introductory note

This introductory note does not form a part of the permit

The main features of the permit are as follows.

This permit allows the operator to store waste and treat it to produce soil, soil substitutes and aggregate. Permitted wastes do not include hazardous wastes. The total quantity of waste that can be stored and subsequently treated at the site shall be no more than 75,000 tonnes per year. This permit does not permit the burning of any wastes, either in the open, inside buildings or in any form of incinerator. This permit does not allow any point source emission into surface waters or groundwater.

The status log of the permit sets out the permitting history, including any changes to the permit reference number.

Status log of the permit		
Description	Date	Comments
Application EPR/BB3105HY/A001	Duty made 21/01/14	Application for treatment of waste to produce soil, soil substitutes and aggregate
Additional information received	17/02/14	Revised environment management system and dust management plan
Permit determined	10/04/14	Permit issued to London Spoil Disposal Limited

End of Introductory note

Permit with introductory note

The Environmental Permitting (England & Wales) Regulations 2010

London Spill Disposal Limited

Bugle Nurseries
171 Upper Halliford Road
Shepperton
TW17 8SN

Permit number

EPR/BB3105HY

Permit FP3393EF/V003 – C G Comley & Sons Ltd

Permit number	FP3393EF/V003
Waste Management Licence No.	83055
Pre-EA Permit Ref	HR078
Licence Holder Name	C G Comley & Sons Ltd
Trading Name	C G Comley & Sons Ltd

Site

Site name	Calf Lane Quarry, Rye Common , Odiham, Rg29
Site type	A9 : Special Waste Transfer Station
Site Address	Calf Lane Quarry, Calf Lane, Rye Common, Odiham, Hampshire, RG29 1HU
Site Postcode	RG29 1HU
Site Grid Reference	SU7734049920
Easting	477340
Northing	149920
Local Authority	Hart

Status

Status Description	Modified
Issued Date	04/08/1993
Variation Date	12/06/1997

Registration CBDU43110 – Luton Environmental Limited

Registration number	CBDU43110
Business name	Luton Environmental Limited
Company number	07854592
Registered as	Carrier Dealer - Upper Tier
Applicant type	Company
Registration date:	15/04/2015
Expiry date:	29/04/2018

Business address

Address	19, BOLINGBROKE ROAD, LUTON, LU1 5JD
Postcode	LU1 5JD

Registration CBDU81963 – WOOLDRIDGE ECOTEC LTD

Registration number	CBDU81963
Business name	WOOLDRIDGE ECOTEC LTD
Company number	03399413
Registered as	Carrier Dealer - Upper Tier
Applicant type	Company
Registration date:	12/01/2016
Expiry date:	09/02/2019

Business address

Address	Hall Grove Farm, Bagshot, Surrey, GU19 5HP
Postcode	GU19 5HP

APPENDIX 7 – REPORT RELIANCE

Notwithstanding any other provisions of this report and in consideration of the sum of ten pounds (£10.00) paid by both St Edward Homes Limited, Berkeley Homes (Western) Limited and Berkeley Homes plc, we Ramboll UK Limited hereby acknowledge receipt of the aforementioned consideration and hereby irrevocably acknowledge and agree that St Edward Homes Limited, Berkeley Homes (Western) Limited and Berkeley Homes plc and any parties acquiring an interest in the works to be carried out at the site and/or the property/properties in respect of which this report has been carried out and/or the property and/or the land in respect of which this report has been carried out or any part or parts thereof (the Project) and/or any party providing finance and/or refinance in connection with the Project and any contractors involved in the development of the site/property to which this report relates and their assigns shall have relied and will continue to rely on the findings of this report and in so doing we acknowledge a duty of care to them provided that the duty of care shall be no greater in terms of obligation than that owed to the company/body who has commissioned the report from us as if the beneficiary had been named jointly with the company/body who have commissioned the report in such commission/appointment.

WOOLDRIDGE

COTEC

W 613030

CONVEYANCE NOTE C (Weight and Vol.)

CONTROLLED WASTE TRANSFER NOTE

ULK EXCAVATION, TOP SOIL, PLANT HIRE,
ROUNDWORK CONTRACTORS
ALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 2-5-2017	VEHICLE REG. No: KV64 XHW	NAME OF PERSON IN CHARGE OF VEHICLE: TIGNEY
CUSTOMER: BERKLEY HOMES		

SITE ADDRESS: GREEN PARK
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading	Nett WAZ	Gross Weight of Vehicle	TONNES	M ³
-----------------	----------	-------------------------	--------	----------------

Description of Material	Muck Away	Tare Weight	
-------------------------	-----------	-------------	--

LORRY HIRE	Cash Sale	Net Weight	1x8
------------	-----------	------------	-----

HOURS WORKED	DESCRIPTION OF MATERIAL ☐ 17.01.07 Clean Hardcore ☐ 17.09.04 Mixed Construction ☐ 20.02.01 Garden / Park Waste ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood ☐ Other	Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in: (a) A sale or an agreement for the sale thereof made by weight. (b) An agreement for the carriage thereof made by weight or volume. Delete (a) or (b) as applicable. On behalf of the Seller SIGNED BY (DRIVER'S SIGNATURE):
--------------	---	---

TRAVELLING TIME	
-----------------	--

No. OF LOADS	
--------------	--

WHERE TIPPED	
--------------	--

CUBIC METERS	TIP CODE
--------------	----------

ADDRESS OF TIP/TRANSFER POINT	TRANSFER OF WASTE
-------------------------------	-------------------

THE BUGLE SUNBURY TW19 8SN	TRANSFER DATE	
	TRANSFER TIME	
	SITE LICENCE No.	

SIGNED BY TIP OPERATOR	SIGNED BY DRIVER
------------------------	------------------

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.	SIGNED BY PRODUCER/CUSTOMER	PRINT NAME
---	-----------------------------	------------

		J. WILKINSON
--	--	--------------

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613031

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 2-5-2017 VEHICLE REG. No: KV04 XKW NAME OF PERSON IN CHARGE OF VEHICLE: TERNY
CUSTOMER: BENKLEY HOMES

SITE ADDRESS: GREEN PARK READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading Non HAZ Gross Weight of Vehicle TONNES M³

Description of Material Muck AWAY Tare Weight

LORRY HIRE Cash Sale Net Weight 1x8

HOURS WORKED DESCRIPTION OF MATERIAL Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

TRAVELLING TIME ☐ 17.01.07 Clean Hardcore ☐ 17.09.04 Mixed Construction ☐ 20.02.01 Garden / Park Waste (a) A sale or an agreement for the sale thereof made by weight.

No. OF LOADS ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal (b) An agreement for the carriage thereof made by weight or volume.

WHERE TIPPED ☐ 17.06.05 Construction Asbestos Delete (a) or (b) as applicable. On behalf of the Seller SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS TIP CODE

ADDRESS OF TIP/TRANSFER POINT TRANSFER OF WASTE

THE BUGLE TRANSFER DATE
SUNBURY TW17 8SM TRANSFER TIME
SITE LICENCE No.

SIGNED BY TIP OPERATOR SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection. SIGNED BY PRODUCER/CUSTOMER PRINT NAME J WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD

WOOLDRIDGE

ECOTEC

W 613015

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27-4-2017 VEHICLE REG. No: KV64XKW NAME OF PERSON IN CHARGE OF VEHICLE: TERRY

CUSTOMER:

Berkley Homes
Green Park
Reading

SITE ADDRESS:

I confirm that I have fulfilled my duty to apply the waste hierarchy as
required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

NON HAZ

Gross Weight
of Vehicle

TONNES

M³

Description of Material

TRUCK PART

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1x8W

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and
relate to the aggregates, sub-based materials and
arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made
by weight.

(b) An agreement for the carriage thereof made by
weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY DRIVER

SIGNED BY TIP OPERATOR

The producer of this load of
waste certifies that recyclable
and non-hazardous materials
have been separated prior to
collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS
ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE
PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613020

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28-4-2017 VEHICLE REG. No: W64XKW NAME OF PERSON IN CHARGE OF VEHICLE: TERN7

CUSTOMER:

BENKLEY HOMES
GREEN PARK
READING

SITE ADDRESS:

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

NON HAZ

Gross Weight
of Vehicle

TONNES

M³

Description of Material

MUCK AWAY

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1x8

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BUGLE
W17897 SUNDURY

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

[Signature]

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

[Signature]

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613019

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28-4-2017 VEHICLE REG. No: LV64XKW NAME OF PERSON IN CHARGE OF VEHICLE: TERRY
CUSTOMER: BENKLEY HOMES

SITE ADDRESS: GREEN PARK READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011		SIC CODE	
Time of Loading	NON HAZ	Gross Weight of Vehicle	TONNES
Description of Material	Muck PHA7	Tare Weight	M ³
LORRY HIRE	Cash Sale	Net Weight	1x8
HOURS WORKED	DESCRIPTION OF MATERIAL		Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in: (a) A sale or an agreement for the sale thereof made by weight. (b) An agreement for the carriage thereof made by weight or volume. Delete (a) or (b) as applicable. On behalf of the Seller SIGNED BY (DRIVER'S SIGNATURE):
TRAVELLING TIME	☐ 17.01.07 Clean Hardcore		
No. OF LOADS	☐ 17.09.04 Mixed Construction		
WHERE TIPPED	☐ 20.02.01 Garden / Park Waste		
CUBIC METERS	☒ 17.05.04 Soil & Stones		
		☐ 17.04.07 Mixed Metal	
		☐ 17.06.05 Construction Asbestos	
		☐ 17.02.01 Wood	
		☐ Other	
TIP CODE			

ADDRESS OF TIP/TRANSFER POINT	TRANSFER OF WASTE
THE BUGLE TW178SN SUNBURY	TRANSFER DATE
	TRANSFER TIME
	SITE LICENCE No.
SIGNED BY TIP OPERATOR	SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER: PRINT NAME: J. WILKINSON

WOOLDRIDGE
ECOTEC

W 613018

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28-4-2017 VEHICLE REG. No: KV64 XKW NAME OF PERSON IN CHARGE OF VEHICLE: TERRY

CUSTOMER: BENKLEY HOMES

SITE ADDRESS: GREEN PARK READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011 SIC CODE

Time of Loading NON HAZ Gross Weight of Vehicle TONNES M³

Description of Material Muck Away Tare Weight

LORRY HIRE Cash Sale Net Weight 18.8

HOURS WORKED TRAVELLING TIME No. OF LOADS WHERE TIPPED CUBIC METERS TIP CODE DESCRIPTION OF MATERIAL
☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other
Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:
(a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.
On behalf of the Seller
SIGNED BY (DRIVER'S SIGNATURE):

ADDRESS OF TIP/TRANSFER POINT TRANSFER OF WASTE

THE BUGLE IW17897 SUNDUNY TRANSFER DATE TRANSFER TIME SITE LICENCE No.

SIGNED BY TIP OPERATOR SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection. SIGNED BY PRODUCER/CUSTOMER PRINT NAME J.WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD

WOOLDRIDGE
ECOTEC

W 613017

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28-4-2017	VEHICLE REG. No: KV64XKW	NAME OF PERSON IN CHARGE OF VEHICLE: TERN7
-----------------	--------------------------	--

CUSTOMER: BERKLEY HOMES

SITE ADDRESS: GREEN PARK
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading	Non Haz	Gross Weight of Vehicle	TONNES	M ³
-----------------	---------	-------------------------	--------	----------------

Description of Material	Muck PWA7	Tare Weight	
-------------------------	-----------	-------------	--

LORRY HIRE	Cash Sale	Net Weight	
------------	-----------	------------	--

HOURS WORKED	DESCRIPTION OF MATERIAL ☐ 17.01.07 Clean Hardcore ☐ 17.09.04 Mixed Construction ☐ 20.02.01 Garden / Park Waste ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood ☐ Other	Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in: (a) A sale or an agreement for the sale thereof made by weight. (b) An agreement for the carriage thereof made by weight or volume. Delete (a) or (b) as applicable. On behalf of the Seller SIGNED BY (DRIVER'S SIGNATURE):
TRAVELLING TIME		
No. OF LOADS		
WHERE TIPPED		

CUBIC METERS	TIP CODE
--------------	----------

ADDRESS OF TIP/TRANSFER POINT	TRANSFER OF WASTE	
THE BUGLE SUNBURY TW17 8ST	TRANSFER DATE	
	TRANSFER TIME	
	SITE LICENCE No.	
	SIGNED BY TIP OPERATOR	SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.	SIGNED BY PRODUCER/CUSTOMER	PRINT NAME
		J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD

WOOLDRIDGE

ECOTEC

W 613007

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27-4-2017 VEHICLE REG. No: KVG4 XKW NAME OF PERSON IN CHARGE OF VEHICLE: IERD7
CUSTOMER: BERKLEY HOMES

SITE ADDRESS: GREEN PARK READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading	Non HAZ	Gross Weight of Vehicle	TONNES	M ³
Description of Material	Muck Away	Tare Weight		
LORRY HIRE	Cash Sale	Net Weight	1 x 2	

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
- ☐ 17.09.04 Mixed Construction
- ☐ 20.02.01 Garden / Park Waste
- ☒ 17.05.04 Soil & Stones
- ☐ 17.04.07 Mixed Metal
- ☐ 17.06.05 Construction Asbestos
- ☐ 17.02.01 Wood
- ☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS	TIP CODE
--------------	----------

ADDRESS OF TIP/TRANSFER POINT	TRANSFER OF WASTE
THE BUGLE	TRANSFER DATE
M17 8SN SUNBURY	TRANSFER TIME
SIGNED BY TIP OPERATOR	SITE LICENCE No.
	SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

J. WILKINSON

WOOLDRIDGE

ECOTEC

W 613008

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27-4-2017 VEHICLE REG. No: AV04XVW NAME OF PERSON IN CHARGE OF VEHICLE: TERRY

CUSTOMER:

BERKLEY HOMES
GREEN PARK
READING

SITE ADDRESS:

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

NON HAZ

Gross Weight
of Vehicle

TONNES

M³

Description of Material

MUCK AWAY

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1.8

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:
(a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.
On behalf of the Seller
SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BUGLE
W17 8SN SUNBURY

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613009

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27-4-2017 VEHICLE REG. No: KV04 XKW NAME OF PERSON IN CHARGE OF VEHICLE: JENNY
CUSTOMER: BERKLEY HOMES

SITE ADDRESS: GREEN PARK READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading Non HAZ Gross Weight of Vehicle TONNES M³

Description of Material Muck PWA7 Tare Weight

LORRY HIRE Cash Sale Net Weight 1x8

HOURS WORKED DESCRIPTION OF MATERIAL

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS TIP CODE

ADDRESS OF TIP/TRANSFER POINT TRANSFER OF WASTE

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR SIGNED BY DRIVER

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613014

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27-4-2017 VEHICLE REG. No: KV64XKW NAME OF PERSON IN CHARGE OF VEHICLE: TERRY

CUSTOMER:

BARKLEY HOMES
GREEN PARK
READING

SITE ADDRESS:

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

NON HAZ

Gross Weight
of Vehicle

TONNES

M³

Description of Material

MUCK AWAY

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1x8

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BUGLE
W19 6SN SUNBURN

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

[Signature]

J. WILKINSON

WOOLDRIDGE

ECOTEC

W 613016

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28-4-2017 VEHICLE REG. No: KV64 XKW NAME OF PERSON IN CHARGE OF VEHICLE: TERRY
CUSTOMER: BENKLEY HOMES

SITE ADDRESS: GREEN PARK DERRING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading NON MAZ Gross Weight of Vehicle TONNES M³

Description of Material MUCK MAZ Tare Weight

LORRY HIRE Cash Sale Net Weight 1x8

HOURS WORKED
TRAVELLING TIME
No. OF LOADS
WHERE TIPPED
DESCRIPTION OF MATERIAL
☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other
Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:
(a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.
On behalf of the Seller
SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS TIP CODE

ADDRESS OF TIP/TRANSFER POINT TRANSFER OF WASTE

THE BUGLE
W178517 SUNBURY
SIGNED BY TIP OPERATOR
TRANSFER DATE
TRANSFER TIME
SITE LICENCE No.
SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.
SIGNED BY PRODUCER/CUSTOMER PRINT NAME J. WILKINSON
THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 614277CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTEBULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPYRegistered Waste Carrier
Registration No. CBDU81963
Issued by Environment AgencyDATE: **27-4-17** VEHICLE REG. No: **KUG SHW** NAME OF PERSON IN CHARGE OF VEHICLE: **MARK**

CUSTOMER:

BERKELEY HOMES
GREEN PARCH
READING

SITE ADDRESS:

I confirm that I have fulfilled my duty to apply the waste hierarchy as
required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

NON HAZ W/A

Tare Weight

148

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKEDTRAVELLING
TIMENo. OF
LOADSWHERE
TIPPED**DESCRIPTION OF MATERIAL**

- ☐
- 17.01.07 Clean Hardcore
-
- ☐
- 17.09.04 Mixed Construction
-
- ☐
- 20.02.01 Garden / Park Waste
-
- ☒
- 17.05.04 Soil & Stones
-
- ☐
- 17.04.07 Mixed Metal
-
- ☐
- 17.06.05 Construction Asbestos
-
- ☐
- 17.02.01 Wood
-
- ☐
- Other

Certified that the above particulars are true and
relate to the aggregates, sub-based materials and
arising materials being conveyed or disposed of in:(a) A sale or an agreement for the sale thereof made
by weight.(b) An agreement for the carriage thereof made by
weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):



CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

BULLE NURSERRIES
SUNBURY TW17 8SN

TRANSFER OF WASTE

TRANSFER DATE

27-4-17

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR



SIGNED BY DRIVER

The producer of this load of
waste certifies that recyclable
and non-hazardous materials
have been separated prior to
collection.**SIGNED BY PRODUCER/CUSTOMER** **PRINT NAME****J. WILKINSON**THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS
ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE
PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 614969

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY


Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27/4/17 VEHICLE REG. No: KPIU TNC NAME OF PERSON IN CHARGE OF VEHICLE: Chris
CUSTOMER: BERKLEY HOMES

SITE ADDRESS: GREEN PARK
Reading


I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011 SIC CODE

Time of Loading	Gross Weight of Vehicle	TONNES	M ³
Description of Material NON-HAZ MUCK AWAY	Tare Weight	1 x 8	
LORRY HIRE	Cash Sale	Net Weight	WHEELER

HOURS WORKED	DESCRIPTION OF MATERIAL ☐ 17.01.07 Clean Hardcore ☐ 17.09.04 Mixed Construction ☐ 20.02.01 Garden / Park Waste ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood ☐ Other	Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in: (a) A sale or an agreement for the sale thereof made by weight. (b) An agreement for the carriage thereof made by weight or volume. Delete (a) or (b) as applicable. On behalf of the Seller SIGNED BY (DRIVER'S SIGNATURE): 
TRAVELLING TIME		
No. OF LOADS		
WHERE TIPPED		
CUBIC METERS	TIP CODE	

ADDRESS OF TIP/TRANSFER POINT THE BULLS SUNBURY TW17SN	TRANSFER OF WASTE TRANSFER DATE: 27/4/17 TRANSFER TIME: SITE LICENCE No.: SIGNED BY DRIVER: 
SIGNED BY TIP OPERATOR: 	

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER 	PRINT NAME J. WILKINSON
--	----------------------------

WOOLDRIDGE

ECOTEC

W 613550

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27.4.17 VEHICLE REG. No: KM 65 KOU NAME OF PERSON IN CHARGE OF VEHICLE: MANJIS

CUSTOMER: BERKELEYS HOMES.

SITE ADDRESS: GREEN PARK
READING.

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

NOV HAZ

Gross Weight
of Vehicle

TONNES

M³

Description of Material

MICK ATKINS

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1.08W

1

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BUGLE NURSERIES
SUNBURY
TW17 8NS

TRANSFER DATE

27.4.17

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

[Signature]

SIGNED BY DRIVER

[Signature]

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

[Signature]

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 614968

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27/4/17 VEHICLE REG. No: KPIU FNC NAME OF PERSON IN CHARGE OF VEHICLE: CUNIS

CUSTOMER: BERKEEY HOMES

SITE ADDRESS: GREEN PARK
Reading

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading Gross Weight of Vehicle TONNES M³

Description of Material NON-HAZ MUCK AWAY Tare Weight 1x8

LORRY HIRE Cash Sale Net Weight WHEELER

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS TIP CODE

ADDRESS OF TIP/TRANSFER POINT TRANSFER OF WASTE

THE BULLS TRANSFER DATE 27/4/17
SUNBURY TW17SN TRANSFER TIME
SITE LICENCE No.

SIGNED BY TIP OPERATOR SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

J. Wilkinson

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 614276

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27-4-17 VEHICLE REG. No: KU05HFW NAME OF PERSON IN CHARGE OF VEHICLE: MARK

CUSTOMER: BERKELEY HOMES

SITE ADDRESS: GREEN PARK READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading Gross Weight of Vehicle TONNES M³

Description of Material NON HAZ Tare Weight 1 LOAD

LORRY HIRE Cash Sale M/A Net Weight

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS TIP CODE

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
- ☐ 17.09.04 Mixed Construction
- ☐ 20.02.01 Garden / Park Waste
- ☒ 17.05.04 Soil & Stones
- ☐ 17.04.07 Mixed Metal
- ☐ 17.06.05 Construction Asbestos
- ☐ 17.02.01 Wood
- ☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

ADDRESS OF TIP/TRANSFER POINT TRANSFER OF WASTE

BUCKLE NURSRIES
SUNBURY, TW17 8SN

TRANSFER DATE 27-4-17

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 615472

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27/4/17 VEHICLE REG. No: KP16 XTD NAME OF PERSON IN CHARGE OF VEHICLE: Don.
CUSTOMER: Borkley Homes

SITE ADDRESS: Green Park Reading

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading Gross Weight of Vehicle TONNES M³

Description of Material NON-HAZ - W/A Tare Weight

LORRY HIRE Cash Sale Net Weight

HOURS WORKED DESCRIPTION OF MATERIAL

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

TRANSFER DATE 27/4/17

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

WOOLDRIDGE

ECOTEC

W 613693

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27/4/17 VEHICLE REG. No: KN16 GXS NAME OF PERSON IN CHARGE OF VEHICLE: LEE

CUSTOMER: BERKELEY Hm's

SITE ADDRESS: GREEN PARK
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BUGLE Nurseries
HALLFORD RD
SUNBURY

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE
ECOTEC

W 597932

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27-4-17	VEHICLE REG. No: EY12 YGM	NAME OF PERSON IN CHARGE OF VEHICLE: MICK
------------------	------------------------------	--

CUSTOMER: BERKELEY HOMES

SITE ADDRESS: GREEN PARK
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading NONHAZ U/A	Gross Weight of Vehicle	TONNES	M ³
-------------------------------	-------------------------	--------	----------------

Description of Material	Tare Weight		
-------------------------	-------------	--	--

LORRY HIRE	Cash Sale	Net Weight	1X8W
------------	-----------	------------	------

HOURS WORKED
TRAVELLING TIME
No. OF LOADS
WHERE TIPPED
CUBIC METERS
TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:
(a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.
On behalf of the Seller
SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

☐ 17.01.07 Clean Hardcore	☒ 17.05.04 Soil & Stones	☐ 17.04.07 Mixed Metal
☐ 17.09.04 Mixed Construction	☐ 17.06.05 Construction Asbestos	☐ 17.02.01 Wood
☐ 20.02.01 Garden / Park Waste	☐ Other	

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER
PRINT NAME

ADDRESS OF TIP/TRANSFER POINT THE BULLY WORSWICKS TW14 8SN	TRANSFER OF WASTE
	TRANSFER DATE
	TRANSFER TIME
	SITE LICENCE No.

IF MULTIPLE TRANSFER BETWEEN DATES

SIGNED BY TIP OPERATOR	SIGNED BY DRIVER
------------------------	------------------

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597933

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27-4-17 VEHICLE REG. No: EY12 YSM NAME OF PERSON IN CHARGE OF VEHICLE: MICK
CUSTOMER: BERKELEY HOMES

SITE ADDRESS: GREEN PARK
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading Gross Weight of Vehicle TONNES M³

Description of Material NON HAZ M/A Tare Weight

LORRY HIRE Cash Sale Net Weight 1x8W

HOURS WORKED
TRAVELLING TIME
No. OF LOADS
WHERE TIPPED
CUBIC METERS

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:
(a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal
☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood
☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BUGLE NURSERY
SHEPPERTON
TW17 8SN
TRANSFER DATE
TRANSFER TIME
SITE
LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 602620

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27/04/17 VEHICLE REG. No: EY12 YGP NAME OF PERSON IN CHARGE OF VEHICLE: Lee
CUSTOMER: BARKLEY HOMES
GREEN PARK
READING

SITE ADDRESS:

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

2/4 - m/4

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1x8w

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BARKLEY NURSRIES

TR17 8SA

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

J. Wilkinson

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 602621

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27/06/17 VEHICLE REG. No: BY12 YAP NAME OF PERSON IN CHARGE OF VEHICLE: Lee
CUSTOMER: BERKELEY HOMES

SITE ADDRESS: GREEN PARK
READING.

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

N/H M/A

Gross Weight
of Vehicle

TONNES

M³

Description of Material

Tare Weight

1x8w

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

DOCK NUBRIES
TW17 8SA.

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME



J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 602619

CONVEYANCE NOTE C (Weight and Vol.)

CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27/04/17 VEHICLE REG. No: EY12 YLP NAME OF PERSON IN CHARGE OF VEHICLE: LEE

CUSTOMER: BERNARD HOMES

SITE ADDRESS: GREEN PARK READING.

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading Gross Weight of Vehicle TONNES M³

Description of Material m/a Tare Weight

LORRY HIRE Cash Sale Net Weight 1x8w

HOURS WORKED DESCRIPTION OF MATERIAL

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS TIP CODE

ADDRESS OF TIP/TRANSFER POINT TRANSFER OF WASTE

BURLE TW17 8JA TRANSFER DATE TRANSFER TIME SITE LICENCE No.

SIGNED BY TIP OPERATOR SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection. SIGNED BY PRODUCER/CUSTOMER PRINT NAME J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597931

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27-4-07 VEHICLE REG. No: EY12 YQM NAME OF PERSON IN CHARGE OF VEHICLE: Mick
CUSTOMER: BERKELEY HOMES

SITE ADDRESS: GREEN PARK
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading Gross Weight of Vehicle TONNES M³

Description of Material NON HAZ M/A Tare Weight

LORRY HIRE Cash Sale Net Weight 1X8W

HOURS WORKED Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

TRAVELLING TIME (a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.

No. OF LOADS On behalf of the Seller

WHERE TIPPED SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS DESCRIPTION OF MATERIAL

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BUYLE NURSERIES
SHEPPERTON
TW17 8SN

IF MULTIPLE TRANSFER BETWEEN DATES

SIGNED BY TIP OPERATOR SIGNED BY DRIVER

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 614966

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27/4/17 VEHICLE REG. No: KPIU FNC NAME OF PERSON IN CHARGE OF VEHICLE: Chris
CUSTOMER:

BEEKLEY HOMES

SITE ADDRESS: GREEN PARK
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

NON-HAZ
MUCK AWAY

Tare Weight

1 x 8

LORRY HIRE

Cash Sale

Net Weight

WHEELER

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BUCK

TRANSFER DATE

27/4/17

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 614274

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27-4-17 VEHICLE REG. No: KUB5HFW NAME OF PERSON IN CHARGE OF VEHICLE: MARK

CUSTOMER:

BENKELEY HOMES
GREEN PARCH
READING

SITE ADDRESS:

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

NON HAZ

Tare Weight

1 LOAD

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BURGE NURSERIES
TW17 8SN


TRANSFER DATE

27-4-17


TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR



SIGNED BY DRIVER



The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME



J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613691

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27/4/17 VEHICLE REG. No: KN16 CXT NAME OF PERSON IN CHARGE OF VEHICLE: LEE

CUSTOMER: BERKELEY Hm's

SITE ADDRESS: GREEN PARK
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BOULE NURSERIES
HARFORD RD
SUNBURY

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 602618

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27-4-17 VEHICLE REG. No: EY12 YSP NAME OF PERSON IN CHARGE OF VEHICLE: LEE

CUSTOMER:

BENKELEY HOMES
GREEN PARK
READING

SITE ADDRESS:

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

N/H M/A

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1 x 8W

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BUGLE

TW17 8SN

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME



J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597930

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27-4-17	VEHICLE REG. No: EY12 YSM	NAME OF PERSON IN CHARGE OF VEHICLE: MICK
-------------------------	-------------------------------------	---

CUSTOMER:

BERKELEY HOMES

SITE ADDRESS: **GREEN PARK**
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading NOWHAZ M/A	Gross Weight of Vehicle	TONNES	M ³
--------------------------------------	-------------------------	--------	----------------

Description of Material	Tare Weight		
-------------------------	-------------	--	--

LORRY HIRE	Cash Sale	Net Weight 1X8W	
------------	-----------	---------------------------	--

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal

☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood

☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

TRANSFER

DATE

TRANSFER

TIME

SITE

LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613682

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

3ULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301
HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 25/4/17 VEHICLE REG. No: KN16 CXS NAME OF PERSON IN CHARGE OF VEHICLE: LEE
CUSTOMER: BERKLEY Hm's

SITE ADDRESS: GREEN PK
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight of Vehicle

TONNES

M³

Description of Material

Tare Weight

1 x 8

LORRY HIRE

Cash Sale

Net Weight

WHEELER

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:


(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):



ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BUCKLE NURSERY
HALLFORD RD
SUNBURY

TRANSFER DATE

25/4/17

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR


SIGNED BY DRIVER



The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME



MICK ATKINS

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE

WOOLDRIDGE

ECOTEC

W 613546

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 25.4.17 VEHICLE REG. No: KM65KOU NAME OF PERSON IN CHARGE OF VEHICLE: MANSIT

CUSTOMER: BERKLEY HOMES

SITE ADDRESS: GREEN PARK

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading: 11.00 AM Gross Weight of Vehicle: TONNES M³

Description of Material: Mixed Ash Tare Weight

LORRY HIRE: Cash Sale Net Weight

HOURS WORKED: DESCRIPTION OF MATERIAL

TRAVELLING TIME: ☐ 17.01.07 Clean Hardcore

No. OF LOADS: ☐ 17.09.04 Mixed Construction

WHERE TIPPED: ☐ 20.02.01 Garden / Park Waste

CUBIC METERS: ☒ 17.05.04 Soil & Stones

ADDRESS OF TIP/TRANSFER POINT: ☐ 17.04.07 Mixed Metal

TRANSFER OF WASTE: ☐ 17.06.05 Construction Asbestos

SIGNED BY TIP OPERATOR: ☐ 17.02.01 Wood

SIGNED BY DRIVER: ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 615403

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301
HAULAGE MANAGER - MICK ATKINS 07831 859111

DATE: 28.6.17 VEHICLE REG. No: KX15NOR NAME OF PERSON IN CHARGE OF VEHICLE: Andy
CUSTOMER: Berkeley Nurseries

SITE ADDRESS: Green Rd
Reading

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading Gross Weight of Vehicle TONNES M³

Description of Material Non Waz M/A Tare Weight

LORRY HIRE Cash Sale Net Weight 1x8W 6m

HOURS WORKED DESCRIPTION OF MATERIAL

TRAVELLING TIME

No. OF LOADS 1x8W

WHERE TIPPED

CUBIC METERS TIP CODE

ADDRESS OF TIP/TRANSFER POINT TRANSFER OF WASTE

Busle Nurseries

TRANSFER DATE 25 4 17

TRANSFER TIME

SITE LICENCE No. 6

SIGNED BY TIP OPERATOR SIGNED BY DRIVER

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY/UNLAWFUL DAMAGE CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 612748

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 25 4 17 VEHICLE REG. No: KX18NPF NAME OF PERSON IN CHARGE OF VEHICLE: ANoy
CUSTOMER: BERULOT LUMES

SITE ADDRESS: GREEN PK
ROADINS

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

NON
LIAZ

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1x8W 600

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

CUBIC METERS

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BUTLE NURSERY'S

TRANSFER DATE

25.4.17

TRANSFER TIME

SITE LICENCE No.

6

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

M. H. H. H.

M. H. H. H.

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS APPROPRIATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE

WOOLDRIDGE

ECOTEC

W 612890

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 25-4-17 VEHICLE REG. No: R11BLZ NAME OF PERSON IN CHARGE OF VEHICLE: COLLIN

CUSTOMER:

BERKLEY HOUSES

SITE ADDRESS:

GREEN PARK
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

NON HAZ.

Gross Weight
of Vehicle

TONNES

M³

Description of Material

MUCK AWAY

Tare Weight

1 X 80 LOAD

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:
(a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

COLLIN

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BUGLE NURSERIES
SUNBURY
TW17 8NS

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE

WOOLDRIDGE

ECOTEC

W 613155

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 25.4.17 VEHICLE REG. No: T111 PPR NAME OF PERSON IN CHARGE OF VEHICLE: Is

CUSTOMER:

Banket Homes
Green Park
Reading

SITE ADDRESS:

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

Tare Weight

1x8

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE Bruce Nurseries
Shepperton
TW17 8SW

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

MURPHY

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE
ECOTEC

W 613153

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

HAULAGE MANAGER - MICK ATKINS 07831 859111

DATE: 25.4.17	VEHICLE REG. No: TUU PPP	NAME OF PERSON IN CHARGE OF VEHICLE: JA
------------------	-----------------------------	--

CUSTOMER: Bankley Homes

SITE ADDRESS: Green Park
Reading

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading	Gross Weight of Vehicle	TONNES	M ³
-----------------	-------------------------	--------	----------------

Description of Material Non Haz MIA	Tare Weight 1x8w
--	---------------------

LORRY HIRE	Cash Sale	Net Weight
------------	-----------	------------

HOURS WORKED	DESCRIPTION OF MATERIAL ☐ 17.01.07 Clean Hardcore ☐ 17.09.04 Mixed Construction ☐ 20.02.01 Garden / Park Waste ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood ☐ Other	Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in: ☒ A sale or an agreement for the sale thereof made by weight. (b) An agreement for the carriage thereof made by weight or volume. Delete (a) or (b) as applicable. On behalf of the Seller SIGNED BY (DRIVER'S SIGNATURE):
TRAVELLING TIME		
No. OF LOADS		
WHERE TIPPED		
CUBIC METERS	TIP CODE	

ADDRESS OF TIP/TRANSFER POINT The Bugle Nurseries Shipton TW17 8SN	TRANSFER OF WASTE TRANSFER DATE TRANSFER TIME SITE LICENCE No.
---	---

SIGNED BY TIP OPERATOR 	SIGNED BY DRIVER
----------------------------	----------------------

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER 	PRINT NAME M. MAROTT
---------------------------------	-------------------------

WOOLDRIDGE

ECOTEC

W 602613

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28/4/17 VEHICLE REG. No: LY12 YSP NAME OF PERSON IN CHARGE OF VEHICLE: JCR

CUSTOMER:

BERKELEY HOMES

SITE ADDRESS:

GREEN PARK

READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

1/142 WOOD AWAY

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

No. OF
LOADS

WHERE
TIPPED

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

M. MCKEAT

M. MCKEAT

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS NECESSARY AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE

WOOLDRIDGE

ECOTEC

W602615

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 25/4/17 VEHICLE REG. No: EY12 YAP NAME OF PERSON IN CHARGE OF VEHICLE: JOE

CUSTOMER:

Berkley Homes
Green Park
Romney

SITE ADDRESS:

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

N/HAZ MUCK AWAY

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:
(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

1x8w

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

Bulk Wastewater
Upper Walsford Road
Berkley
SW17 8SN

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

M. McLETT

M. McLETT

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

VOOLDRIDGE

WOTEC

LK EXCAVATION, TOP SOIL, PLANT HIRE,
OUNDWORK CONTRACTORS
ALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
t: (01276) 470333 Fax: (01276) 470301
AULAGE MANAGER - MICK ATKINS 07831 859111

W 597920

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: **25-4-17** VEHICLE REG. No: **EY12 YGM** NAME OF PERSON IN CHARGE OF VEHICLE: **Mick**

CUSTOMER:

BERKLEY HOMES
GREEN PARK
READING

SITE ADDRESS:

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

NIHAZ M/A

Tare Weight

Net Weight

LORRY HIRE

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

THE BUCKLE
NURSERIES
SHPPER TOWN
TW17 8SN.

TRANSFER OF WASTE

TRANSFER

DATE

TRANSFER

TIME

SITE

LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY
COMPANY AND ITS AGENTS WILL NOT BE

WOOLDRIDGE

ECOTEC

W 613157CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTEBULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPYRegistered Waste Carrier
Registration No. CBDU81963
Issued by Environment AgencyDATE: **25.4.17** VEHICLE REG. No: **T111 PPP** NAME OF PERSON IN CHARGE OF VEHICLE: **IA**

CUSTOMER:

Banquet Homes
Green Park
Reading

SITE ADDRESS:

I confirm that I have fulfilled my duty to apply the waste hierarchy as
required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKEDTRAVELLING
TIMENo. OF
LOADSWHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐
- 17.01.07 Clean Hardcore
-
- ☐
- 17.09.04 Mixed Construction
-
- ☐
- 20.02.01 Garden / Park Waste
-
- ☒
- 17.05.04 Soil & Stones
-
- ☐
- 17.04.07 Mixed Metal
-
- ☐
- 17.06.05 Construction Asbestos
-
- ☐
- 17.02.01 Wood
-
- ☐
- Other

Certified that the above particulars are true and
relate to the aggregates, sub-based materials and
arising materials being conveyed or disposed of in:
~~(a)~~ A sale or an agreement for the sale thereof made
by weight.(b) An agreement for the carriage thereof made by
weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BUFILE
SHEPPARTON
TW17 8SN

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of
waste certifies that recyclable
and non-hazardous materials
have been separated prior to
collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS
ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE
PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597917

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 25-4-17 VEHICLE REG. No: EY12 YSM NAME OF PERSON IN CHARGE OF VEHICLE: MICK

CUSTOMER:

BERKELEY HOMES

SITE ADDRESS: GREEN PARK

REDDING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

N/HAZ M/A

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal

☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood

☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

TW17 8SN
THE BUCKEN NURSERIES
SHEPPERTON.

TRANSFER

DATE

TRANSFER

TIME

SITE

LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 612895

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 26-4-17 VEHICLE REG. No: R113UE NAME OF PERSON IN CHARGE OF VEHICLE: COLIN

CUSTOMER:

Berkley Homes

SITE ADDRESS:

Green Park

Reading

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

NON HAZ

Gross Weight
of Vehicle

TONNES

M³

Description of Material

Muck Away

Tare Weight

1 x 8.5 Load

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

Colin

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

Tier Bugle Nurseries
Sunbury
TW17 8SN

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

[Signature]

SIGNED BY DRIVER

Colin

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

[Signature]

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613158

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 26.4.17 VEHICLE REG. No: T111 PPP NAME OF PERSON IN CHARGE OF VEHICLE: Ian

CUSTOMER:

Bankers Homes
Circus Park
Reading.

SITE ADDRESS:

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

The Bruce Nurseries
Sherpinton
TW17 8SN

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

J. Wilkinson

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 615468

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 26/4/17 VEHICLE REG. No: KP6 XED NAME OF PERSON IN CHARGE OF VEHICLE: Don
CUSTOMER: Bonkows Homes

SITE ADDRESS: Green Park
Mordun

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

WON-142-41/A

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BUGLE WILSON'S
SHOPPOTON TW17 8SN

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

J. WILKINSON

J. WILKINSON

WOOLDRIDGE

ECOTEC

W 613689

CONVEYANCE NOTE C (Weight and Vol.)

CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 26/4/17 VEHICLE REG. No: KN16 CXT NAME OF PERSON IN CHARGE OF VEHICLE: LEE

CUSTOMER:

BERKELEY Hm's

SITE ADDRESS:

GREEN PARK
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as
required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

Tare Weight

Non HAZ
M/Away

1 x 8

LORRY HIRE

Cash Sale

Net Weight

WHEELER

HOURS
WORKEDTRAVELLING
TIMENo. OF
LOADSWHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and
relate to the aggregates, sub-based materials and
arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made
by weight.

(b) An agreement for the carriage thereof made by
weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BUGLE Nurseries
Halsford Rd
SUNBURY

TRANSFER DATE

26/4/17

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of
waste certifies that recyclable
and non-hazardous materials
have been separated prior to
collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS
ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE
PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 614271CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTEBULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPYRegistered Waste Carrier
Registration No. CBDU81963
Issued by Environment AgencyDATE: **26-4-17** VEHICLE REG. No: **KUBS HFW** NAME OF PERSON IN CHARGE OF VEHICLE: **MARK**

CUSTOMER:

BERKELEY HOMES

SITE ADDRESS:

GREEN PARK**READING**I confirm that I have fulfilled my duty to apply the waste hierarchy as
required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

NON HAZ

Tare Weight

1 LOAD

LORRY HIRE

Cash Sale

N/A

Net Weight

HOURS
WORKEDTRAVELLING
TIMENo. OF
LOADSWHERE
TIPPED**DESCRIPTION OF MATERIAL**

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and
relate to the aggregates, sub-based materials and
arising materials being conveyed or disposed of in:
(a) A sale or an agreement for the sale thereof made
by weight.
(b) An agreement for the carriage thereof made by
weight or volume.
Delete (a) or (b) as applicable.
On behalf of the Seller
SIGNED BY (DRIVER'S SIGNATURE):



CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

TRANSFER DATE

26-4-17


TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of
waste certifies that recyclable
and non-hazardous materials
have been separated prior to
collection.

SIGNED BY PRODUCER/CUSTOMER**PRINT NAME****J. WILKINSON**

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS
ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE
PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 615405

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 26 4 17	VEHICLE REG. No: KXISNAP	NAME OF PERSON IN CHARGE OF VEHICLE: Andy
-------------------------	------------------------------------	---

CUSTOMER:

Berkley James

SITE ADDRESS:

**Green PK
Roads**

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

**new use
MIA**

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1292500

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

1 x 2 loads

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
- ☐ 17.09.04 Mixed Construction
- ☒ 20.02.01 Garden / Park Waste
- ☒ 17.05.04 Soil & Stones
- ☐ 17.04.07 Mixed Metal
- ☐ 17.06.05 Construction Asbestos
- ☐ 17.02.01 Wood
- ☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

[Signature]

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BUSCK NORSOYS

TRANSFER DATE

25. 4. 17

SUNBU

TW178 SW

TRANSFER TIME

SITE LICENCE No.

60

SIGNED BY TIP OPERATOR

[Signature]

SIGNED BY DRIVER

[Signature]

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

[Signature]

J. WILKINS

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613549

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 26.4.17 VEHICLE REG. No: KM 65 ROU NAME OF PERSON IN CHARGE OF VEHICLE: MICK ATKINS

CUSTOMER:

BERKLEY HOMES

SITE ADDRESS:

GREEN PARK BENDING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

NOV HAZ

Gross Weight
of Vehicle

TONNES

M³

Description of Material

MICK ATKINS

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1.78W

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☐ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BOYLE NURSERIES

SUNBURY

TW17 8 NS.

TRANSFER DATE

26.4.17

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

[Signature]

SIGNED BY DRIVER

[Signature]

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

[Signature]

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY/VEHICLES CAUSED BY THE WASTE CARRIER'S LOADS.

WOOLDRIDGE

ECOTEC

W 597929

CONVEYANCE NOTE C (Weight and Vol.)

CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 26-4-17	VEHICLE REG. No: EY12 YEM	NAME OF PERSON IN CHARGE OF VEHICLE: MICK
CUSTOMER:		

SITE ADDRESS:	BERKELEY HOUSES GREEN PARK READING
---------------	---

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading	Gross Weight of Vehicle	TONNES	M ³
Description of Material NON HAZ M/A	Tare Weight		
LORRY HIRE	Cash Sale	Net Weight	1X8W

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal

☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood

☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BUGLE NURSERIES SHEPPERTON TW17 8SN	TRANSFER DATE	
	TRANSFER TIME	
	SITE LICENCE No.	

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597927

CONVEYANCE NOTE C (Weight and Vol.)

CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 26-4-17	VEHICLE REG. No: EY12 YEM	NAME OF PERSON IN CHARGE OF VEHICLE: Mick
CUSTOMER:		

BERKELEY HOMESSITE ADDRESS: **GREEN PARK****READING**

I confirm that I have fulfilled my duty to apply the waste hierarchy as
required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading	Gross Weight of Vehicle	TONNES	M ³
-----------------	----------------------------	--------	----------------

Description of Material	Tare Weight	
-------------------------	-------------	--

NONHAZ M/A

LORRY HIRE	Cash Sale	Net Weight	1X860
------------	-----------	------------	--------------

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and
arising materials being conveyed or disposed of in:

- (a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal
☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood
☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been
separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BUYLE NURSERIES SHEPPERTON TW17 8SN	TRANSFER DATE	
	TRANSFER TIME	
	SITE	
	LICENCE No.	

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY
WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE
LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597925CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTEBULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPYRegistered Waste Carrier
Registration No. CBDU81963
Issued by Environment AgencyDATE: **26-4-17** VEHICLE REG. No: **EY12 4SM** NAME OF PERSON IN CHARGE OF VEHICLE: **MICK**

CUSTOMER:

BERKELEY HOME

SITE ADDRESS:

**GREEN PARK
READDINGS**I confirm that I have fulfilled my duty to apply the waste hierarchy as
required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

NON HAZ M/A

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1 x 8 wheel

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and
arising materials being conveyed or disposed of in:

- (a) A sale or an agreement for the sale thereof made by weight.
-
- (b) An agreement for the carriage thereof made by weight or volume.
-
- Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

- ☐
- 17.01.07 Clean Hardcore
- ☒
- 17.05.04 Soil & Stones
- ☐
- 17.04.07 Mixed Metal
-
- ☐
- 17.09.04 Mixed Construction
- ☐
- 17.06.05 Construction Asbestos
- ☐
- 17.02.01 Wood
-
- ☐
- 20.02.01 Garden / Park Waste
- ☐
- Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been
separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

**THE BUYLE NEAR SEKIS
SHEPPERTON
TW17 8SN**

TRANSFER

DATE

TRANSFER

TIME

SITE

LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

ANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY
ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE
ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597923CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTEBULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPYRegistered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 26-4-17	VEHICLE REG. No: EY12 YSM	NAME OF PERSON IN CHARGE OF VEHICLE: MICK
-------------------------	-------------------------------------	---

CUSTOMER:

BERKELEY HOMESSITE ADDRESS: **GREEN PARK**
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading	Gross Weight of Vehicle	TONNES	M ³
-----------------	-------------------------	--------	----------------

Description of Material NON HAZ M/A	Tare Weight		
--	-------------	--	--

LORRY HIRE	Cash Sale	Net Weight	
------------	-----------	------------	--

HOURS WORKED

TRAVELLING TIME

No. OF LOADS
DESCRIPTION OF MATERIALWHERE TIPPED
☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed MetalCUBIC METERS
☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 WoodTIP CODE
☐ 20.02.01 Garden / Park Waste ☐ Other

ADDRESS OF TIP/TRANSFER POINT

THE BUGLE NURSERIE SHEPPERTON TW18 8SN	TRANSFER DATE	
	TRANSFER TIME	
	SITE LICENCE No.	

IF MULTIPLE TRANSFER BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 615407

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28 4 17 VEHICLE REG. No: KXISNPF NAME OF PERSON IN CHARGE OF VEHICLE: Andy
CUSTOMER: BERKLEY WINGS

SITE ADDRESS: GREEN DR

READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading Gross Weight of Vehicle TONNES M³

Description of Material NON HAZ Tare Weight

LORRY HIRE Cash Sale Net Weight 1 x 8W Luro

HOURS WORKED DESCRIPTION OF MATERIAL

TRAVELLING TIME

No. OF LOADS 1 x 8W Luro

WHERE TIPPED

CUBIC METERS TIP CODE

ADDRESS OF TIP/TRANSFER POINT TRANSFER OF WASTE

BUSLE NURSERY TRANSFER DATE 28 4 17

SUNBURY TRANSFER TIME

TW17 8SN SITE LICENCE No. 6

SIGNED BY TIP OPERATOR SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

[Signature]

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597934CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE**CUSTOMER COPY**BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

HAULAGE MANAGER - MICK ATKINS 07831 859111

DATE: 27-4-17	VEHICLE REG. No: EY12 YSM	NAME OF PERSON IN CHARGE OF VEHICLE: MICK
-------------------------	-------------------------------------	---

CUSTOMER:

BERKLEY HOMES

SITE ADDRESS:

**GREEN PARK
READING**I confirm that I have fulfilled my duty to apply the waste hierarchy as
required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

NON HAZ M/M

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1X8W

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and
arising materials being conveyed or disposed of in:

- (a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal
☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood
☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been
separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

**THE BUCKLE NURSERIES
SHEPPERTON
TW17 8SN**

TRANSFER DATE	
TRANSFER TIME	
SITE LICENCE No.	

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY
WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE
LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W611793

CONVEYANCE NOTE C (Weight and Vol.)

CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27-4-17 VEHICLE REG. No: Km65Kos NAME OF PERSON IN CHARGE OF VEHICLE: DAVE

CUSTOMER:

SITE ADDRESS:

Berkley Homes
Green Park Village
Reading

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Non Haz

Gross Weight
of Vehicle

TONNES

1x8^{M3} wheeler
Load

Description of Material

Much Away

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

[Signature]

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

Bugle Nursery
upper Hatfield Road
Shropshire TW17 8SN

TRANSFER DATE

27-4-17

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

[Signature]

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

[Signature]

J. WILKINSON

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 602622

CONVEYANCE NOTE C (Weight and Vol.)

CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 27/04/17 VEHICLE REG. No: BY12 YLP NAME OF PERSON IN CHARGE OF VEHICLE: LEE

CUSTOMER: BARK RECY THOMAS

SITE ADDRESS: GREEN PARK

I confirm that I have fulfilled my duty to apply the waste hierarchy as
required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material N/HAZ m/a

Tare Weight

LORRY HIRE

Cash Sale

Net Weight 1x8w

HOURS
WORKED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and
relate to the aggregates, sub-based materials and
arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made
by weight.

(b) An agreement for the carriage thereof made by
weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

TRAVELLING
TIMENo. OF
LOADSWHERE
TIPPED

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BULK WASTES
TW17 8SA

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of
waste certifies that recyclable
and non-hazardous materials
have been separated prior to
collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS
ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE
PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613169

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 2-8-17 VEHICLE REG. No: T111 PPP NAME OF PERSON IN CHARGE OF VEHICLE: JA

CUSTOMER: Benceley Haines

SITE ADDRESS: Green Park Reading

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading Gross Weight of Vehicle TONNES M³

Description of Material New Haz MIA Tare Weight 1x8w

LORRY HIRE Cash Sale Net Weight

HOURS WORKED DESCRIPTION OF MATERIAL

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS TIP CODE

ADDRESS OF TIP/TRANSFER POINT TRANSFER OF WASTE

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR SIGNED BY DRIVER

SIGNED BY PRODUCER/CUSTOMER PRINT NAME J. WILKINSON

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 614761

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 02.05.17 VEHICLE REG. No: KM 65KOU NAME OF PERSON IN CHARGE OF VEHICLE: MANSIS

CUSTOMER: BERKLEY HOMES

SITE ADDRESS: GREEN PARK

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading: NOW HAZ Gross Weight of Vehicle: TONNES: M³

Description of Material: MUCK AND Tare Weight:

LORRY HIRE

Cash Sale

Net Weight

1 x 8W

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BUGLE NURSERIES

TRANSFER DATE

2.5.17

TW 17 8WS SUNBURY

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597943

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 2-5-17 VEHICLE REG. No: EY12 YGM NAME OF PERSON IN CHARGE OF VEHICLE: Mick

CUSTOMER:

BERKELEY HOMES

SITE ADDRESS: GREEN PARK
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

NON HAZ M/A

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1 X 80

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true, and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal

☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood

☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BOYLE NURSERIES
SHEPPERTON
TW17 8SN.

TRANSFER
DATE

TRANSFER
TIME

SITE

LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597783

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 2/5/17 VEHICLE REG. No: GY12 YSP NAME OF PERSON IN CHARGE OF VEHICLE: JCS

CUSTOMER:

SITE ADDRESS: BARNLEY HILLS
GREEN PARK
BARNLEY

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

N/HW2 Mixed Waste

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1 X 8

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal

☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood

☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

Buyle Farm
Upper Haulfield Road
Shipbourne TW17 8SA

TRANSFER
DATE
TRANSFER
TIME
SITE
LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613168

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 2-5-17 VEHICLE REG. No: T111 PPP NAME OF PERSON IN CHARGE OF VEHICLE: J

CUSTOMER:

Bankerley Homes

SITE ADDRESS:

Lincoln Park

Reading

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

New Haz MHA

Tare Weight

1x8w

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):



CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

The Bugle Nurseries
Shepperton
TW17 8SW

TRANSFER DATE

TRANSFER TIME

SITE LICENCE

SIGNED BY TIP OPERATOR



SIGNED BY DRIVER



The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME



J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597781CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTEBULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPYRegistered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 2/5/17	VEHICLE REG. No: E/12 YSP	NAME OF PERSON IN CHARGE OF VEHICLE: JOE
--------------	---------------------------	--

CUSTOMER: BARKER/ HOLLIS

SITE ADDRESS: Green Park

RATONS

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading	Gross Weight of Vehicle	TONNES	M ³
-----------------	-------------------------	--------	----------------

Description of Material M/HAL mixed clay	Tare Weight		
--	-------------	--	--

LORRY HIRE	Cash Sale	Net Weight	1482
------------	-----------	------------	------

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

DATE

TRANSFER TIME

SITE LICENCE No.

IF MULTIPLE TRANSFER BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597941CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTEBULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPYRegistered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 2-5-15	VEHICLE REG. No: EY12 YSM	NAME OF PERSON IN CHARGE OF VEHICLE: OTICE
------------------------	-------------------------------------	--

CUSTOMER:

BERKELEY HOMES

SITE ADDRESS:

**GREEN PARK
READING**I confirm that I have fulfilled my duty to apply the waste hierarchy as
required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

WON HAZ M/AGross Weight
of Vehicle

TONNES

M³

Description of Material

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1X8W

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and
arising materials being conveyed or disposed of in:

- (a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal
☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood
☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been
separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

**THE BUGLE NURSERIES
SHEPPERTON
TW17 8SN**

TRANSFER

DATE

TRANSFER

TIME

SITE

LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY
WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE
LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613167

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 2-5-17 VEHICLE REG. No: T111 PPP NAME OF PERSON IN CHARGE OF VEHICLE: J

CUSTOMER:

Banker's Homes

SITE ADDRESS:

Green Pk
Reading

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

Tare Weight

1x8w

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:
~~(a)~~ A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

The Bunch Nurseries
Shepperton
TW17 8SW

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597940

CONVEYANCE NOTE C (Weight and Vol.)

CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 2-5-17	VEHICLE REG. No: E412 YSM	NAME OF PERSON IN CHARGE OF VEHICLE: MICK
------------------------	-------------------------------------	---

CUSTOMER:

BERKELEY HOMES

SITE ADDRESS:

**GREEN PARK
READING**

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

NORMAL M/A

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1X8W

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

- (a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal
☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood
☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

**THE BUGLE NURSERY
SHARPERLOW
TW17 8SN**

TRANSFER
DATE
TRANSFER
TIME
SITE
LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597780

CONVEYANCE NOTE C (Weight and Vol.)

CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 2/5/17 VEHICLE REG. No: BY12 YSP NAME OF PERSON IN CHARGE OF VEHICLE: JOE

CUSTOMER:

BARKER / HENNES

SITE ADDRESS:

GREEN PARK
ROMNEY

I confirm that I have fulfilled my duty to apply the waste hierarchy as
required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

N/HW Muck

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1x8W

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

178W

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and
arising materials being conveyed or disposed of in:

- (a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal
☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood
☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been
separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

Bugh Nersum
Upper Haverhill Rd
Slipway Twp 8321

TRANSFER
DATE
TRANSFER
TIME
SITE
LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY
WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE
LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597942

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 2-5-17 VEHICLE REG. No: EY12 YQM NAME OF PERSON IN CHARGE OF VEHICLE: Mick

CUSTOMER:

BERKELEY HOME
GREEN PARK
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Now 11:02 04/17

Gross Weight
of Vehicle

TONNES

M³

Description of Material

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1 X SW

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

- (a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal
☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood
☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BUGLE WURSEIRES
SHEPPERTON
TW17 8SN

TRANSFER

DATE

TRANSFER

TIME

SITE

LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597782

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 2/5/17 VEHICLE REG. No: EY12-1SP NAME OF PERSON IN CHARGE OF VEHICLE: JOK

CUSTOMER:

BARKLEY HOMES

SITE ADDRESS:

Green Park

Reading

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

R1/HAZ MUCH AWA

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1 x 8

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

- (a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal
☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood
☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

Bugle Nodum
Upper Haulford Road

Slough Road TW17 8SA

TRANSFER

DATE

TRANSFER

TIME

SITE

LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597949

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28/4/17 VEHICLE REG. No: EY12 YSP NAME OF PERSON IN CHARGE OF VEHICLE: JES

CUSTOMER: BARNLEY HOLLOW

SITE ADDRESS: GARDEN BRICK
BRICKERY

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading Gross Weight of Vehicle TONNES M³

Description of Material 1/2 HAD MUCH DEBRIS Tare Weight

LORRY HIRE Cash Sale Net Weight

HOURS WORKED
TRAVELLING TIME
No. OF LOADS
WHERE TIPPED
CUBIC METERS 1 x 950

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:
(a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal
☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood
☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

30gth Nonsburg
Upper Hylfardd Road
SILFORD
TRANSFER DATE
TRANSFER TIME
SITE
LICENCE No.

IF MULTIPLE TRANSFER BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597938

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28-4-17	VEHICLE REG. No: EY12 YSM	NAME OF PERSON IN CHARGE OF VEHICLE: MICK
-------------------------	-------------------------------------	---

CUSTOMER:

BERKELEY HOMES

SITE ADDRESS: **GREEN PARK**
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading	Gross Weight of Vehicle	TONNES	M ³
-----------------	-------------------------	--------	----------------

Description of Material NON HAZ M/A	Tare Weight		
--	-------------	--	--

LORRY HIRE	Cash Sale	Net Weight	1 X 80
------------	-----------	------------	---------------

HOURS WORKED
TRAVELLING TIME
No. OF LOADS
WHERE TIPPED

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:
(a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal
☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood
☐ 20.02.01 Garden / Park Waste ☐ Other


CUBIC METERS	The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.
--------------	---

TIP CODE	SIGNED BY PRODUCER/CUSTOMER PRINT NAME
----------	---

ADDRESS OF TIP/TRANSFER POINT	TRANSFER OF WASTE
-------------------------------	-------------------

THE BUCKENHURST SHEPPER TON TW17 8SW	TRANSFER DATE TRANSFER TIME SITE LICENCE No.
---	---

IF MULTIPLE TRANSFER BETWEEN DATES	
------------------------------------	--

SIGNED BY TIP OPERATOR 	SIGNED BY DRIVER 
--	---

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597937CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTEBULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPYRegistered Waste Carrier
Registration No. CBDU81963
Issued by Environment AgencyDATE: **28-7-17** VEHICLE REG. No: **EY12 YSM** NAME OF PERSON IN CHARGE OF VEHICLE: **Mick**

CUSTOMER:

BERKELEY HOMESSITE ADDRESS: **GREEN PARK**
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

NON HAZ M/A

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1X800

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

☐ 17.01.07 Clean Hardcore☒ 17.05.04 Soil & Stones☐ 17.04.07 Mixed Metal☐ 17.09.04 Mixed Construction☐ 17.06.05 Construction Asbestos☐ 17.02.01 Wood☐ 20.02.01 Garden / Park Waste☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

TRANSFER

DATE

TRANSFER

TIME

SITE

LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 614758

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28.4.17 VEHICLE REG. No: KM 65 KOU NAME OF PERSON IN CHARGE OF VEHICLE: MARTIN

CUSTOMER:

BERKLEY HOMES

SITE ADDRESS:

GREEN PARK.

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

NON HAZ

Gross Weight
of Vehicle

TONNES

M³

Description of Material

MICK ATKINS

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1 x 8m

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BUGLE NURSERIES
SUNBURY
TW 17 8NS

TRANSFER DATE

28.4.17

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

[Signature]

SIGNED BY DRIVER

[Signature]

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

[Signature]

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613699

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28/4/17 VEHICLE REG. No: KN16 GXT NAME OF PERSON IN CHARGE OF VEHICLE: LEE

CUSTOMER: BERKELEY Hm's

SITE ADDRESS: GREEN PARK
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight of Vehicle

TONNES

M³

Description of Material

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

BUGLE NURSERIES
HALIFORD RD
SOMERSET

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597948

CONVEYANCE NOTE C (Weight and Vol.)

CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28/06/07 VEHICLE REG. No: EY12 YSP NAME OF PERSON IN CHARGE OF VEHICLE: JCE

CUSTOMER:

SITE ADDRESS: Barkers / Howley Green Park Building

I confirm that I have fulfilled my duty to apply the waste hierarchy as
required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material 4/HAZ WASTE

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS 1x8w

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and
arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

☐ 17.01.07 Clean Hardcore

☒ 17.05.04 Soil & Stones

☐ 17.04.07 Mixed Metal

☐ 17.09.04 Mixed Construction

☐ 17.06.05 Construction Asbestos

☐ 17.02.01 Wood

☐ 20.02.01 Garden / Park Waste

☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been
separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

Begle Nussan
Upperbusham Road
Buckingham TW17 8SN

TRANSFER

DATE

TRANSFER

TIME

SITE

LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY
WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE
LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

W 597936

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28-4-17 VEHICLE REG. No: EY12 YGT NAME OF PERSON IN CHARGE OF VEHICLE: Mick

CUSTOMER:

BERKELEY HOMES

SITE ADDRESS:

GREEN PARK

READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

Now HAZ - MA

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1X800

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

- (a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal
☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood
☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BUSLE NURSERIES
SHEPPERTON
TW17 8SN

TRANSFER

DATE

TRANSFER

TIME

SITE

LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 602624

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28/4/17 VEHICLE REG. No: EYR YSP NAME OF PERSON IN CHARGE OF VEHICLE: JCS

CUSTOMER:

BARKLEY HOMES

SITE ADDRESS: GREEN PARK

Reading

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material H/HAZ MIXED WASTE

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

18.5

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

Bulk material
uppon 2nd floor Revs
Sulphur TW17 8SN

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

J. WILKINSON

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613697

CONVEYANCE NOTE C (Weight and Vol.)

CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28/4/17 VEHICLE REG. No: KN16 CXT NAME OF PERSON IN CHARGE OF VEHICLE: LEE

CUSTOMER: Berkeley Hm's

SITE ADDRESS: Green Park
Reading

I confirm that I have fulfilled my duty to apply the waste hierarchy as
required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKEDTRAVELLING
TIMENo. OF
LOADSWHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and
relate to the aggregates, sub-based materials and
arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made
by weight.

(b) An agreement for the carriage thereof made by
weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

Boyle Nurseries
Halford Rd
SUNBURY

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of
waste certifies that recyclable
and non-hazardous materials
have been separated prior to
collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS
ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE
PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597935

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28-4-17	VEHICLE REG. No: EA124SM	NAME OF PERSON IN CHARGE OF VEHICLE: MICK
-------------------------	------------------------------------	---

CUSTOMER:

BERKELEY HOMES

SITE ADDRESS: **GREEN PARK**
READING

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading NOV H02 M/A	Gross Weight of Vehicle	TONNES	M ³
---------------------------------------	-------------------------	--------	----------------

Description of Material	Tare Weight		
-------------------------	-------------	--	--

LORRY HIRE	Cash Sale	Net Weight	1x8W
------------	-----------	------------	-------------

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

- (a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal
☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood
☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BULLY NEAR SERIES
SHEPPERTON
7W17 85N

TRANSFER

DATE

TRANSFER

TIME

SITE

LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W602623

CONVEYANCE NOTE C (Weight and Vol.)

CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28/4/17 VEHICLE REG. No: 12/12 YSP NAME OF PERSON IN CHARGE OF VEHICLE: JOW

CUSTOMER:

Buckley/Henrys

SITE ADDRESS:

GILSON PARK
Rushley

I confirm that I have fulfilled my duty to apply the waste hierarchy as
required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

21/HAZ mixed waste

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

HOURS
WORKEDTRAVELLING
TIMENo. OF
LOADSWHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and
relate to the aggregates, sub-based materials and
arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made
by weight.

(b) An agreement for the carriage thereof made by
weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

14.50

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

Boggy Nether
Upper Hallen Road
Shipston Turf 83N

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of
waste certifies that recyclable
and non-hazardous materials
have been separated prior to
collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS
ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE
PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 614756

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28-4-17 VEHICLE REG. No: KM 65 KOU NAME OF PERSON IN CHARGE OF VEHICLE: MAN-TIT

CUSTOMER: BERKLEY HOMES

SITE ADDRESS: GREEN PARK ROAD, WIMBORNE

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading WON HAZ Gross Weight of Vehicle TONNES M³

Description of Material MICK ATKINS Tare Weight

LORRY HIRE Cash Sale Net Weight 1 x SW

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

TIP CODE

DESCRIPTION OF MATERIAL

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 614972

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28/4/17 VEHICLE REG. No: KP14 FNC NAME OF PERSON IN CHARGE OF VEHICLE: Chris
CUSTOMER: BEEKLEY HOMES

SITE ADDRESS: Green Park
Reading

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

NON-HAZ
MUCK ANY

Tare Weight

1 x 8

LORRY HIRE

Cash Sale

Net Weight

WHEELS

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

THE BRICK
SUNBURY TW17 8SN

TRANSFER DATE

28/4/17

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597939

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: **28-4-17** VEHICLE REG. No: **EY12 YQM** NAME OF PERSON IN CHARGE OF VEHICLE: **Mick**

CUSTOMER:

BERKELEY HOMES

SITE ADDRESS:

**GREEN PARK
READING**

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

NON HAZ M/A

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1X8W

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

- (a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal
☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood
☐ 20.02.01 Garden / Park Waste ☐ Other

CUBIC METERS

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

TIP CODE

SIGNED BY PRODUCER/CUSTOMER
PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

**THE BUCCLE NURSERIES
SHEPPERTON
TW17 8SN**

TRANSFER
DATE
TRANSFER
TIME
SITE
LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 614760

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28.4.17 VEHICLE REG. No: KM 65 KOU NAME OF PERSON IN CHARGE OF VEHICLE: MANDIT

CUSTOMER:

Berkley Homes

SITE ADDRESS:

Green Park

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

NON HAZ

Gross Weight
of Vehicle

TONNES

M³

Description of Material

Muck Aug

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1 x 8m

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:
(a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.
Delete (a) or (b) as applicable.
On behalf of the Seller
SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

Boyle Nurseries
Sunbury
TW17 8NS

TRANSFER DATE

28-4-17

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR



SIGNED BY DRIVER



The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME



J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 597947

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 28/11/17 VEHICLE REG. No: 12/12-150 NAME OF PERSON IN CHARGE OF VEHICLE: SCS

CUSTOMER: BORNELEY HOMES

SITE ADDRESS: Green Park
Reading

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

Gross Weight
of Vehicle

TONNES

M³

Description of Material

1/1/12 mixture

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

HOURS WORKED

TRAVELLING TIME

No. OF LOADS

WHERE TIPPED

CUBIC METERS

1x80

TIP CODE

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.
(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

DESCRIPTION OF MATERIAL

☐ 17.01.07 Clean Hardcore ☒ 17.05.04 Soil & Stones ☐ 17.04.07 Mixed Metal

☐ 17.09.04 Mixed Construction ☐ 17.06.05 Construction Asbestos ☐ 17.02.01 Wood

☐ 20.02.01 Garden / Park Waste ☐ Other

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER

PRINT NAME

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

Begle Newburn
Upper Oldfield Road
Chippingwood Town

TRANSFER
DATE
TRANSFER
TIME
SITE
LICENCE No.

IF MULTIPLE TRANSFER
BETWEEN DATES

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

WOOLDRIDGE

ECOTEC

W 613029

CONVEYANCE NOTE C (Weight and Vol.)
CONTROLLED WASTE TRANSFER NOTE

BULK EXCAVATION, TOP SOIL, PLANT HIRE,
GROUNDWORK CONTRACTORS
HALL GROVE FARM, BAGSHOT, SURREY GU19 5HP
Tel: (01276) 470333 Fax: (01276) 470301

HAULAGE MANAGER - MICK ATKINS 07831 859111

CUSTOMER COPY

Registered Waste Carrier
Registration No. CBDU81963
Issued by Environment Agency

DATE: 2-5-2017 VEHICLE REG. No: KV04 XKW NAME OF PERSON IN CHARGE OF VEHICLE: TGM7

CUSTOMER:

BENKLEY HOMES
GREEN PARK
READING

SITE ADDRESS:

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by regulation 12 of the waste regulations (England and Wales) 2011

SIC CODE

Time of Loading

NON HAZ

Gross Weight
of Vehicle

TONNES

M³

Description of Material

MOCK ALLOY

Tare Weight

LORRY HIRE

Cash Sale

Net Weight

1x8

HOURS
WORKED

TRAVELLING
TIME

No. OF
LOADS

WHERE
TIPPED

DESCRIPTION OF MATERIAL

- ☐ 17.01.07 Clean Hardcore
☐ 17.09.04 Mixed Construction
☐ 20.02.01 Garden / Park Waste
☒ 17.05.04 Soil & Stones
☐ 17.04.07 Mixed Metal
☐ 17.06.05 Construction Asbestos
☐ 17.02.01 Wood
☐ Other

Certified that the above particulars are true and relate to the aggregates, sub-based materials and arising materials being conveyed or disposed of in:

(a) A sale or an agreement for the sale thereof made by weight.

(b) An agreement for the carriage thereof made by weight or volume.

Delete (a) or (b) as applicable.

On behalf of the Seller

SIGNED BY (DRIVER'S SIGNATURE):

CUBIC METERS

TIP CODE

ADDRESS OF TIP/TRANSFER POINT

TRANSFER OF WASTE

TRANSFER DATE

TRANSFER TIME

SITE LICENCE No.

SIGNED BY TIP OPERATOR

SIGNED BY DRIVER

The producer of this load of waste certifies that recyclable and non-hazardous materials have been separated prior to collection.

SIGNED BY PRODUCER/CUSTOMER PRINT NAME

J. WILKINSON

THE COMPANY UNDERTAKES DELIVERY TO THE NEAREST HARD ROAD AND WILL ONLY ENTER PRIVATE PROPERTY WHERE ACCESS IS ADEQUATE AND ON CONSIGNEE'S INVITATION. THE COMPANY AND ITS AGENTS WILL NOT BE LIABLE FOR ANY DAMAGE TO PRIVATE PROPERTY WHATSOEVER CAUSED BY THE VEHICLE AND/OR LOAD.

COMLEY SKIPS

Calf Lane Quarry Waste Transfer Station
Rye Common
Odiham RG29 1HU
Tel: 01252 851 863 www.comleyskips.co.uk
Tel: 01256 702178



DUTY OF CARE WASTE TRANSFER NOTE / INVOICE

SITE PERMIT No. HR078

DATE 05/10/2016
TIME
TICKET No. 16527

CUSTOMER **Wooldridge EcoTec Ltd** ACCOUNT
Unit 17
Hall Grove Farm
Bagshot
GU19 5HP

DESCRIPTION OF MATERIAL Bonded asbestos 17 06 05 INWARD

Weighing Information:

Gross 1,800 kg 05/10/16 10:38:09
Tare 1,740 kg 05/10/16 10:46:42
Net 60 kg

Additions HWCN Qty 1

ORDER HAULIER
Wooldridge EcoTec Ltd

VEHICLE REG'N. No.
MA08 MRX

CONVEYANCE NOTE No.

SPECIAL WASTE NOTE No.

DRIVERS SIGNATURE

CASH SALES INVOICE

	£	P
RATE		
VAT @ %		
TOTAL		

Conditions of Acceptance: THE COMPANY ACCEPT NO RESPONSIBILITY WHATSOEVER FOR DAMAGE OR INJURY OF ANY NATURE AND HOWEVER CAUSED TO THE VEHICLE OR PERSONS USING THE SITE. ONLY MATERIAL PERMITTED UNDER THE WASTE MANAGEMENT LICENCE MAY BE DEPOSITED ON THE SITE. THE COMPANY RESERVE THE RIGHT TO REJECT ANY MATERIAL WHICH IS CONSIDERED TO BE OBJECTIONAL OR UNSUITABLE FOR DEPOSIT ON THE COMPANY'S SITE.

WASTE PRODUCERS SIGNATURE

C G Comley & Sons Ltd Company Reg. No. 1672195
Vat Reg. No. 199 9304 04

WOOLDRIDGE

PRODUCER'S/HOLDER'S/CONSIGNOR'S COPY (Delete as appropriate)

1 Consignment note code:

N	O	O	L	D	E	/	0	0	0	1	8
---	---	---	---	---	---	---	---	---	---	---	---

2 The waste described below is to be removed from (name, address, postcode, telephone, e-mail, facsimile): *c/o Berkeley Group, Phase 5, Green Park Village, Long Water Rd, Reading, Berkshire, RG2 6PG*

3 Premises code (where applicable):

--	--	--	--	--	--

Comleya Sons, Calf Lane, Rye
Common, Oduham, RG29 4PH

Woodbridge Ecotec Ltd, Unit 17,
Hail Grove Farm, Bagshot, Surrey
GU19 5HP TEL. 01276 470333

If continuation sheet used, tick here ☐

2 SIC for the process giving rise to the waste: 45.11/

3 WASTE DETAILS (where more than one waste type is collected all of the information given below must be completed for each EWC identified)

The information given below is to be completed for each EWC identified

EWC code						Packing group(s)	UN identification number(s)	Proper shipping name(s)	UN class(es)	Special handling requirements
1	7	0	6	0	5	III	2590	White waste Asbestos	9	Do not inhale

PART D Consignor's certificate

I certify that the information in A, B and C has been completed and is correct, that the carrier is registered or exempt and was advised of the appropriate precautionary measures. All of the waste is packaged and labelled correctly and the carrier has been advised of any special handling requirements.

I certify that I today collected the consignment and that the details in A2, A4 and B3 are correct and I have been advised of any specific handling requirements.

Where this note comprises part of a multiple collection the round number and collection number are:

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by Regulation 12 of the Waste (England and Wales) Regulations 2011.

1 Carrier name:

On behalf of (name, address, postcode, telephone, e-mail, facsimile):

Woodbridge Ecotec Ltd, As AS above.

2 Carrier registration no./reason for exemption:

3. Vehicle registration no. (or mode of transport, if not road):

Signature MA08 mrx

Date	D	D	M	M	Y	Y	Y	Y	Time	H	H	FF	SS
------	---	---	---	---	---	---	---	---	------	---	---	----	----

1 Consignor name:

On behalf of (name, address, postcode, telephone, e-mail, facsimile):

As AS Above

Signature

Date	D	D	M	M	Y	Y	Y	Y	Time	H	H	M	M
------	---	---	---	---	---	---	---	---	------	---	---	---	---

PART E Consignee's certificate (where more than one waste type is collected all of the information given below must be completed for each EWC)

Individual EWC code(s) received	Quantity of each EWC code received (kg)	EWC code accepted/rejected	Waste management operation (R or D code)
170605	60kg	ACC	D15

1 I received this waste at the address given in A4 on:

Date 05/10/2016 Time 1040

2 Vehicle registration no. (or mode of transport if not road):

3 Where waste is rejected please provide details:

Name: J. Turva

On behalf of (name, address, postcode, telephone, e-mail, facsimile):

I certify that waste management licence/permit/authorised exemption no(s).

authorises the management of the waste described in B at the address given in A4.

Where the consignment forms part of a multiple collection, as identified in Part C, I certify that the total number of consignments forming the collection are:

Signature M. Turner

Date	05	10	20	16	Time	10	40
------	----	----	----	----	------	----	----

The Hazardous Waste Regulations 2005: Consignment Note



Environment
Agency

CONSIGNEE'S COPY

Delete as appropriate

PART A Notification details

Consignment note code: **LUTONE14528** **SMALLMEAD ROAD**

2 The waste described below is to be removed from (name, address, postcode, telephone, e-mail, facsimile):
READING RG30 3UR

3 Premises code (where applicable): **LUTONE**

4 The waste will be taken to (name, address and postcode):

ASBESTOS WASTE SOLUTION, 27 OLIVER CLOSE, WESTTHURCK RM20 3EE

5 The waste producer was of different from 2) (name, address, postcode, telephone, e-mail, facsimile): **Luton Environmental Ltd. 19 Bolingbroke Road, Luton. LU1 5JD**

PART B Description of the waste

1 The process giving rise to the waste(s) was: **COLLECTION**

2 SIC for the process giving rise to the waste: **39.001**

3 WASTE DETAILS (where more than one waste type is collected all of the Information given below must be completed for each EWC identified)

Description of the waste	List of wastes (EWC code)(6 digits)	Quantity (kg)	The chemical/biological components in the waste and their concentrations are:		Physical form (gas, liquid, solid, powder, sludge or mixed)	Hazard code(s)	Container type, number and size
			Component	Concentration (% or mg/kg)			
Asbestosoma	170605	80	Calson	15	Solid	H3/7	8 BAGS

The information given below is to be completed for each EWC identified

EWC code	UN identification number(s)	Proper shipping name (s)	UN class(es)	Packing group(s)	Special handling requirements
170605	2590	Asbestos waste	9	III	MANAGE

PART C Carrier's certificate

(If more than one carrier is used, please attach schedule for subsequent carriers.)

If schedule of carriers is attached tick here. ☐

I certify that I today collected the consignment and that the details in A2, A4 and B3 are correct and I have been advised of any specific handling requirements.

Where this note comprises part of a multiple collection the round number and collection number are:

LUTONE / L14MNA / L0528712

1 Carrier name: **A MCKINSTRON**
On behalf of (name, address, postcode, telephone, e-mail, facsimile):

**Luton Environmental Ltd
19 Bolingbroke Road, Luton. LU1 5JD**

2 Carrier registration no./reason for exemption:

EBD 43110

3 Vehicle registration no. (or mode of transport, if not road):

L14MNA

Signature

Date **10052017** Time **1100**

PART D Consignor's certificate

I certify that the information in A, B and C has been completed and is correct, that the carrier is registered or exempt and was advised of the appropriate precautionary measures. All of the waste is packaged and labelled correctly and the carrier has been advised of any special handling requirements.

I confirm that I have fulfilled my duty to apply the waste hierarchy as required by Regulation 12 Of the Waste (England and Wales) Regulations 2011.

1 Consignor name: **A MCKINSTRON**
On behalf of (name, address, postcode, telephone, e-mail, facsimile):

**Luton Environmental Ltd
19 Bolingbroke Road, Luton. LU1 5JD**

Signature

Date **10052017** Time **1100**

PART E Consignee's certificate

Individual EWC code(s) received	Quantity of each EWC code received (kg)	EWC code Accepted/rejected	Waste management operation (R or D code)
170605	80KG	A	D15

1 I received this waste at the address given in A4 on:

Date **12052017** Time **1239**

2 Vehicle registration no. (or mode of transport if not road):

L14MNA

3 Where waste is rejected please provide details:

Name: **K POKUS**
On behalf of (name, address, postcode, telephone, e-mail, facsimile):

I certify that waste permit/exempt waste operation number:

GR/AP 3694VC

authorise the management of the waste described in B at the address given in A4.

Where the consignment forms part of a multiple collection, as identified in Part C, I certify that the total number of consignments forming the collection are:

3

**AWS, 27a Oliver Close West
Thurrock, Essex, RM20 3EE**

Signature

Date **12052017** Time **1239**
