



Before any construction activity or material delivery takes place within areas identified on the Tree Protection Plan, temporary ground protection and fencing must be installed to prevent soil compaction. Ground protection and fencing must remain in place for the duration of the works and shall only be removed once all construction activities have been completed. Due to the narrow side access, only small digger can be used for construction, therefore ground protection as per 6.2.3.3 (b), below, is planned.

6.2.3.3 New temporary ground protection should be capable of supporting any traffic entering or using the site without being distorted or causing compaction of underlying soil.

NOTE The ground protection might comprise one of the following:

- for pedestrian movements only, a single thickness of scaffold boards placed either on top of a driven scaffold frame, so as to form a suspended walkway, or on top of a compression-resistant layer (e.g. 100 mm depth of woodchip), laid onto a geotextile membrane;
- for pedestrian-operated plant up to a gross weight of 2 t, proprietary, inter-linked ground protection boards placed on top of a compression-resistant layer (e.g. 150 mm depth of woodchip), laid onto a geotextile membrane;
- for wheeled or tracked construction traffic exceeding 2 t gross weight, an alternative system (e.g. proprietary systems or pre-cast reinforced concrete slabs) to an engineering specification designed in conjunction with arboricultural advice, to accommodate the likely loading to which it will be subjected.

Figure 2 Default specification for protective barrier

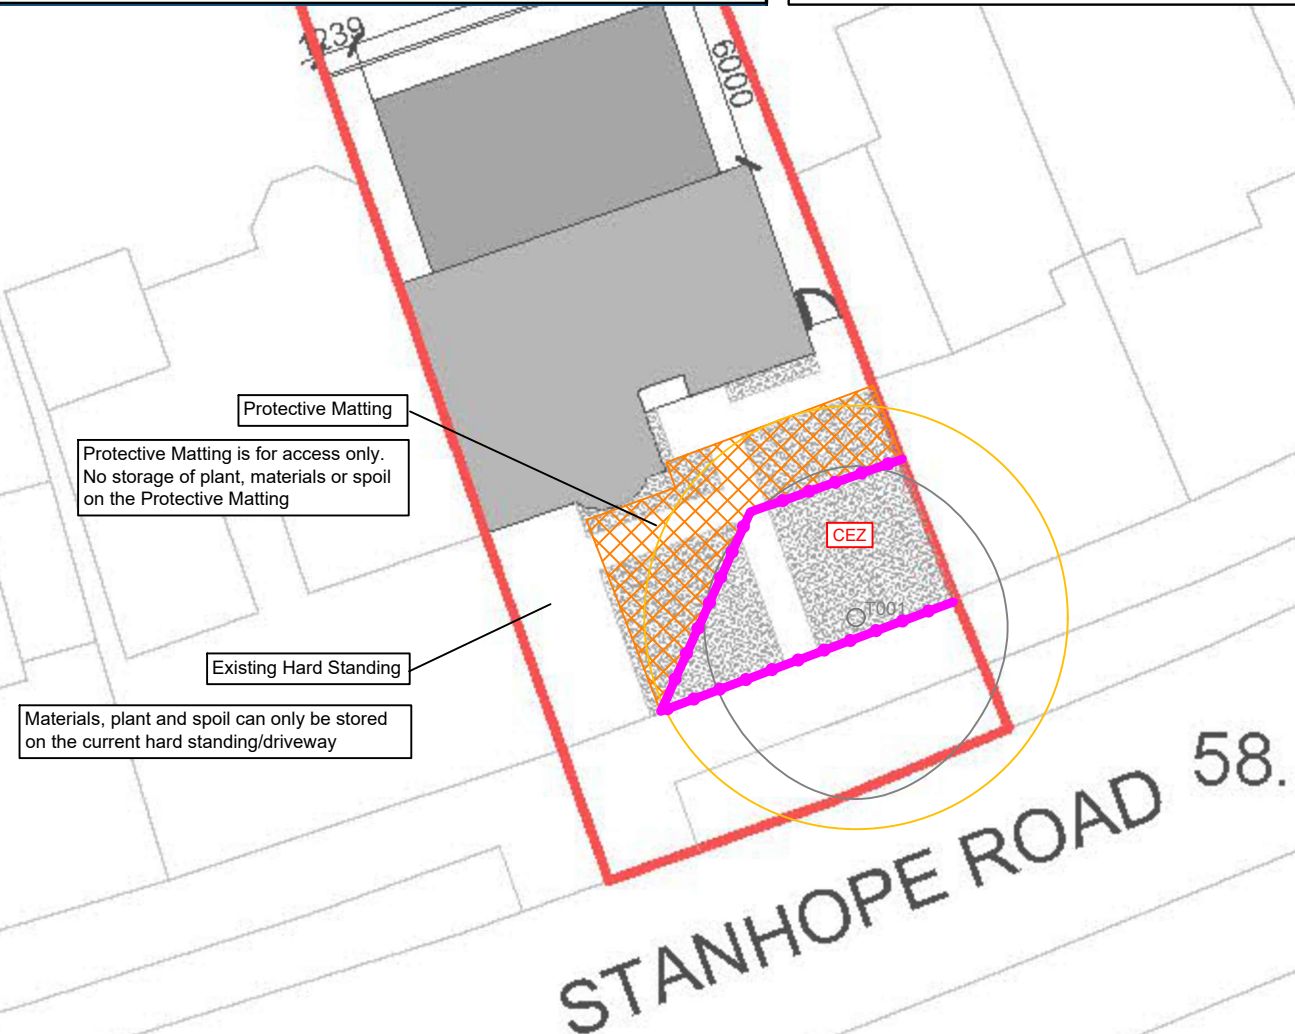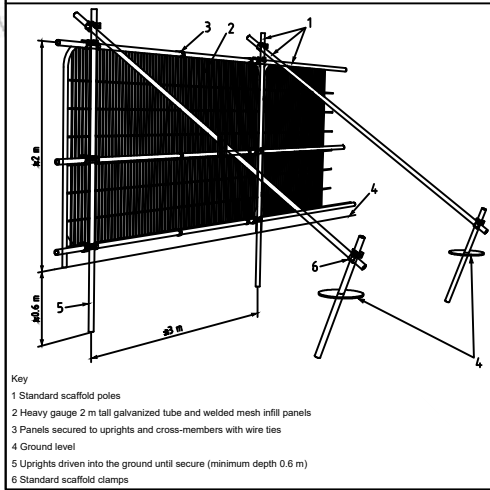



David Randall Tree Consultancy
07941794154
www.davidrandalltreeconsultancy.com

Site: 38 Stanhope Road	1:250 @ A4
Drawing Title: Tree Protection Plan	August 2026

Key:

- Category A
- Category B
- Category C
- Category U

Tree Protection Fencing

CEZ – Construction Exclusion Zone

Root Protection Area

Crown Spread

Tree Number

Temporary Protective Matting

NOTE: Tree/group numbers marked have approximate locations.
